1. Semiannual Social Monitoring Report

PUBLIC

Reporting Period: January - June 2024

Submission to ADB: October 2024

Pakistan: Balakot Hydropower Development Project

Prepared by the Project Implementation Unit, Pakhtunkhwa Energy Development Organization, Government of Khyber Pakhtunkhwa, for the Islamic Republic of Pakistan and the Asian Development Bank (ADB).

This internal semi-annual social monitoring report of land acquisition and resettlement plan is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area.


ROJECT IMPLEMENTATION UNIT (PIU) PAKHTUNKHWA ENERGY DEVELOPMENT ORGANIZATION (PEDO) GOVERNMENT OF KHYBER PAKHTUNKHWA



BALAKOT HYDROPOWER DEVELOPMEMNT PROJECT LOAN No: ADB 4057-PAK & AIIB 8397-PAK



Semiannual Social Monitoring Report (Internal) of Sectional Land Acquisition and Resettlement Plans (Sections 1 & 2), January – June 2024

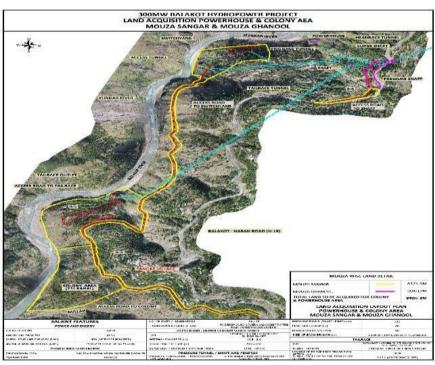

Submission of revised SMR to ADB: October 2024

TABLE OF CONTENTS

EXE	CUTIVE SUMMARY	1
1	INTRODUCTION	1-1
1.1 1.2 1.3 1.3.1 1.3.2	Section-2: Mouza Bela Sacha and Paras (under 2 nd Sectional LARP)	1-1 1-2 1-4 1-4
2	INTERNAL MONITORING REPORT OF LARP IMPLEMENTATION	
2.1 2.2 2.3 3	Internal Monitoring Requirements of LARPs Objectives of the Internal Monitoring Report Monitoring Indicators INSTITUTIONAL ARRANGEMENT AT PIU FOR BHPP	2-8 2-9
3.1 3.2 3.3 3.4 3.5 4	LARP's Implementation and Monitoring Set-up Project Steering Committee Disbursement of Allowances by LAC/ PIU Independent Valuation Study (IVS) LARP's Addendum LARP IMPLEMENTATION PROGRESS REVIEW	3-10 3-10 3-10
4.1 4.2 4.3 4.3.1 4.3.2 4.3.3 4.3.4	Disbursement of Built-up Property Compensation Pending Payment of Land Compensation Payment of Allowances by LAC/ PIU Section and Mouza (village) wise Hydropower Component and Cleared Acqual Land of BHPP	4-13 4-14 4-18 4-19 4-22 uired 4-26
5	LARP IMPLEMENTATION MONITORING SET-UP	5-28
5.1 5.2 5.3 5.4 5.5 6	LARP Implementation Monitoring Exhaustive Efforts Community Consultations/Meetings Coordination Meetings with District Revenue Officials Dissemination of LARP related Information. PROJECT IMPACT ON WOMEN MOBILITY AND PRIVACY	5-28 5-29 5-30 5-31
7	LIVELIHOOD SUPPORT INTERVENTION MEASURE	7-33
7.1 7.2 8	Employment Opportunities	7-33
9	LARP Implementation and Social Safeguards Compliance Plan	9-38

LIST OF TABLES

Table 1.1: Section, Mouza and Component wise Summary of Acquired Land with No. of I of BHPP	
Table 1.2: Section and Mouza wise Summary of Affected Trees with No. of DPs of BHPP Table 1.3: Section and Mouza wise Summary of Built-up Property with No. of DPs of BHF	
	.1-3
Table 3.1: Tentative Schedule for Implementation LARPs Addendum	3-11
Table 4.1: Summary of Section wise LAR Impacts and Entitlement Categories of BHP Project	
Table 4.0. Mayor (illaga) and Candan vias Commany of Daid Land Commany sting Area	+ -10
Table 4.2: Mouza (village) and Gender wise Summary of Paid Land Compensation Amou and Paid DPs	
Table 4.3: Mouza (village) wise Summary of Paid DPs and Paid Compensation Amount of	
Trees	
Table 4.4: Mouza (village) wise Summary of Paid DPs and Paid Compensation amount of	
Built-up Property	
Table 4.5: Mouza (village) wise Summary of Impediments causing delay in Payment of La Compensation	
Table 4.6: Section and Mouza wise No. of DPs and Allowances and Progress of	
Disbursement of each Allowances	4-24
Table 4.7: Section and Mouza-wise Clearance of LARP Implementation under BHPP4	
Table 5.1: Summary of Community Consultation Meetings with DPs (January-June 2024) 29)5-
Table 5.2: Issues/ Concerns of DPs and Response from the project team	5-29
Table 5.3: Summary of Coordination Meetings with District Administration	
Table 7.1: Summary of Skilled and Un-Skilled Laborers	
Table 8.1: Summary of Complaints Registered of BHPP	
Table 9.1: Updated Action Plan for LARP Implementation of BHPP	9-38
LIST OF FIGURES	
Figure 1.1: Location Map of Section-1 of BHP Project	.1-6
Figure 1.2: Location Map of Section-2 of BHP Project	.1-7
LIST OF ANNEXURES	
Annexure-1: Guidance Note on handling compensation cases with legal and administrative	ve
impediments of ADB	
Annexure-2: Scanned copies (sample) of recorded documents for DPs with impediments 50	
	اہ ما
Annexure-3: Compensation and Allowance Voucher/ Payment Receipt of Mouza Paras a	
Bela Sacha	9-55
Annexure-4: Community Consultation Meetings Report and Attendance Sheet of DPs	
Annexure-5: Meeting Minutes and Presentation of IVS Consultants and GRC/ Community	y
Members	9-59
Annexure-6: Meeting Minutes with Deputy Commissioner, District Mansehra9	9-63
Annexure-7: Advertisement in Newspaper, Public Notices and Social Media Link (Local L	
Language)	
Annexure-8: Information Brochure in Local Urdu Language for DPs	0-65
Annexure-9: Notifications of Allowances Disbursement Committee at LAC/ PIU	
Annexure-10: Notifications of Grievances Redressal Committees	ყ-ხგ
Annexure-11: Statement of Satisfaction Certificates (IVS and LARP Allowances) of the	
Complainants	
Annexure-12: Skilled and Un-Skilled Employment by Contractors/ PIU	9-72

ABBREVIATIONS

ADB Asian Development Bank AC Assistant Commissioner

ADC Assistant Deputy Commissioner
CNIC Computerized National Identity Card

DC Deputy Commissioner
DP Displaced Person

EMA External Monitoring Agent
EMR External Monitoring Report
ERM external resettlement monitor

GAP Gender Action Plan

GRC Grievance Redress Committee
GRM Grievance Redress Mechanism
IVS Independent Valuation Study

KP Khyber Pakhtunkhwa

PEDO Pakhtunkhwa Energy Development Organization

LAA Land Acquisition Act 1894 LAC Land Acquisition Collector

LAR Land Acquisition and Resettlement

LARP Land Acquisition and Resettlement Plan

LRP Livelihood Restoration Plan

MW megawatt

NGO nongovernment organization

PEDO Pakhtunkhwa Energy Development Organization

PD Project Director

PIU Project Implementation Unit

PMC Project Management Consultants

SPS Safeguard Policy Statement

SASMR Semi-Annual Social Monitoring Report

EXECUTIVE SUMMARY

- 2. The Project Implementation Unit (PIU) is implementing the Balakot Hydropower Project (BHPP) with the financial assistance from Asian Development Bank (ADB) and Asian Infrastructure Investment Bank. The project will (i) improve energy security by increasing the clean energy share in the country's energy mix currently dominated by thermal power generation; (ii) boost the economy and promote revenue generating investments in the hydroabundant Khyber Pakhtunkhwa (KP) Province; and (iii) build capacity and awareness on climate change impacts, adaptation and mitigation measures. The project has been divided into two sections for construction purposes. Therefore, two separate land acquisition and resettlement plans (LARPs) (section-wise) were prepared. The 1st Sectional LARP (Mouza Ghanool and Sangar) was approved by ADB on July 27, 2022, and 2nd sectional LARP (Mouza Bela Sacha and Paras) was approved by ADB on November 29, 2022.
- 3. As per approved 1st sectional LARP comprising Mouza Ghanool and Sangar, total acquired land is 848.40 Kanals (106.05 acres, including 168.2 Kanals of communal land) owned by 1,791 DPs and non-land impacts consisting of (i) 3,045 wood trees, owned by 1,725 DPs, and 876 fruit trees owned by 48 DPs; and (ii) 46 residential structures owned by 40 displaced persons (DPs) with 25 DPs requiring physically relocation. 1 commercial structure (only commercial structure affected but the owner/DP was not required relocate., and 1 masjid (common prayer place). However, total number of land DPs has changed from the original number (1,791 to 1,874 DPs) due to inheritance mutation. Similarly, owners of trees also increased from original number (1,773 to 1,862 DPs). Nonetheless, the amount of payable compensation remains unchanged. Additionally, 39 DPs are eligible for different admissible allowances in the entire 1st sectional LARP.
- 4. As per approved sectional LARP 2 (covering the villages Bela Sacha and Paras), total acquired land is 962.950 Kanals (120.369 acres including 324.52 Kanals of communal land) owned by 1,766 DPs. Similarly, other LAR-related impacts included the following: (i) 9,189 wood trees owned by 1,457 DPs, and 1,448 fruit trees owned by 118 DPs; and (ii) 410 structures owned by 398 DPs (of which 196 DPs required physical relocation), and 9 communal or public structures, including 2 masjids (prayer place), 2 graveyards, and 5 government buildings (2 government schools, 1 basic health facility, 1 revenue office, and 1 forest office) in villages Bela Sacha and Paras.³ However, total number of land DPs changed from the original number (1,766 to 1,821 DPs) due to inheritance mutation. Similarly, the owners of trees also increased (1,575 to 1,647 DPs). Nonetheless, the amount of payable compensation remains unchanged. Additionally, 286 DPs are eligible for different admissible allowances in the entire 2nd sectional LARP.
- 5. In addition to the land already acquired for the project, PIU is acquiring 15.4 kanal (1.925 acres) of additional private land for slope stabilization at the dam's right side abatement

¹ https://www.adb.org/projects/documents/pak-49055-007-rp-0

² https://www.adb.org/projects/documents/pak-49055-007-rp-1

³ Total of 410 private structures, 15 commercial structures, 4 communal structures including 2 masjids (prayer place), 2 graveyards and 5 government buildings in villages Bela Sacha and Paras.

- in Mouza Bela Sacha. Acquisition of land and LAR impacts and compensation will be documented under LARP addendum, which is currently under ADB's approval.
- 6. The LARP's addendum under section-1 and 2 aims to document the additional/missing claims for eligible allowances and their validation/ verification based on the matrix of entitlements and criteria as per the approved LARPs, the additional compensation for the positive differential between the replacement cost determined by the IVS and the official rates in the approved LARPs and additional land (15.4 kanal) to be acquired at the dam site area in Mouza Bela Sacha under Section-2.
- 7. Implementation of LARP is monitored internally by the PIU and externally by an external resettlement monitor (ERM) engaged by PIU, and internal and external monitoring reports are provided to PIU and shared with ADB. This SSMR (internal) covers the implementation of both sectional LARPs 1 and 2 for the period from January to June 2024. Implementation of sectional LARPs began in August 2022 by the PIU and Land Acquisition Collector (LAC), Mansehra District Officer Revenue. Initially, implementation of sectional LARPs encountered delays due to frequent transfers of relevant officials in the land revenue department and engagement of revenue staff in the provincial and national level election throughout the country. Nonetheless, the PIU, with support from the project management consultant (PMC), continued exhaustive efforts to move the compensation process, while also addressing the compensation cases stuck or impeded due to different administrative and legal reasons. No DPs have been physically displaced by PIU from housing so far, (while under already demolished structures no owners have been displaced as such demolished structures was vacant since long time and not in used/functional by any owners). Although many DPs left their structures after receiving full compensation from LAC office Mansehra. As of reporting period 208 DPs left their structures voluntarily since April 2024. PIU and PMC continue to coordinate with the district revenue department/LAC office Mansehra to accelerate the disbursement of compensation and allowances to all unpaid DPs (including those with legal impediments to compensation). Staff of PIU/PMC also continue to inform the unpaid DPs through their relatives and Patwaris to come forward and receive their compensation as soon as possible. These efforts of PIU and PMC are in accordance with ADB's guidance note on handling compensation cases with legal and administrative impediments in Annexure-1. Sample copies of impediment documents (scanned) are in Annexure-2.
- 8. **Status of Implementation:** As per approved sectional LARPs (section-1), PKR 92.66 million (65.63%) of the total payable land compensation amount of PKR 141.19 million has been disbursed to 795 of total 1,874 DPs (42.4%, 1,791 DPs of approved LARPs, and 83 DPs of inheritance mutation) for land of 544.94 kanal (68.12 acres) out of total 848.40 kanal (106.05 acres) or 64.23% in two villages under section-1. Accordingly, for trees compensation, 788 of total 1,862 DPs (42.3%) received PKR 23.63 million out of total PKR 32.71 million (72.25%). Moreover, affected built-up property compensation paid to 100% of total 40 DPs with an amount of PKR 72.52 million of total PKR 74.53 million (97.30%) in two villages under section 1 of BHPP. Similarly, LAC (revenue department) and PIU supported by PMC is responsible for all types of payments of allowances, such as for severity, vulnerability, structure relocation, shifting for houses, shifting for commercial structures, transition, business moving assistance, house rent, business allowance for 12 months, electricity, and household dislocation (chulla)

allowance. As per approved LARPs in the affected two villages of the project, 38 DPs of total 39 DPs (97.4%) have been paid for all their admissible allowances, including dislocation (chulla) allowance, and 17 DPs are paid for their vulnerability allowance amounting PKR 59.50 million of total PKR 59.56 million (99.9%). The 1 unpaid DP of allowance amounting PKR 0.063 million are undisbursed mainly because DP is out of the village. The DP was already informed through their relatives and neighbors, and soon will receive their due allowance once he returns to the village.

- 9. As per approved sectional LARPs (section-2), PKR 236.68 million of the total payable land compensation amount of PKR 426.50 million (55.49%) has been disbursed to 653 of total 1.821 DPs (35.86%) (1.766 DPs of approved LARPs, and 55 DPs of inheritance mutation) for land of 405.20 kanal (50.65 acres) of total 962.95 kanal (120.369 acres) (42.08%) in two villages under section-2 of BHPP, Accordingly, for trees compensation, 375 DPs of total 1,647 DPs (22.77%) received PKR 44.33 million out of total PKR 49.10 million (90.28%). Moreover, affected built-up property compensation was paid to 100% of total 398 DPs with an amount of PKR 1,323.32 million of total PKR 1,424.47 million (92.90%) in two villages under section 2 of BHPP. Similarly, LAC (revenue department) and PIU supported by PMC is responsible for all types of payments of allowances such as severity, vulnerability, structure relocation, shifting for houses, shifting for commercial structures, transition, business moving assistance, house rent, business allowance for 12 months, electricity and household dislocation (chulla) allowance. As per approved LARP section 2 in the affected two villages of the project, 220 of total 286 DPs (76.92%) have been paid for all their admissible allowances, including dislocation (chulla) allowance, and 41 DPs are paid for their vulnerability allowance amounting PKR 440.97 million of total PKR 468.21 million (94.18%). The 66 unpaid DPs of allowances amounting PKR 27.25 million are undisbursed mainly because these DPs are out of village. They were already informed through their relatives and neighbors, and soon will receive their due allowances once they return to the village.
- 10. Hence, 258 of total 325 DPs have been paid PKR 500.467 million of total PKR 527.78 million (94.83%) during the reporting period in all four villages of the project. Overall status of disbursement of LARP (land and non-land assets compensation and allowances) in mouzas/villages under each section are in chapter 4. Scanned copies of land and non-land assets compensation and allowance voucher (payment receipt) are in **Annexure-3.** The Table ES-1 shows the progress during previous quarters, progress during reporting period January-June 2024 and overall cumulative progress. Table ES-2 shows the paid and unpaid DPs of land and non-land compensation amount under each category.

Table ES-1: Summary of Section wise LAR Impacts and Entitlement Categories of BHP Project

		Tot	al DPs and	l Payable Ar	mount		ess Durin				ress Duri					_	
						Quarters	(July- De	cembe	er 2023)	Quarter	s (Januar	y-Jun	e 2024)	Cu	mulative	Progres	S
S. No.	Type of Compensation & Admissible Allowances	Payable Payment (Million)	Total DPs as per approved LARP	Additional DPs of inheritance Mutation	Total DPs (Approved LARP + inheritance Mutation)	Paid Amount (Million)		Paid DPs	Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs
1	Land Compensation (Awarded)																
i.	Section-1	141.19	1,791	83	1,874	82.11	59.08	639	1235	10.55	48.53	156	1,079	92.66	48.53	795	1,079
ii.	Section-2	426.50	1,766	55	1,821	188.27	238.22	460	1361	48.41	189.82	193	1,168	236.68	189.82	653	1,168
Tota	al Land Compensation Amount	567.69	3,557	138	3,695	270.39	297.31	1,099	2,596	58.96	238.35	349	2,247	329.34	238.35	1,448	2,247
2	Non-Land Compensation																
2.1	Section-1																
i.	Trees Compensation	32.71	1,773	89	1,862	17.70	15.01	645	1217	5.93	9.07	143	1,074	23.63	9.07	788	1,074
ii.	Built-up Property	74.53	40	N. A	40	72.52	2.01	40	0	-	-	-	-	72.52	2.01	40	0
2.2	Section-2																
i.	Trees Compensation	49.10	1,575	72	1,647	32.24	16.86	223	1424	12.09	4.77	152	1,272	44.33	4.77	375	1,272
ii.	Built-up Property	1424.47	398	N. A	398	1323.32	101.20	398	0	-	-	-	-	1323.32	101.20	398	0
	al of Non-Land Compensation bunt	1580.81	3,786	161	3,947	1445.78	135.08	1,306	2,641	18.02	13.84	295	2,346	1463.8	117.05	1,601	2,346
3	Other Admissible Allowances																
3.1	Section-1																
i.	Vulnerability Allowance (18 DPs)																
ii.	Structure Relocation (27 DPs)																
iii.	Shifting Allowance (For House) (27 DPs)																
iv.	Transition Allowance (25 DPs)				0.0		0.400			0.400				=0 =00			
V.	House Rent Allowance (25 DPs)	59.565	39	N. A	39	59.376	0.189	36	3	0.126	0.063	2	1	59.502	0.063	38	1
vi	Electricity Allowance (25 DPs)																
vii.	Household Dislocation (Chula) Allowance (25 DPs)																
viii.	Severe Impact Allowance (26 DPs)																

		Tota	al DPs and	Payable Ar	mount		ess Durin (July- De				ress Durii s (Januar			Cu	mulative	Progres	ss
S. No.	Type of Compensation & Admissible Allowances	Payable Payment (Million)	Total DPs as per approved LARP	Additional DPs of inheritance Mutation	Total DPs (Approved LARP + inheritance Mutation)	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs
ix.	Shifting Allowance (Commercial Structure) (1 DP)				,												
x.	Business Moving assistance (1 DP)																
xi.	Business Allowance for 12 Month (1 DP)																
3.2	Section-2																
i.	Vulnerability Allowance (52 DPs)																
ii.	Structure Relocation (190 DPs)																
iii.	Shifting Allowance (For House) (190 DPs)																
iv.	Transition Allowance (190 DPs)																
V.	House Rent Allowance (190 DPs)																
vi	Electricity Allowance (190 DPs)																
vii.	Household Dislocation (Chula) Allowance (196 DPs)	468.214	286	N. A	286	403.829	64.385	204	82	37.136	27.249	16	66	440.965	27.249	220	66
viii.	Severe Impact Allowance (219 DPs)																
ix.	Shifting Allowance (Commercial Structure) (15 DPs)																
х.	Business Moving assistance (15 DPs)																
xi.	Business Allowance for 12 Month (15 DPs)																
xii.	Loss of Temporary Employment (44 DPs)																
	nd Total of Section-1 & 2	0.070.077	7.000	000	7.007	0470 0=	400.00	0.645	F 000	444.046	070 500	000	4.000	2293.607	200 746	0.007	4.000
	nd & Non-Land Compensation llowances Amount)	2,676.275	7,668	299	7,967	2179.37	496.92	2,645	5,322	114.242	279.502	662	4,660	(85.7%)	382.712	3,307	4,660

Table ES-2: Summary of Paid and Unpaid DPs under each Category of Compensation

(Amount in PKR)

											ensation		,					(7 117	iodiii ii	II FKN)
							er Appro	oved LARP & A	dditional	DPs du					P implementa					
				1	DPs of	Acquired Land		T			<u>D</u>	Ps of A	Affected Trees	<u> </u>	1		Ps of A	Affected Built-up	Proper	ty
Section	Mouzas (Villages)	No. of DPs as per LARP	Additional DPs due to Inheritance Mutation	Total No. of DPs	Paid DPs	Paid Compensation Amount	Unpaid DPs	Unpaid Compensation Amount	No. of DPs as per LARP	Additional DPs due to Inheritance Mutation	Total No. of DPs	Paid DPs	Paid Compensation Amount	Unpaid DPs	Unpaid Compensation Amount	No. of DPs as per LARP	Paid DPs	Paid Compensation Amount	Residential Relocation Paid DPs	Residential Relocation Unpaid DPs
	Ghanool	126	36	162	98	1,964,067	64	799,834	100	36	136	94	1,785,548	42	713,402	N. A	N. A	N. A	N. A	N. A
1	Sangar	1665	47	1712	697	90,695,235	1015	47,734,563	1673	53	1726	694	21,845,330	1,032	8,361,352	40	40	72,523,045	25	0
Total of	Section-1	1,791	83	1,874	795	92,659,302	1,079	48,534,397	1,773	89	1,862	788	23,630,878	1,074	9,074,754	40	40	72,523,045	25	0
2	Bela Sacha	126	41	167	128	67,260,480	39	13,861,943	138	72	210	152	10,336,355	58	868,924	32	32	184,291,946	5	0
2	Paras	1,640	14	1654	525	169,415,108	1,129	175,960,997	1,437	0	1,437	223	33,989,957	1,214	3,904,211	366	366	1,139,022,723	185	0
Total of	Section-2	1,766	55	1,821	653	236,675,588	1,168	189,822,940	1,575	72	1,647	375	44,326,312	1,272	4,773,135	398	398	1,323,314,669	190	0
	Total of o-1 & 2	3,557	138	3,695	1,448	329,334,890	2,247	238,357,337	3,348	161	3,509	1163	67,957,190	2,346	13,847,889	438	438	1,395,837,714	215	0

Table ES-2: Summary of Paid and Unpaid DPs under each Category of Allowances

					N	o. of	Entitle	d DPs	& No.	of A	dmissil	ole A	lowanc				
				-		ion-1							Secti				
		M	ouza (\		e)	N	Mouza (e)	I	Mouza			N	louza (V	illage)
			Ghan	1001	1		San	igar			Bela S	Sacna	1		Para	S	ı
S. No.	All Admissible Allowances	Total No. of DPs	Total No. of Admissible Allowances	Paid DPs	Unpaid DPs	Total No. of DPs	Total No. of Admissible Allowances	Paid DPs	Unpaid DPs	Total No. of DPs	Total No. of Admissible Allowances	Paid DPs	Unpaid DPs	Total No. of DPs	Total No. of Admissible Allowances	Paid DPs	Unpaid DPs
1	Vulnerability Allowance	3	3	3	0		15				9				42		
2	Structure Relocation						27				5				185		
3	Shifting Allowance (For House)						27				5				185		
4	Transition Allowance						25				5				185		
5	House Rent Allowance						25				5				185		
6	Electricity Allowance						25				5				185		
7	Household Dislocation (Chula) Allowance	NA	NA	NA	NA	36	25	35	1	24	5	10	14	218	191	192	26
8	Severe Impact Allowance						26				7				212		
9	Shifting Allowance (Commercial Structure)						1				3				12		
10	Business Moving assistance						1				3				12		
11	Business Allowance for 12 Month						1				3				12		
12	Loss of Temporary Employment	NA	NA	NA	NA	NA	NA	NA	NA	8	8	2	6	36	36	16	20
	No. of DPs & ances	3	3	3	0	36	198	35	1	32	63	12	20	254	1,442	208	46

NA = not applicable

- 11. The field staff of PIU and PMC continued to support the revenue department staff to expedite the disbursement of compensation to the DPs of both sectional LARPs. PIU/PMC collected the field data of both sectional LARPs, and prepared the required documentation of the DPs whose compensation payment is unpaid due to legal and administrative impediments. Consultation meetings with DPs and awareness campaigns were launched by PIU/PMC in their efforts to reach out to the DPs. A scanned copy of these efforts is in **Annexure-4**.
- 12. Valuation of affected land and non-land assets by an independent valuation expert: As required under ADB's Safeguard Policy Statement 2009, PIU engaged a certified independent valuer to undertake an independent valuation study of the affected assets to determine if the awarded prices meet the SPS's requirement of full replacement costs". The valuer undertook a sample valuation study (IVS) during January-March 2023. The study determined a differential between the awarded compensation rates and the IVS rates. The

IVS report and the differential has been reviewed and approved by the Provincial Cabinet of the Government of Khyber Pakhtunkhwa (GoKPK). Earlier, ADB also reviewed the report and solicited clarifications from the expert on the valuation and the payment of differential to DPs through an addendum LARP.

- 13. Following the governmental approval, the results of IVS were presented to the members of GRCs including a few DPs and community members. ADB representative joined that meeting virtually while others including PIU and GRC members/DPs joined in-person. The GRC members and DPs/ community members expressed their satisfaction on the study findings, and they requested PIU for early release of differential payments. The Project Director to them that payment of differential will be paid through the Addendums of LARP-1 and 2 separately after approval of the same by ADB. The minutes of meeting/ presentation of IVS available at **Annexure-5**. The addendum of 1st sectional LARP has been submitted to ADB on June 13, 2024, for onward approval.
- 14. The LARP implementation status during the reporting period (January-June 2024) is in Table 4.7 in chapter 4 (section-wise mouzas highlighted in gray, green and blue colors where full implementation of LARP is confirmed, and already validated by the EMA [External Resettlement Agent of PIU] through the 1st, 2nd, 3rd and 4th EMRs, respectively). The undisbursed compensation amount for acquired land is already deposited and secured in the district treasury for payment to the unpaid DPs having legal/administrative impediments as and when they will show up with valid claim documents after resolving their issues/impediments. The PIU confirms that all DPs other than those unpaid due to legal and administrative impediments have been fully compensated for all LAR impacts and payable allowances in all mouzas under 1st and 2nd sectional LARP as of June 2024. The detailed list of paid and unpaid DPs of land, trees and built-up property of each mouzas was previously provided in 3rd SASMR (July-December 2022) for mouza Bela Sacha and Paras which available separately in Appendixes-13, 14, 15, 16, 17 and 18, while for mouza Sangar provided in 2nd SASMR (July-October 2022) available in Appendixes-1, 2 and 3, and for mouza Ghanool provided in 1st SASMR (July-October 2022) available in Appendix-5.
- 15. The findings of the internal SSMR of January-June 2024 for both the sectional LARPs 1 and 2 show that from the total 3,695 DPs of all 4 villages, 1,448 DPs have been fully compensated, whereas the remaining 2,247 DPs are still unpaid due to different reasons (i.e. legal and administrative impediments) that are beyond PIU's power to address or resolve alone. The details of unpaid 2,247 DPs by type of impediment are as follows: 45 DPs have court cases on internal family disputes; 65 DPs live/work abroad; 266 DPs have inheritance mutation issues; 1,118 DPs continue to remain disinterested in receiving compensation due to meager amount compensation; 4 DPs are juvenile and do not have either national identity card (CNIC) or guardian certificates, which PIU and LAC require to address this impediment to the compensation disbursement; 317 DPs live out of city; and 432 DPs out of village. While PIU/PMC continue to reach out to the unpaid DPs through different means and make all possible efforts in addressing all types of impediments to compensation, no unpaid DPs have been dislocated so far. Table ES-3 presents a detailed summary of unpaid DPs (by category of impediment) for a clear understanding of the situation.

- 16. The institutional set up of PIU has well established safeguards management arrangements with social and environmental management specialists available full time for implementation and internal monitoring of sectional LARPs, environmental impact assessment, environmental management plan, and site-specific environmental management plans. Overall, Project Director BHPP at PIU is responsible to implement and ensure compliance with social and environmental safeguard requirements of ADB's Safeguard Policy Statement 2009 (SPS), and project-specific requirements of social and environment safeguards. PD PIU and the Safeguard Unit are further assisted by the PMC, which have the services of social and environmental specialists made available to PIU under PMC.
- 17. The safeguard unit/team at PIU is headed by Deputy Director Social & Resettlement responsible for implementation of LARP supported by Deputy Director Land Acquisition, Assistant Director Social & Resettlement and Patwaris (land record keeper). The BHPP staff regularly conducted meetings with Deputy Commissioner (DC), Mansehra and revenue department staff, including Additional Deputy Commissioner (ADC), Assistant Commissioner (AC), Tehsildar and Patwari (land record keeper) of Tehsil concerned, to pursue disbursement of all types of compensation and allowances on fast track, and the meager compensation amount to the unpaid DPs as soon as possible. The minutes of meeting with DC/ADC/revenue officials are annexed in **Annexure-6**.

Table ES-3: Summary of Unpaid DPs under each unpaid Category

(Amount in PKR)

				-	_			DP In	herita	nce			-	DP	s Juve	nile									1		
	ages)		y Orde ivil Co			s out ountr		Muta	tion u	nder		with N Amou	/leager nt		er the a			munal and	DPs	out of	City	DPs	Out of	Village	of OPs	aid	paid nt
Section	Mouzas (Villages)	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	Total No. of Unpaid DPs	Total un-paid Land Parcel	Total Unpaid Amount
	Ghanool	1	_	222,018	5	5	98,174	13	13	276,905	27	27	38,169	4	4	7,429	0.95	14,755	A.A.	A.A.	N.A	14	14	142,384	64	64	799,834
1	Sangar	8	80	5,586,587	39	39	2,516,686	155	155	10,284,382	508	508	878,928	N.A	A.N	Ą. Z	167.25	16,282,145	135	135	1,262,370	170	170	10,923,465	1,015	1015	47,734,563
	al of tion-1	6	6	5,808,605	44	44	2,614,860	168	168	10,561,287	535	535	917,097	4	4	7,429	168	16,296,900	135	135	1,262,370	184	184	11,065,849	1,079	1079	48,534,397 47,734,563
2	Bela Sacha	0	0		10	10	2,753,281	6	6	5,972,372	2	2	4,668	N.A	N.A	N.A	24.33	130,480	8	8	2,296,974	10	10	2,704,168	39	39	13,861,943
2	Paras	36	36	1,207,852	11	11	4,735,000	89	68	18,739,649	581	581	525,219	N.A	N.A	A.S	300.19	51,027,070	174	174	79,817,086	238	238	19,909,121	1129	1129	175,960,997
	al of tion-2	36	36	1,207,852	21	21	7,488,281	86	86	24,712,021	583	583	529,887	N.A	A.A	Ą.	324.52	51,157,550	182	182	82,114,060	248	248	22,613,289	1,168	1,168	189,822,940
of Se	d Total ction-1	45	45	7,016,457	65	9	10,103,141	266	266	35,273,308	1118	1118	1,446,984	4	4	7,429	492.52	67,454,450	317	317	83,376,430	432	432	33,679,138	2,247	2,247	238,357,337

- 18. PIU, supported by safeguard unit team and PMC safeguard experts, is making continuous efforts to expedite implementation of sectional LARPs. Part of this effort includes dissemination to the DPs through installation and public display banners at public offices such as AC/Tehsildar office Balakot service delivery center at Balakot, and public places Jamia Masjid, and notable places in the affected mouzas of the project. Under exhaustive efforts, the PIU provided LARP-related information to DPs through public advertisements published in local newspaper and other means of social media informing the DPs about compensation and allowances they can receive from the concerned Tehsildar office of revenue department. A copy of the advertisement and link to social media are annexed at **Annexure-7**. The additional measures undertaken by the project through an IVS to validate replacement rates were already communicated to the DPs through information brochure on LARP in Urdu (local) language among the DPs in all the affected mouzas of the project. The process of dissemination of information brochures is going on till the complete payment of compensation and allowances in the affected mouzas. A scanned copy of information brochure of LARP in Urdu/local language is in **Annexure-8**.
- 19. In order to facilitate and expedite disbursement of allowance (payable to DPs as per sectional LARPs), an "Allowance Disbursement Committee" has been constituted under the Chairmanship of ADC (general) Mansehra along with Deputy Director Social and Resettlement of PIU, supported by PMC. The committee members examine every single case of allowance with assistance of PIU/PMC field staff to ascertain and cross verify the required information for considering any DPs for a particular allowance. The LAC/PIU staff, after completing all the verifications, prepare/sign the payment vouchers for eligible DPs. The notification of the LARP's committee for allowances is annexed at the end of report at **Annexure-9**.
- 20. The project's Grievance Redress Mechanism (GRM) is fully operational. The village level Grievance Redress Committees (GRCs) for Ghanool and Sangar were established and made fully functional on 15 September 2022 under sectional LARP 1, whereas GRCs for Bela Sacha and Paras were established under sectional LARP 2 on 26 September 2022 and 12 January 2023, respectively. All GRCs in all four villages are fully functional, and several meetings have been held during the reporting period. However, it was decided by the GRC members that meetings will be held on need basis for the smooth implementation of project activities and best interest of complainants as well. The notifications of GRC committees are annexed in **Annexure-10**. All DPs and local community of the four villages have been fully informed about the GRM and GRCs available to them through community consultation meetings as well as through LARP information brochure dissemination. DPs have been informed about how they can access GRM/GRCs and file any concerns or grievances with the contractors working on the sites, PIU and PMC.
- 21. During field visits in all affected villages, PIU/PMC staff conducted additional consultations with members of GRCs on the issue of "Chullah allowance". The GRC of Mouza Paras initially submitted applications of 279 DPs for Chulla allowance, which after thorough scrutinization by PIU and PMC and clarifications, were reduced to only 124 cases by the demands of the GRC. Similarly, in Mouza Bela Sacha, DPs initially identified as 29 but came down to only 18 by the GRC, whereas in the Mouza of Sangar, the DPs are recorded as 10. After deliberate discussion/meetings with GRC members by PIU/PMC and based on provided documentary proof, the finalized and agreed number of eligible DPs for Chulla Allowance from

each village are completed i.e., the eligible number of DPs under missing Chulla allowances from village Paras are 45, from village Bela Sacha is 1 DP and from village Sangar is also 1 DP. However, remaining DPs are mostly eligible for one-time structure relocation (255 DPs) and business allowance (25 DPs) in all 4 villages. All such DPs along with their claims and provided documents are scrutinized in accordance with the criteria in approved LARPs under section-1 and 2. The detailed information of the eligible DPs under missing allowances are available in the 1st and 2nd sectional LARP's addendum.

- 22. **Applications/ Concern of DPs Submitted to PIU:** As of reporting period of January-June 2024, total of 45 applications/ concerns registered under GRC which were received by PIU from the affected communities, i.e., 2 applications regarding pending labor wages, 26 concerns/ apprehension related to additional/missing allowances, 10 applications related to internal family disputes on LARP's allowances, 1 concern regarding partial assessment of built-up property, 2 concern about demanding of business allowances, 3 applications regarding objection on the GRC members of village Paras GRC and 1 application related to damage of material mixture machine by local administration. Out of total, 43 applications/ concerns have been resolved and only 2 pending applications/ concerns unresolved due to non-availability of both parties for attending the grievance resolution meeting at GRC level.
- 23. Complaints of DPs Submitted to ADB's Accountability Mechanism: Office of Special Facilitator (OSPF) and Compliance Review Panel (CRP): Before implementation of LARP-1, OSPF received one complaint in June 2022 from the village which was related to land acquisition, valuation and compensation. However, CRP received twocomplaints in January 2024 regarding missing business allowance from village Bela Sacha. Parallel commencement of LARPs implementation, PIU completed an IVS that determined a differential in the awarded prices and IVS rates. The IVS differential has been approved by the provincial government for additional payments to DPs through the addendum LARPs. Similarly, CRP complainant provided additional documents to support his claims of business allowance. Based on the documented provided, PIU has accepted the claims for business allowance Annex 11 provides the complainant's satisfaction note on PIU accepting the claim of business allowance.
- 24. The sectional LARPs have provision for employment of local laborers and DPs. PIU continued to follow up with contractors for providing job opportunities to the locals and DPs. The PIU has strongly intimated to the contractor to provide job opportunities to the affected community on priority basis either skilled or unskilled. The contractors maintained a list of skilled and unskilled employed persons on monthly basis, and the Deputy Director Social and Resettlement of PIU is responsible for monitoring and verification of these list of the affected community (locals). The affected community is aware about the job opportunities through community meetings, and meetings with local administration at the tehsil and district levels. The contractor submitted a monthly progress report including data/information of employed persons and locally/affected community. Similarly, the Deputy Director social and resettlement of PIU regularly monitored the locally employed persons with the contractors. As per the contractor's record, the project contractors and consultants have employed a total of 932 persons for short-term employment (skilled and unskilled labor), of which 63.8% (595) has been employed from the project area. All the 595 persons are locals employed from the affected mouzas of the project. Hiring of skilled and unskilled laborers from the local project

area is monitored by PIU every month through the monthly progress reports of contractors. A list of skilled and unskilled employed persons by the contractors during the reporting period is in **Annexure-12**.

- 25. Similarly, long-term project-based employment which is related to output-4 of the project including, relevant training facilitation support under the livelihood restoration plan (LRP) will be provided, i.e. training on agriculture production, livestock rearing, beekeeping, fish farming and linkages with microfinance institution, to the DPs or as per the local requirements, particularly unemployed youths covering both men and women, for relevant skill improvement/ capacity building. This will reduce impact on their livelihood during project implementation. All such training linked and included in draft LRP of BHPP will be finalized and conducted by an NGO. The consultant NGO has been mobilized since September 7, 2023. The final LRP will be finalized and will be shared with all stakeholders before implementation by NGO. The selected NGO will provide realistic date for updating of LRP after mobilization. The mobilization of NGO was delayed due to late submission of the technical and financial evaluations.
- 26. The LARP implementation is also externally monitored through an EMA by PIU. The EMA has been mobilized since June 9, 2022, and submitted external SASMRs to PIU/ADB regularly. On validation of EMA under 1st sectional LARPs, the 1st and 2nd SASMRs (external by EMA) for mouza Ghanool and Sangar (separately) was approved by ADB on December 23, 2022, and December 27, 2022 respectively. Under 2nd sectional LARP, the 3rd SASMR (external by EMA) for mouza Bela Sacha and Paras was approved by ADB on March 7, 2023. The ERM has submitted his last External Monitoring Report (EMR) for July to December 2023 to ADB which was disclosed on March 22, 2024.

1 INTRODUCTION

1.1 Project Background

- 27. The Islamic Republic of Pakistan has received a loan for "Balakot Hydropower Development Project", from ADB loan 4057 PAK and Asian Infrastructure Investment Bank loan 8397 with the cost of \$665 Million, including counterpart fund of \$115 million, for the entire BHPP. This is the SASMR (internal) on LARP implementation for the period from July to December 2023 of BHPP.
- 28. The KP Energy and Power Department is the executing agency, and PEDO is the implementing agency. The PIU was established in May 2019 at PEDO office, Peshawar to manage all the project activities associated with LARP. The PIU is headed by a Project Director responsible for execution and implementation of LARP, and also to ensure the availability of funds for LARP implementation. The PD PIU, with the assistance of Deputy Director Social & Resettlement, Deputy Director Land Acquisition, Assistant Director Social & Resettlement and other staff, is responsible for the timely updating, implementation and monitoring of LAR activities.
- 29. BHPP is classified as category "A" because the involuntary resettlement impacts of ADB supported project are considered significant as more than 200 persons are experiencing major impact, i.e. losing 10% or more of their productive assets or physically relocating.

1.2 Project Objectives

- 30. The BHPP aims to develop a 300 megawatt (MW) run-of-river hydropower scheme on the Kunhar River in Kaghan Valley, between Balakot and Kaghan, Manshera District of KP. The project is aligned with the carbon footprint reduced, and energy sector made more renewable, efficient and reliable. The Project has the following major objectives to achieve:
 - Climate-resilient hydropower plant commissioned: A 300 MW hydropower plant will be commissioned near Balakot City in KP Province.
 - Capacity for climate change risk management in hydropower production enhanced: Awareness will be developed among the communities with specific training for women and youth groups to serve as climate change leaders.
 - PEDO's revenues from indigenous resources increased. PEDO will supply one-third
 of the electricity generated from the 300 MW hydropower plant to the Peshawar
 Electricity Supply Company, and the rest to the National Transmission Dispatch
 Company Limited.
 - Income-earning opportunities and skills for local communities increased. During construction, the local population will benefit from job opportunities, commercial activities, and material supply. The project will generate more than 1,200 skilled and unskilled jobs for male and female workers, of which about 40% will be sourced locally.

1.3 Project LARP Description

31. Resettlement Monitoring and Evaluation is an integral part of the social safeguard requirements (Involuntary Resettlement and Indigenous Peoples), including the LAR process covering the preparation, implementation and monitoring of LARPs. This is a requirement under ADB's SPS and the corresponding loan and project agreements. The BHPP has been divided into two sections for construction purpose. Therefore, two separate LARPs (sectionwise) were prepared for the entire project. The 1st sectional LARP4 (mouza Ghanool and Sangar) and 2nd sectional LARP⁵ (mouza Bela Sacha and Paras) were approved by ADB on July 27, 2022 and November 29, 2022, respectively. Therefore, this SASMR (internal) is prepared for both sections and all affected mouzas under the 1st and 2nd sectional LARPs. In addition to the land already acquired for the project, PIU is acquiring 15.4 kanal (1.925 acres) additional private land for slope stabilization at dam right side abetment in Mouza Bela Sacha. Acquisition of land and LAR impacts and compensation will be documented under LARP addendum, which is currently under ADB's approval. More information on the project sections, component of BHPP, mouza, acquired land affected (only) and number of DPs are summarized in Table 1.1.

Table 1.1: Section, Mouza and Component wise Summary of Acquired Land with No. of DPs⁶ of BHPP

				,		No. of DPs Affect		
Sectio n	Mouzas (Villages)	Component of BHPP	UTM Coordinates	Acquired Land in Kanals (Acres)	Total No. of Land Plots	As per approved LARP	Additional No. of DPs due to Inheritance Mutation (as per LARP implementation)	Total No. of Land DPs
	Ghanool	Surge Shaft and access road to Surge Shaft	E 351684.82 N 3830355.72	30.95/ (3.87)	126	126	36	162
1	Sangar	Powerhouse, access road, tailrace, staff colony and switch yard	E 3503113.03 N 3828607.92	817.45/ (102.18)	1,665	1,665	47	1,712
Total of	Section-1			848.40/ 106.05)	1791	1791	83	1874
2	Bela Sacha	Dam Right Side Abutment, Reservoir, Diversion/ Sediment By-Pass Tunnel and Access Road to Diversion/ Sediment By- Pass Tunnel	E 357872.122 N	175.575/ (21.947)	126	126	41	167
		Additional land for construction of slope stabilization of right abutment	3836447.78	15.4/ (1.925)	44*	-	-	44
	Paras	Dam Left Side Abutment, Reservoir, Intake of	E 359038.92	787.375/ (98.422)	1640	1640	14	1654

⁴ https://www.adb.org/projects/documents/pak-49055-007-rp-0

https://www.adb.org/projects/documents/pak-49055-007-rp-1

⁶ In the context of the LARP, the affected persons corresponding to all persons belonging to affected households, and DPs refer to all landowners and shareholders found on land records (co-owners) and eligible for land compensation for Board of Revenue purposes.

				,	_	No. of DP: Affect	cted	
Sectio n	Mouzas (Villages)	Component of BHPP	UTM Coordinates	Acquired Land in Kanals / (Acres)	Total No. of Land Plots	As per approved LARP	Additional No. of DPs due to Inheritance Mutation (as per LARP implementation)	Total No. of Land DPs
		Headrace Tunnel and	N					
		Access Road to Dam Crest	3836812.05					
Total of	Section-2			962.950/ (120.369)	1,766	1,766	55	1,821
Total of	Section-1	& 2		1811.35/ (226.419)	3,557	3,557	138	3,695
Total of Land)	Section-2	(under Addendum LARP of	Additional	15.4/ (1.925)	44*	-		44*

^{*} The 44 DPs under additional land are part of the DPs in the main Section-2 LARP. However, exact share/portion due to these 44 DPs losing additional land will be finalized once the acquaintance roll for additional land is finalized by the revenue department.

Table 1.2: Section and Mouza wise Summary of Affected Trees with No. of DPs of BHPP

			No.	of DPs of Trees	s Affected	Total Trace	
Section	Mouza (Village)		No. of DPs as Per Approved LARP	dditional DPs o inheritance Mutation	Total No. of DPs as per Approved LARP + Inheritance Mutation)	Total Trees Compensation Amount Payable	Total No. of Trees Affected
	Ghanool	Timber Tree	100	36	136	2,498,950	192
1	Congor	Fruit Trees	48	5	53	20,723,092	876
	Sangar	Timber Tree	1,625	48	1,673	9,483,590	2,853
Tota	I of Section-1	Fruit Trees	48	5	53	20,723,092	876
TOLA	ii oi section-i	Timber Tree	1,725	84	1,809	11,982,540	3,045
		Fruit Trees	13	0	13	9,114,061	319
	Bela Sacha	Timber Tree	125	72	197	2,091,218	5,357
2	Paras	Fruit Trees	105	0	105	34,028,730	1,129
	Paras	Timber Tree	1,332	0	1,332	3,865,438	3,832
	Total of	Fruit Trees	118	0	118	43,142,791	1448
	Section-2	Timber Tree	1,457	72	1,529	5,956,656	9,189
Total	of Section-1 &	Fruit Trees	166	5	171	63,865,883	2,324
	2	Timber Tree	3,182	156	3,338	17,939,196	12,234
	Grand Tot	al	3,348	161	3,509	81,805,079	14,558

Table 1.3: Section and Mouza wise Summary of Built-up Property with No. of DPs of BHPP

		Built-up	Т	ypes & No. o	f Built-up P	roperties			Total Built-up
Section	Mouza (Village)	Property Category	Residential	Commercia I		Communal (Graveyard)	Public	Total DPs	Property Compensation Amount Payable
1	Sangar	Private (Individual)	25	1	N. A	N. A	N. A	40	72,523,045
'	Sangar	Private (Communal)	N. A	N. A	1	N. A	N. A	N. A	2,009,972
2	Bela Sacha	Private (Individual)	29	3	N. A	N. A	N. A	32	184,291,938
	Paras	Private (Individual)	366	12	N. A	N. A	N. A	366	1,139,022,723

_		Built-up	T	ypes & No. o	f Built-up P	roperties			Total Built-up
Section	Mouza (Village)	Property Category	Residential	Commercia I		Communal (Graveyard)	Public	Total DPs	Property Compensation Amount Payable
		Private (Communal)	N. A	N. A	2	2	N. A	N. A	101,151,625
		Public	N. A	N. A	N. A	N. A	5	N. A	101,101,020
_	otal of	Private (Individual)	420	16	0	0	0	438	1,395,837,706
	Total of Section- 1 & 2	Private (Communal)	0	0	3	2	0	0	103,161,597
		Public	0	0	0	0	5	0	
	Grand '	Total	420	16	3	2	5	438	1,498,999,303
		•	Amo	ount in Million	n		•		1498.999

1.3.1 Section-1: Mouza Ghanool and Sangar (under 1st Sectional LARP)

1.3.1.1 Mouza Ghanool

32. Based on approved 1st sectional LARP of the project, BHPP component comprises of Surge Shaft and access road to Surge Shaft in Mouza Ghanool. A land of 30.95 kanal (3.87 acres) has been acquired for the above-mentioned dam component/infrastructure under section-1. As per LARP implementation in mouza Ghanool under paid land of 21.36 Kanal (2.67 acres) (69.01%), comprise maximum 2.91 kanal (0.363 acres) (13.62%), minimum 0.03 kanal (0.00375 acres) (0.14%), and average 0.218 kanal (0.2727 acres) (1.02%) of land impacted as per paid DPs. Similarly, under unpaid land of 9.59 Kanal (1.20 acres) (30.99%), comprise maximum 2.93 kanal (0.366 acres) (30.55%), minimum 0.023 kanal (0.0028 acres) (0.24%), and average 0.15 kanal (0.019 acres) (1.56%) of land impacted as per unpaid DPs. Location map of mouza Ghanool (section-1) is in Figure 1.1.

1.3.1.2 Mouza Sangar

33. Similarly, as per approved 1st sectional LARP of the project, BHPP component comprises Access Tunnel to Cavern Powerhouse, access roads, tailrace, staff colony, and switch yard in mouza Sangar. A land of 817.45 kanal (102.18 acres) has been acquired for the above-mentioned dam component/infrastructure in mouza Sangar under section-1. As per LARP implementation in mouza Sangar under paid land of 523.58 kanal (65.45 acres) (64.1%), comprise maximum 24.30 kanal (3.04 acres) (5.37%), minimum 0.00033 kanal (0.0000413 acres) (0.000073%), and average 0.75 kanal (0.094 acres) (0.143%) of land impacted as per paid DPs. Similarly, under unpaid land of 293.87 Kanal (36.73 acres) (35.95%), comprise maximum 7.19 kanal (0.899 acres) (2.45%), minimum 0.002 kanal (0.00025 acres) (0.00068%), and average 0.28 kanal (0.035 acres) (0.095%) of land impacted as per unpaid DPs. During LARP implementation and as per revenue record, no DP was identified as squatter or unregistered user of the affected land plots. Location map of mouza Sangar (section-1) is in Figure 1.1.

1.3.2 Section-2: Mouza Bela Sacha and Paras (under 2nd Sectional LARP)

1.3.2.1 Mouza Bela Sacha

34. Based on approved 2nd sectional LARP of the project, BHPP component comprises Dam Right Side Abutment, Reservoir, Diversion/Sediment By-Pass Tunnel and Access Road to Diversion/Sediment bypass Tunnel in mouza Bela Sacha. A land of 175.575 kanal (21.947)

acres) has been acquired for the above-mentioned dam component/infrastructure in mouza Bela Sacha under section-2. As per LARP implementation in mouza Bela Sacha under paid land of 132.03 kanal (16.50 acres) (75.2%), comprise maximum 12.87 kanal (1.61 acres) (9.75%), minimum 0.01 kanal (0.00125 acres) (0.008%), and average 1.03 kanal (0.129 acres) (0.780%) of land impacted as per paid DPs. Similarly, under unpaid land of 43.55 Kanal (5.44 acres) (27.80%), comprise maximum 11.37 kanal (1.42 acres) (26.11%), minimum 0.002 kanal (0.0025 acres) (0.046%), and average 1.11 kanal (0.14 acres) (2.55%) of land impacted as per unpaid DPs. During LARP implementation and as per revenue record, no DP was identified as squatter or unregistered user under the affected land plots. Location map of mouza Bela Sacha (section-2) is in Figure 1.2.

1.3.2.2 Mouza Paras

35. Similarly, based on approved 2nd sectional LARP of the project, BHPP component comprises Dam Left Side Abutment, Reservoir, Intake of Headrace Tunnel and Access Road to Dam Crest in mouza Paras. A land of 787.375 kanal (98.422 acres) has been acquired for the above-mentioned dam component/infrastructure in mouza Paras under section-2. As per LARP implementation in mouza Paras under paid land of 273.17 kanal (34.15 acres) (34.70%), comprise maximum 10.85 kanal (1.36 acres) (3.97%), minimum 0.0034 kanal (0.00043 acres) (0.00125%), and average 0.52 kanal (0.065 acres) (0.190%) of land impacted as per paid DPs. Similarly, under unpaid land of 514.205 Kanal (64.28 acres) (65.31%), comprise maximum 7.55 kanal (0.944acres) (1.47%), minimum 0.0010 kanal (0.000125 acres) (0.000178%), and average 0.46 kanal (0.058 acres) (0.089%) of land impacted as per unpaid DPs. During LARP implementation and as per revenue record, no DP was identified as squatter or unregistered user of the affected land plots. Location map of mouza Paras (section-2) is in **Figure 1.2**.


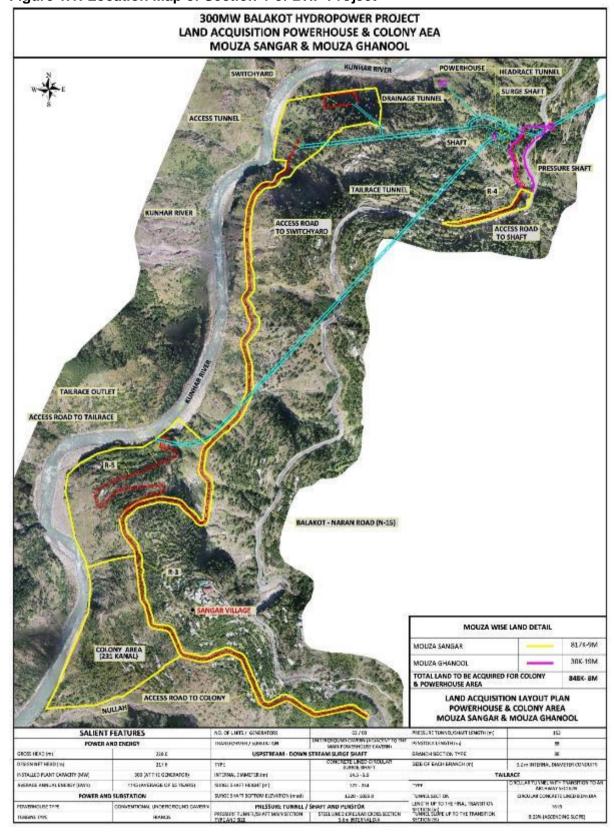


Figure 1.1: Location Map of Section-1 of BHP Project

Figure 1.2: Location Map of Section-2 of BHP Project

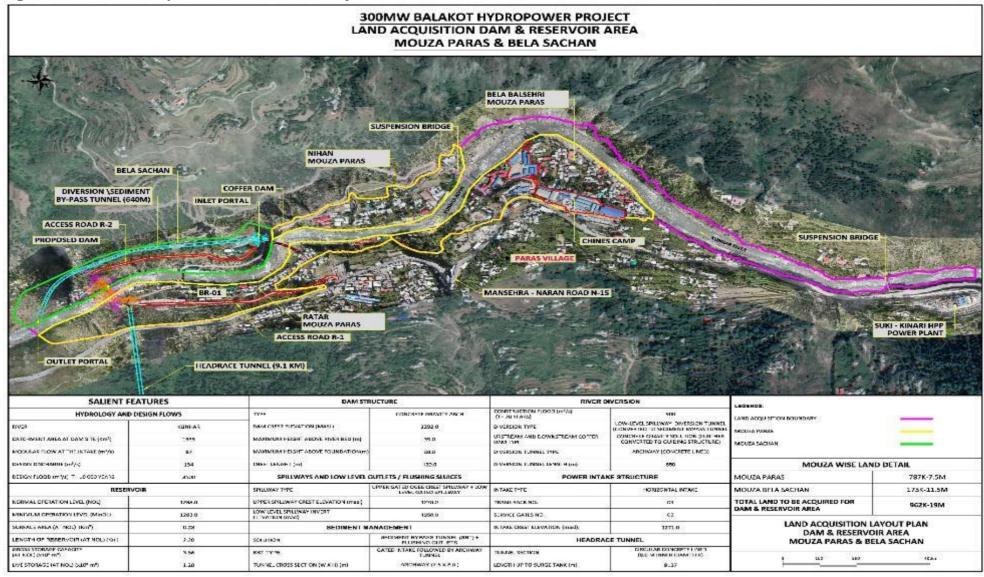

2 INTERNAL MONITORING REPORT OF LARP IMPLEMENTATION

2.1 Internal Monitoring Requirements of LARPs

The LARP implementation is internally monitored by the safeguard's unit in PIU and 36. an ERM is engaged to review and validate the monitoring progress, and deliver EMRs. Internal monitoring is conducted on semi-annual basis, and this LARP implementation SASMR for the period from 1 January to 30 June 2024 of BHPP covers both sectional LARPs. Implementation of sectional LARPs began in August 2022 by the PIU and LAC, Mansehra District Revenue Office. Initially, implementation of sectional LARPs encountered delays due to frequent transfers of relevant officials in the land revenue department and engagement of revenue staff in the provincial and national level election throughout the country. Nonetheless, PIU with support from PMC consultants continued exhaustive efforts to move the compensation process while addressing the compensation cases stuck or impeded due to different administrative and legal reasons. No DPs have been physically displaced by PIU from housing so far, although many DPs left their structures after receiving full compensation from PIU. This has been confirmed by PIU's EMA in his last external SASMR of July to December 2023. However, compensation has been disbursed accordingly, and the land and non-land affected owners compensated as per provisions of the approved LARPs. This LARP SASMR (internal) for January-June 2024 shows the status of full implementation of LARP in all mouzas which is previously validated by the EMA through his 1st, 2nd, 3rd and 4th EMRs.

2.2 Objectives of the Internal Monitoring Report

- 37. This internal monitoring report presents the safeguards management progress achieved, and coordination and consultations to mobilize and assist the DPs for receiving compensation and redress their grievances. It summarizes the progress on following aspects:
 - Delivery of compensation for assets and entitled allowances.
 - Collection of DPs data and preparation of LAR record, issues and progress.
 - Activities and actions for the compensation of payment to the DPs with which efforts were implemented by recording additional documentation as required under ADB's SPS 2009 guidance notes on handling compensation cases with legal and administrative impediments.
 - Community consultation and information dissemination activities performed for compensation disbursement.
 - Updates on recording and handling of grievances.
 - Employment (skilled/ unskilled) data of DPs and local community who got opportunity in the construction work.
 - Any scope changes, design changes, new and unanticipated LAR impacts and damages, if any.

2.3 Monitoring Indicators

- 38. Specific monitoring benchmarks are based on the approved LARP and cover the following:
 - Mouza (village) wise disbursement of compensation and status of land acquisition in all affected Mouzas of BHPP.
 - Information campaign and consultation with DPs.
 - Status of land acquisition and payments on land compensation.
 - Status of trees and structures compensation.
 - Status of payment for all admissible allowances.
 - Income restoration activities.
 - Adherence to gender mitigation measures (complaints/grievances) in the LARP during bi-annual internal monitoring and reporting process.
 - Employment opportunities.

3 INSTITUTIONAL ARRANGEMENT AT PIU FOR BHPP

3.1 LARP's Implementation and Monitoring Set-up

39. The safeguards management set-up makes the PIU responsible for timely and smooth implementation of LARP for BHPP. Under supervision of the PD, PIU staff kept a close liaison with the LAC, district land revenue offices and the DPs to facilitate processing and delivery of compensation claims to the DPs. The safeguards set-up of PIU headed by PD include Deputy Director Social & Resettlement, Deputy Director Land Acquisition, Deputy Director Health, Safety, Environment and Gender, Assistant Director Social & Resettlement and Patwaris (land record keepers) revenue. In addition, the Land Acquisition Collector/DC Mansehra from District Land Revenue Department with land revenue staff is supporting PIU/PMC in land acquisition and payment of awarded compensation under Land Acquisition Act (LAA) 1894.

3.2 Project Steering Committee

40. The Project Steering Committee comprises under the Chairmanship of Additional Chief Secretary, KP and DC Mansehra. During the reporting period, no Project Steering Committee meeting have been conducted as meetings are conducted on need basis. However, DC Mansehra, directed the revenue staff to ensure disbursement of land compensation and allowances on fast track to the unpaid DPs.

3.3 Disbursement of Allowances by LAC/ PIU

41. The LAC and PIU are responsible for payments of allowances such as severity, vulnerability, shifting allowance for house/commercial, transition, house rent, business, electricity, structure relocation, household dislocation allowances and business moving assistance. For this purpose, an allowances disbursement committee (notification in **Annexure-9**) has been constituted at the office of LAC/DC under the chairmanship of ADC along with Deputy Director Social & Resettlement and Assistant Resettlement Expert of PMC. The committee members keenly examine every single case with assistance of PIU staff in order to ascertain required information for considering any individual for a particular allowance. The LAC/PIU staff, after completing all the verifications out in the field, submit its report to the committee, and then the vouchers are accordingly signed. As soon as the committee completes its review and signs the cases, cheques are issued to the eligible DPs. The photographs of different activities are in **Annexure-13**.

3.4 Independent Valuation Study (IVS)

42. Valuation of affected land and non-land assets by an independent valuation expert: The ADB's Safeguard Policy Statement 2009 requires that the compensation provided to DPs should be based on full replacement costs. In order to determine if the compensation rates awarded by the LAC fulfill the requirement of replacement costs, PEDO/ PIU engaged an independent but accredited valuation expert to determine the value of affected assets considering the ADB's requirement of replacement costs and the international valuation standards. The valuation expert undertook a sample valuation study (IVS) during January-March 2023. The study determined a differential between the awarded compensation rates and the IVS rates. The IVS report and the differential has been reviewed and approved by the Provincial Cabinet of the Government of Khyber Pakhtunkhwa (GoKPK). Earlier, ADB also

reviewed the report and solicited clarifications from the expert on the valuation and the payment of differential to DPs through an addendum LARP.

43. A detailed virtual meeting and presentation including question and answer session was conducted by the IVS consultants regarding the IVS study findings and dissemination to all the GRCs members, DPs/ community members. The GRCs members and DPs/ community members expressed their satisfaction on the study findings and they requested PIU for early release of payment of differential of land compensation. The PD of BHP clarified to them that payment of differential will be paid through the Addendums of LARP-1 and 2 separately after approval of the same by ADB. The minutes of meeting/ presentation of IVS available at **Annexure-5**. The addendum of 1st sectional LARP has been submitted to ADB on June 13, 2024 for onward approval.

3.5 LARP's Addendum

44. The LARP's addendum under section-1 and 2 aims to document the additional/missing claims for eligible allowances and their validation/ verification based on the matrix of entitlements and criteria as per the approved LARPs, the additional compensation for the positive differential between the replacement cost determined by the IVS and the official rates in the approved LARPs and additional land (15.4 kanal) to be acquired at the dam site area in Mouza Bela Sacha under Section-2.

Table 3: Tentative Schedule for Implementation LARPs Addendum

S. No.	Actions	Tentative Ti	imeline/ Status	Posponsibility	
5. NO.	Actions	Timeline	Status	Responsibility	
1	LARPs addendum submitted to ADB	12 July 2024		PIU/ PMC	
2	LARPs addendum commented by ADB	22 July 2024		ADB	
3	 Replacement Cost of IVS for land deposited in District Treasury under LAC/ DC Mansehra. Transfer of fund for additional/ missing allowances of DPs deposited in District Treasury of District Mansehra. Transfer of fund for additional land of DPs deposited in District Treasury of District Mansehra. 	July 2024	PEDO will deposit replacement cost and funds for additional allowances and additional land in the treasury of district Mansehra.	PIU/ PEDO	
4	LARPs addendum submitted to ADB	31 July 2024		PIU/PEDO	
5	LARPs addendum reviewed and cleared by ADB.	10 August 2024		ADB	
6	Acquaintance Roll under LARPs addendum as per IVS cost prepared	August 2024		IVS/ DC/LAC and PIU	
7	Acquaintance Roll preparation for additional/ missing allowances under LARPs addendum.	September 2024		PIU/ PMC	
8	Compensation payment under IVS cost will be disbursed.	September 2024		DC/ LAC and PIU	
9	Payment of missing/additional allowances will be disbursed.	September 2024		DC/ LAC and PIU	
10	Issuance of notification under	August 2024		DC/ LAC District	

C No	Antiona	Tentative Ti	meline/ Status	Doononoihility		
S. No.	Actions	Timeline	Status	Responsibility		
	Section-5 of LAA for Additional Land in Mouza Bela Sacha.			Mansehra		
11	Issuance of notification under Section-6 of LAA for Additional Land in Mouza Bela Sacha.	September 2024		DC/ LAC District Mansehra		
12	Issuance of notification of land award under Section-9 & 10 of LAA for Additional Land in Mouza Bela Sacha.	October 2024		DC/ LAC District Mansehra		
13	Issuance of notification of land award under Section-11 of LAA for Additional Land in Mouza Bela Sacha.	November 2024		DC/ LAC District Mansehra		
14	Acquaintance Roll preparation for additional land under Section-2 LARP addendum.	November 2024		DC/ LAC and PIU		
15	Compensation payment under additional land Section-2 LARP addendum.	November 2024		DC/ LAC and PIU		
16	Internal Monitoring Report prepared and submitted to ADB	December 2024		PIU/ PMC		
17	External Monitoring Report prepared and submitted to ADB	January 2025		EMA/ ERM		
18	IMR and EMR report on completion of payment of compensation and allowances as per addendum reviewed by ADB	January 2025		ADB		
19	No-objection for clearing of all sites issued by ADB	One week after clearing the EMR		ADB		

4 LARP IMPLEMENTATION PROGRESS REVIEW

4.1 LARP Implementation Progress in reporting period

As per approved LARPs, the compensation and admissible allowances for land and above land assets awarded under LAA 1894 was deposited in the district treasury at the disposal of LAC assigned by the Land Revenue Department in the District Mansehra for completing land acquisition process and disbursement of awarded compensation and allowances. Disbursement of land and non-land compensation awarded under the law commenced on August 2, 2022 for 1st sectional LARP, and on August 23, 2022 for 2nd sectional LARP by the LAC in the district revenue department. Similarly, all the admissible allowances mentioned below were also paid by LAC/PIU supported by PMC. The field staff of PIU and PMC thoroughly supported the revenue department staff to expedite the disbursement of compensation and allowances to the DPs. As per procedure, DPs visited the ADC Mansehra revenue office to receive compensation. The concerned Tehsildar prepared voucher for the DPs for all their due compensation for affected land and non-land assets from the respective acquaintance rolls. The same voucher was forwarded to the DC office for signing and approval. After signing, the voucher was handed over to the DPs for submission in the district account office. The district account office then prepared a cheque on account of respective DPs. Similarly, DPs then directly submitted their cheques in their respective bank accounts for

onward clearance/receiving the desired amount. Payment voucher in **Annexure-3**. The field data of the unpaid DPs of all mouzas under sections-1 and 2 are collected by PIU/PMC field staff and prepared all the requisite legal and administrative impediments of unpaid DPs.

4.2 Section and Mouza wise LARP's Implementation and Handing over of Sites

- 46. The PIU, in consultation with ADB project team, adopted section and mouza wise LARP implementation approach to facilitate handing over of sections/mouza for construction where implementation of LARP is completed and validated by the External Monitor in parallel with implementation of LARP in other sections/mouza. Accordingly, resources were focused to complete disbursement of compensation and document all unpaid DPs having impediments to confirm implementation of LARP. All four mouzas under sections-1 and 2 have been cleared and handed over to the contractor on validation of EMA. Under 1st sectional LARP, the 1st and 2nd EMRs for mouza Ghanool and Sangar (separately) were approved by ADB on December 23, 2022 and December 27, 2022 respectively. Under 2nd sectional LARP, the 3rd EMR for mouza Bela Sacha and Paras was approved by ADB on March 7, 2023. The latest EMR for July to December 2023 was approved by ADB on March 22, 2024.
- 47. The PIU and PMC staff during reporting period (January-June 2024), continued exhaustive efforts through all sources to inform and mobilize all the unpaid DPs in the affected mouzas/villages to get their compensation and allowances for their acquired land and affected trees, and resolve their issues related to land or non-land. The overall detail of disbursement of compensation and allowances of each sectional LARPs during the reporting period are presented as under.

4.3 Overall Summary of LARP Implementation in all Sections and Mouzas

48. Under the land award of section-11 of LAA 1894, acquaintance roll (DPs land/ trees/ built-up property compensation payment book) has been prepared for the entire affected land and non-land assets of each mouzas separately under sections-1 & 2 by the LAC of land revenue department of district Mansehra. According to "land award", a total of 1811.35 kanal (226.419 acres) of land (including 492.72 kanal (61.59 acres) communal land. The revenue department of Mansehra District is working on the assessment/compilation of communal land DPs and once it is completed, then the detail will be incorporated in the upcoming report. As per approved LARP under section 1, total number of land DPs has changed from the original number (1,791 to 1,874 DPs) due to inheritance mutation. Similarly, owners of trees also increased from original number (1,773 to 1,862 DPs). Nonetheless, the amount of payable compensation remains unchanged. As per approved LARP under section 2, total number of land DPs has changed from the original number (1,766 to 1,821 DPs) due to inheritance mutation. Similarly, owners of trees also increased from original number (1,575 to 1,647 DPs). Nonetheless, the amount of payable compensation remains unchanged. All the "awarded amount" compensation of land, trees, built-up property and all the requisite amount for admissible allowances has been deposited in the district treasury department of District Mansehra by PEDO. The tables 4.1 and 4.2 indicate that during the reporting period from January-June 2024, PKR 329.34 million (58.01%) of total amount of land compensation payable PKR 567.69 million has been disbursed to 1,448 (39.19 %) out of total 3,695 DPs for acquired land of 950.14 kanal (118.77 acres) (52.45%) out of total 1,811.35 kanal (226.42 acres) in all four mouzas under sections-1 & 2. Similarly, 1,163 (33.14%) out of total 3,509 DPs of trees affected received PKR 67.96(83.07%) out of total PKR 81.81 million of trees compensation. However, total number of land DPs has changed from the original number (3,557 to 3,695 DPs) due to inheritance mutation. Similarly, owners of trees also increased from original number (3,348 to 3,509 DPs) in all four villages of BHPP. Nonetheless, the amount of payable compensation remains unchanged. Moreover, affected built-up property compensation paid to 438 DPs (100%) out of total 438 DPs with PKR 1395.838 (93.12%) out of total PKR 1498.999 million in entire affected mouzas of BHPP. Additionally, based on their income analysis/investigation there is no new DP eligible for vulnerability allowance among the additional DPs due to inheritance mutation. For comparative analysis, section and mouza wise summary of compensation, disbursement for LAR impacts (land, trees and built-up property), and progress of payments achieved during reporting period (January-June 2024) are presented in Table 4.1, Table 4.2, Table 4.3 and Table 4.4.

4.3.1 Disbursement of Trees Compensation

49. In the reporting period (January-June 2024), PKR 67.96 million of total PKR 81.81 million compensation amount of fruit and non-fruit trees has been disbursed to 1,163 of total 3,509 DPs (33.14%) in entire four mouzas of the Project. However, owners of trees increased from original number (3,182 to 3,338 DPs of timber trees) and (166 to 171 DPs of fruit trees) due to inheritance mutation. The slow progress of tree compensation amount disbursement is due to non-availability of the DPs to receive the tree compensation amount. The undisbursed compensation amount is secured in the district treasury account to ensure payment as and when the DPs will show up with valid claim documents after resolving their issues. The section and mouza wise detail of awarded fruit and non-fruit trees compensation amount, number of DPs, progress of disbursement and its percentage are presented in **Table** 4.3.

Table 4.1: Summary of Section wise LAR Impacts and Entitlement Categories of BHP Project

(Amount in PKR Million)

	T							_				_		Г	(Amo	unt in Pr	(R Million)
		Tot	al DPs and	l Payable Ar	nount		ess During (July- De				ress Durii s (Januar			Cu	Paid Unpaid DPs 795 1,079 653 1,168 1,448 2,247 788 1,074 40 0 375 1,272 398 0 1,601 2,346		
S. No.	Type of Compensation & Admissible Allowances	Payable Payment (Million)	Total DPs as per approved LARP	DPs of	Total DPs (Approved LARP + inheritance Mutation)	Paid Amount (Million)	Unpaid Amount (Million)		Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid
1	Land Compensation (Awarded)																
i.	Section-1	141.19	1,791	83	1,874	82.11	59.08	639	1235	10.55	48.53	156	1,079	92.66	48.53	795	1,079
ii.	Section-2	426.50	1,766	55	1,821	188.27	238.22	460	1361	48.41	189.82	193	1,168	236.68	189.82	653	1,168
Tota	al Land Compensation Amount	567.69	3,557	138	3,695	270.39	297.31	1,099	2,596	58.96	238.35	349	2,247	329.34	238.35	1,448	2,247
2	Non-Land Compensation																
2.1	Section-1																
i.	Trees Compensation	32.71	1,773	89	1,862	17.70	15.01	645	1217	5.93	9.07	143	1,074	23.63	9.07	788	1,074
ii.	Built-up Property	74.53	40	N. A	40	72.52	2.01	40	0	-	-	-	-	72.52	2.01	40	0
2.2	Section-2																
i.	Trees Compensation	49.10	1,575	72	1,647	32.24	16.86	223	1424	12.09	4.77	152	1,272	44.33	4.77	375	1,272
ii.	Built-up Property	1424.47	398	N. A	398	1323.32	101.20	398	0	-	-	-	-	1323.32	101.20	398	0
	al of Non-Land Compensation ount	1580.81	3,786	161	3,947	1445.78	135.08	1,306	2,641	18.02	13.84	295	2,346	1463.8	117.05	1,601	2,346
3	Other Admissible Allowances																
3.1	Section-1																
i.	Vulnerability Allowance																
ii.	Structure Relocation																
iii.	Shifting Allowance (For House)																
iv.	Transition Allowance	59.565							_			_					1
٧.	House Rent Allowance		39	N. A	39	59.376	0.189	36	3	0.126	0.063	2	1	59.502	0.063	38	
vi	Electricity Allowance																
vii.	Household Dislocation (Chula) Allowance																
viii.	Severe Impact Allowance																

		Tot	al DPs and	Payable An	nount	Progre Quarters	ess Durin				ogress During Current ters (January-June 2024)						
S. No.	Type of Compensation & Admissible Allowances	Payable Payment (Million)	Total DPs as per approved LARP	Additional DPs of inheritance Mutation	Total DPs (Approved LARP + inheritance Mutation)	Paid Amount (Million)	Unpaid Amount (Million)		Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)		Unpaid DPs	Paid Amount (Million)	Unpaid Amount (Million)	Paid DPs	Unpaid DPs
ix.	Shifting Allowance (Commercial Structure)																
Х.	Business Moving assistance																
xi.	Business Allowance for 12 Month																
3.2	Section-2																
i.	Vulnerability Allowance																
ii.	Structure Relocation				A 286	403.829	64.385	204		37.136	27.249			440.965	27.249	220	66
iii.	Shifting Allowance (For House)																
iv.	Transition Allowance											16	66				
٧.	House Rent Allowance								82								
vi	Electricity Allowance			N. A													
vii.	Household Dislocation (Chula) Allowance	468.214	286														
viii.	Severe Impact Allowance																
ix.	Shifting Allowance (Commercial Structure)										,						
х.	Business Moving assistance																
xi.	Business Allowance for 12 Month																
xii.	Loss of Temporary Employment																
& No	Grand Total of Section-1 & 2 (Land & Non-Land Compensation & Allowances Amount)		7,668	299	7,967	2179.37	496.92	2,645	5,322	114.242	279.502	662	4,660	2293.607 (85.7%)	382.712	3,307	4,660

Table 4.2: Mouza (village) and Gender wise Summary of Paid Land Compensation Amount and Paid DPs

(Amount in PKR)

					No. o	f DPs	of La	and						Paid DI	Ps and Paid L	and Compens	ation Amount	unouncili i ruty
Section	Mouza (Village)				Additional DPs of inheritance Mutation			Total No. of DPs as per Approved LARP + Inheritance Mutation)			Paid DPs (Approved LARP + Inheritance Mutation)		Paid Land Compensation Amount			Land Compensation Amount Payable	Percentage of Paic Land Compensation Amount	
Š	(Village)	Male	Female	Total	Male	Female	Total	Male	Female	Total	Male	Female	Total	Male	Female	Total		
1	Ghanool	63	63	126	23	13	36	86	76	162	59	39	98	1,369,742	594,325	1,964,067	2,763,901	71.06
	Sangar	909	756	1665	32	15	47	941	771	1,712	398	299	697	68,963,833	21,731,402	90,695,235	138,429,798	65.52
	Total of Section-1	972	819	1791	55	28	83	1027	847	1874	457	338	795	70,333,575	22,325,727	92,659,302	141,193,699	65.63
2	Bela Sacha	64	62	126	18	23	41	82	85	167	59	69	128	38,676,137	28,584,343	67,260,480	81,122,423	82.91
	Paras	800	840	1,640	14	0	14	814	840	1,654	264	261	525	96,810,683	72,604,424	169,415,107	345,376,105	49.05
	Total of Section-2	864	902	1766	32	23	55	896	925	1821	323	330	653	135,486,820	101,188,767	236,675,587	426,498,528	55.49
_	rand Total f Section-1 & 2	1,836	1,721	3,557	87	51	138	1,923	1,772	3,695	780	668	1448	205,820,395	123,514,494	329,334,889	567,692,227	58.01
	Amount in Million											205.82	123.51	329.33	567.692			

Table 4.3: Mouza (village) wise Summary of Paid DPs and Paid Compensation Amount of Trees

(Amount in PKR)

			No. of DPs of Trees Affected Paid No. of Trees Comp Amou			npensation	(2)		in PKR)	
Section	Mouza (Village)	Category of Trees	No. of DPs as Per Approved LARP Additional DPs of inheritance Mutation Total No. of DPs as pe Approved LARP + Inheritance Mutation)		Total No. of DPs as per Approved LARP + Inheritance Mutation)	No. of Paid DPs	Amount	Total Trees Compensation Amount Payable	Percentage of Disbursement	Total No. of Trees Affected
	Ghanool	Timber Tree	100	36	136	94	1,785,548	2,498,950	71.45	192
1	Congor	Fruit Trees	48	5	53	42	14,863,606	20,723,092	71.73	876
	Sangar	Timber Tree	1,625 48 1		1,673	652	6,981,724	9,483,590	73.62	2,853
	Total of	Fruit Trees	48	5	53	42	14,863,606	20,723,092	71.73	876
,	Section-1	Timber Tree	1,725	84	1,809	746	8,767,272	11,982,540	73.17	3,045
	Bela	Fruit Trees 13		Fruit Trees 13 0		12	8,734,388	9,114,061	95.83	319
	Sacha	Timber Tree	125	72	197	140	1,601,967	2,091,218	76.60	5,357
2	Paras	Fruit Trees	105	0	105	86	31,759,722	34,028,730	93.33	1,129
2	Palas	Timber Tree	1,332	0	1,332	137	2,230,235	3,865,438	57.70	3,832
	Total of	Fruit Trees	118	0	118	98	40,494,110	43,142,791	93.86	1,448
	Section-2	Timber Tree	1,457	72	1,529	277	3,832,202	5,956,656	64.33	9,189
	Total of	Fruit Trees	166	5	171	140	55,357,716	63,865,883	86.68	2,324
Se	ction-1 & 2	Timber Tree	3,182	156	3,338	1023	12,599,474	17,939,196	70.23	12,234
	Grand	Total	3,348	161	3,509	1163	67,957,190	81,805,079	83.07	14,558
		Am	ount in	Million		67.96	81.81			

4.3.2 Disbursement of Built-up Property Compensation

50. During the reporting period (January-June 2024), PKR 1,395.84 million of total PKR 1,498.99 million (93.12%) compensation amount of built-up property has been disbursed to 100% of total 438 DPs in entire mouzas of BHPP. All DPs of built-up property have been paid, and only communal and public built-up property amount is undisbursed. The undisbursed compensation amount of communal private and public built-up property is secured in the district treasury account to ensure payment as and when unpaid DPs/public department will show up with valid claim documents after completing the required documentation. As per LARPs, total of 197 graves (19 in mouza Sangar, and 178 graves in mouza Paras) are affected due to the project. The PIU has transferred all the requisite amount regarding graves management to the district treasury of district Mansehra. During the reporting period, under the DC Mansehra, already formed a committee for shifting of graves of the affected

communities, the contract has been awarded to the selected contractor for shifting of graves and the contractor working on the graves shifting from the Mouza of Sangar and soon will complete the process of shifting. Similarly, as per award notification under section-11 of LAA 1894 and physical verification by PIU and PMC, no other Masjid exists in the mouza of Sangar. The section and mouza wise category of built-up properties awarded compensation amount, number of DPs, progress of disbursement and its percentage are presented in Table 4.4.

Table 4.4: Mouza (village) wise Summary of Paid DPs and Paid Compensation amount of Built-up Property

(Amount in PKR)

on	(Village)	Built-up	Ту	Types & No. of Built-up Properties			otal DPs	DP: Buil	No. of s of t-up perty	Built-up Property	Total Built-up	ment tage	
Section	Mouza (V	Property Category	Residential	Commercial	Communal (Masjid)	Communal (Graveyard)	Public	Total I	No. of DPs	Percentage	Compensati on Paid to DPs	Property Compensation Payable	Disbursement Percentage
	gar	Private (Individual)	25	1	N. A	N. A	N. A	40	40	100	72,523,045	72,523,045	100
1	Sangar	Private (Communal)	N. A	N. A	1	N. A	N. A	N. A	N. A	N. A	N. A	2,009,972	0
2	Bela Sacha	Private (Individual)	29	3	N. A	N. A	N. A	32	32	100	184,291,938	184,291,938	100
_	S	Private (Individual)	366	12	N. A	N. A	N. A	366	366	100	1,139,022,72 3	1,139,022,723	100
	Paras	Private (Communal)	N. A	N. A	2	2	N. A	N. A	N. A	N. A	N. A	101,151,625	0
		Public	N. A	N. A	N. A	N. A	5	N. A	N. A	N. A	N. A		
Tot	al of	Private (Individual)	420	16	0	0	0	438	438	100	1,395,837,70 6	1,395,837,706	100
	tion & 2	Private (Communal)	0	0	3	2	0	0	0	0	0	103,161,597	0
		Public	0	0	0	0	5	0	0	0	0		
	Gra	and Total	420	16	3	2	5	438	438	100	1,395,837,706	1,498,999,303	93.12
			Α	mount	in Milli	on					1395.838	1498.999	

4.3.2.1 Restoration of Built-up Property

51. According to the DPs of affected built-up property, they will restore/reconstruct by their own choice or in another parcel of their own land through the received compensation amount along with other admissible allowances of their affected structures, and also reuse the affected structure salvaged building materials. Furthermore, the project has impact on the built-up properties (public and community structures). However, the negotiation of PIU continued with the respective government departments and district administration of Mansehra and local community for the relocation of the structures.

4.3.3 Pending Payment of Land Compensation

52. The findings of the LARP SASMR (internal) revealed that left-over land payments are impeded due to the following legal and administrative impediments. The required additional documents are recorded following templates provided in the ADB's guidance note on handling of compensation cases having legal and administrative impediments in **Annexure-1**. The staff

of PIU/PMC also continue to inform the unpaid DPs through their relatives and Patwaris to come forward and receive their compensation soonest. These efforts of PIU and PMC are in accordance with ADB's guidance note. In the previous reporting period (July-December 2023), total of 2,596 unpaid DPs of land compensation were pended/impeded, while during the current reporting quarter (January-June 2024), the unpaid number of DPs decreased to 2,247 of land compensation are impeded due to various reasons. The undisbursed compensation amount for acquired land and non-land is already deposited and secured in district treasury for payment to the unpaid DPs having legal/administrative impediments as and when they will show up with valid claim documents after resolving their issues/impediments. The additional documents were recorded for unpaid DPs having impediments in all four mouzas of the project. Sample copies of impeded cases are in **Annexure-2**.

- Stay order by civil court: The landowners/DPs (45 DPs having PKR 7.02 million amounts identified so far) filed their reference and title disputes in the courts which have not been resolved. The compensation amount could not be paid to them until land compensation and title issues are resolved/decided by the competent revenue authorities/courts. Summary of unpaid litigating number of DPs in each mouza under sections-1 and 2 is presented in Table 4.5.
- DPs working abroad: As per LAA 1894, DPs have to submit their claims supported with valid title documents, and receive compensation voucher/cheque in person after due verification of their documents and records. The staff of PIU regularly contacted their relatives to advise the DPs to get the compensation, or issue a valid power of attorney to collect the awarded compensation amount on behalf of the unpaid DP. Currently, a total of 65 DPs (no co-owner existed) having land compensation amount PKR 10.10 million are identified as working abroad. These DPs will be paid either if they show up personally or provide a valid power of attorney. The unpaid number of DPs of each affected mouza living/working abroad is in **Table** 4.5.
- Inheritance mutation issues: The landowners (266 DPs amounting PKR 35.27 million so far identified) who passed away require mutation of land to the legal heirs. Payments of compensation to legal heirs will be made after mutation of land is affected by the district revenue authority. For this purpose, PIU staff thoroughly support the revenue staff and mobilize known legal heirs to speed up the mutation process for DPs. After the inheritance mutation is reflected in the land record, all heirs of deceased DPs will receive entitled compensation as per their inherited share. However, the cases of DPs with pending mutations have been documented for all mouzas of project following ADB's guidance note on handling compensation cases with legal and administrative impediments in Annexure-1. The number of DPs with inheritance mutation in each mouza is presented in Table 4.5.
- Awarded meager⁷ compensation amount: A total of 1,118 unpaid DPs are entitled to awarded compensation amount less than PKR 5,000. Total sum of meager compensation amount is PKR 1.44 million that have not yet been disbursed because DPs are not inclined to get valid title documents and submit claims. As procedural

4-20

⁷ Compensation amounts up to PKR 5000 is defined as meager amount. It is likely that most of the DPs in this category may lack interest in claiming compensation following prevalent payment mode under LAA 1894.

requirement, DPs have to get the land title documents from land record office, open bank accounts, and appear in person before the LAC and District Accounts Office for verification and to receive compensation vouchers and cheques. No mechanism is available to make cash compensation to DPs in the revenue department/LAC at district Mansehra. Due to cumbersome procedural requirements for receiving such a small amount of compensation, DPs are reluctant to open bank accounts as the amount required for opening a bank account is much more than the entitled compensation amount. The unpaid meager compensation amount of land, and total number of unpaid DPs of meager amount of each mouza is in **Table** 4.5.

- Juvenile DPs (under the age of 18): Currently, a total of 4 DPs having compensation amount PKR 7,429 are juvenile and lack CNIC in all mouzas of the project. Such juvenile DPs can be paid either through their guardian, provided guardianship certificate issued by a competent court is produced or when the juvenile DP gets his CNIC after turning 18 years old. Accordingly, statements of natural guardians will be documented in accordance with the template in ADB's guidance note. The unpaid juvenile DPs of each mouza is presented in Table 4.5.
- DPs having communal land: As per revenue record and LAR implementation, 492.72 kanal of communal land amounting to PKR 67.45 million are unpaid due to communal/joint compensation amount, and not viable to disburse among all the DPs. Under the record of revenue department, the total DPs are not yet identified, and the disbursement of compensation is possible when the exact number of DPs under this category is identified/communicated by the revenue department. Hence, it will take time to disburse as and when all the DPs are identified and are available to receive their due compensation amount from the revenue department. Additionally, the revenue department is working on the separate acquaintance roll for such DPs against communal land, which is not yet finalized. Also, the DPs of communal land having some internal family dispute filed reference/stay order from the civil court against each other. The timeline depends upon the availability of DPs, and resolving their internal family dispute.
- DPs out of city: As per available revenue record, 317 DPs identified having land compensation amounting to PKR 83.38 million have migrated/out of city in Pakistan for better work opportunities. Even though they all were informed by their relatives to collect their due compensation amount, they are neither showing up in person nor nominating attorneys to collect compensation on their behalf. Out of city unpaid DPs are documented, and their records are maintained as per ADB's guidance note. A summary of all mouzas are in Table 4.5.
- **DPs out of village:** As per revenue record, 432 DPs identified having land compensation amounting to PKR 33.68 million in all affected mouzas of the project, were unknown by their respective mouza inhabitants and revenue staff. Their whereabouts are also unknown. So, these DPs and their current residences are not known. The out of village unpaid DPs of all four mouzas are presented in **Table** 4.5.

Table 4.5: Mouza (village) wise Summary of Impediments causing delay in Payment of Land Compensation

(Amount in PKR)

	(6		y Or		DPs	s out	of		DP erita			Ps wi			DPs veni	le	unal	פ	DPs	s out	of	DPs	Out	nou t o f			
ion	Village		y Civ Cour			ount		u	utation inde oces	r		eage		(un	der t	the	Communal	Land		City			illag		DPs U	Land F	aid Amo
Section	Mouzas (Villages)	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	No. of DPs	Land Parcel	Amount	Total No. of DPs Unpaid	Total un-paid Land Parcel	Total Unpaid Amount
	Ghanool	1	1	222,018	5	5	98,174	13	13	276,905	27	27	38,169	4	4	7,429	0.95	14,755	N.A	N.A	N.A	14	14	142,384	64	64	799,834
1	Sangar	8	8	5,586,587	39	39	2,516,686	155	155	10,284,382	508	508	878,928	N.A	A.N	A.N	167.25	16,282,145	135	135	1,262,370	170	170	10,923,465	1,015	1015	47,734,563
_	tal of ction- 1	9	9	5,808,605	44	44	2,614,860	168	168	10,561,287	535	535	917,097	4	4	7,429	168	16,296,900	135	135	1,262,370	184	184	11,065,849	1,079	1079	48,534,397
	Bela Sacha	N.A	N.A	N.A	10	10	2,753,281	6	6	5,972,372	2	2	4,668	A.N	A.A	A.N	24.33	130,480	8	8	2,296,974	10	10	2,704,168	39	39	13,861,943
2	Paras	36	36	1,207,852	11	11	4,735,000	89	89	18,739,649	581	581	525,219	N.A	N.A	N.A	300.19	51,027,070	174	174	79,817,086	238	238	19,909,121	1129	1129	175,960,997
	tal of ction- 2	36	36	1,207,852	21	21	7,488,281	86	86	24,712,021	583	583	529,887	A.A	A.A	N.A	324.52	51,157,550	182	182	82,114,060	248	248	22,613,289	1,168	1,168	189,822,940
To:	and al of tion- & 2	45	45	7,016,457	65	65	10,103,141	266	266	35,273,308	1118	1118	1,446,984	4	4	7,429	492.52	67,454,450	317	317	83,376,430	432	432	33,679,138	2,247	2,247	238,357,337

4.3.4 Payment of Allowances by LAC/ PIU

53. During the reporting period (January-June 2024), all the admissible allowances have been mostly paid to the entitled DPs of all four mouzas. As per approved LARPs, 258 of total 325 DPs have been paid for their 1,595 of total 1,706 admissible allowances, totaling PKR 500.467 million of total PKR 527.779 million (94.83%). The 66 DPs having 111 unpaid number of allowances amounting to PKR 27.31 million are unpaid due to out of village. They were already informed through their relatives and neighbors, and soon will receive their due allowances. All the admissible allowances for entitled DPs are already deposited and secured in the district treasury for payment to the DPs. Similarly, as per approved LARPs and LAR implementation, no other DPs are eligible in the remaining unpaid DPs of land compensation

for any sort of allowance in all affected mouzas. A sample copy of payment receipt of allowances in **Annexure-3**. All the admissible number of allowances, number of entitled DPs, payable allowances, and progress of disbursement of allowances and its percentage is presented in **Table 4.6**.

Table 4.6: Section and Mouza wise No. of DPs and Allowances and Progress of Disbursement of each Allowances

(Amount in PKR)

														Progres	s of	Disbu	seme	nt of	Allo	wances								AIIIOUIII III	1 100
				/ouz	a /Vill	lage) Gha	anool		Section	on-1	N/	louza	(Village) Saı	ngar				Монг	// cv	llage) Bela	Sacha		Sec	tion-2		Mou	za (Village) Par	96	
		No. of Entitled DPs &	No. of Admissible Allowances	Pa	id No	o. of DPs,	Paid No. Payment		No. of Entitled DPs &	<u></u>		No. of	f DPs, Paid N and Payment Allowand	lo. of Allowa of each	nces	No. of Entitled DPs &			Paid	No. of DPs,	Paid No. of syment of eac	: h	No. of Entitled DPs &	No. of Admissible Allowances	Pai		of DPs, Paid No Payment o Allowand	. of Allowance f each	es and
S. No.	Admissible Allowances	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage
1	Vulnerability Allowance	3	3	3	3	189,000	189,000	100		15		14	882,000	945,000	93		9		8	504,000	567,000	89		42		33	2,079,000	2,646,000	78.57
2	Structure Relocation									27		27	837,000	837,000			5		2	62,000	155,000	40		185		181	5,611,000	5,735,000	97.84
3	Shifting Allowance (For House)									27		27	837,000	837,000			5		2	62,000	155,000	40		185		181	5,611,000	5,735,000	97.84
4	Transition Allowance									25		25	1,425,000	1,425,000			5		2	114,000	285,000	40		185		181	10,317,000	10,545,000	97.84
5	House Rent Allowance								36	25	35	25	2,500,000	2,500,000		24	5	10	2	200,000	500,000	40	218	185	192	181	18,100,000	18,500,000	97.84
6	Electricity Allowance	Z A	N. A	A.	Σ. A	∢ Ż	∢ Ż	Z Z		25	00	25	500,000	500,000	100		5		2	40,000	100,000	40	210	185	102	181	3,620,000	3,700,000	97.84
7	Household Dislocation (Chula) Allowance									25		25	50,000,000	50,000,000			5		2	4,000,000	10,000,000	40		191		185	370,000,000	382,000,000	96.86
8	Severe Impact Allowance									26		26	1,638,000	1,638,000			7		2	126,000	441,000	29		212		199	12,537,000	13,356,000	93.87
9	Shifting Allowance									1		1	31,000	31,000			3	0	0	0	93,000	0		12		11	341,000	372,000	91.7

														Progres	ss of	Disbu	seme	nt of	Allo	wances									
								S	Section	on-1				-									Sec	tion-2					
			N	/louz	a (Vil	lage) Gha	anool					/louza	ı (Village) Saı	ngar				Mouz	a (Vi	llage)Bela S	Sacha					Mou	za (Village) Par	as	
		No. of Entitled DPs &	No. of Admissible Allowances		lowai			of t of	No. of Entitled DPs &	of Admissible Illowances	Paid		f DPs, Paid N and Payment Allowand	of each	nces	No. of Entitled DPs &	Allowances			No. of DPs, nces and Pa Allowand	yment of eac	h	No. of Entitled DPs &	No. of Admissible Allowances	Paid	d No. d	of DPs, Paid No Payment o Allowand	f each	es and
S. No.	Admissible Allowances	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage	Total DPs	Total No. of Admissible Allowances	Paid DPs	Paid No. of Allowances	Paid Allowances Amount	Total Payable Amount of Allowance	Payment Percentage
	(Commercial Structure)																												
10	Business Moving assistance									1		1	63,000	63,000			3	0	0	0	189,000	0		12		11	693,000	756,000	91.7
11	Business Allowance for 12 Month									1		1	600,000	600,000			3	0	0	0	1,560,000	0		12		11	4,680,000	5,280,000	88.6
12	Loss of Temporary Employment								N. A	A A	۲ ۲	۲ ۲	Z A	Υ Ż	۲ ۲	8	8	2	2	252,000	1,008,000	25	36	36	16	16	2,016,000	4,536,000	44.4
	Total	3	3	3	3	189,000	189,000	100	36	198	35	197	59,313,000	59,376,000	99.9	32	63	12	24	5,360,000	15,053,000	36	254	1,442	208	1371	435,605,000	453,161,000	96.13

4.3.5 Section and Mouza (village) wise Hydropower Component and Cleared Acquired Land of BHPP

54. The PIU is committed to complete the implementation process of LARPs in the entire project. Based on the approved LARPs' implementation progress in the reporting period, the PIU confirms that all payable DPs have been fully paid as per LARP provisions, and there is no unpaid DP left without valid legal and administrative impediments. The undisbursed compensation amount for acquired land is already deposited and secured in the district treasury. Payment will be made to the unpaid DPs (60.81%) having legal/administrative impediments as and when they will show up with valid claim documents after resolving their issues/impediments. The mouzas (villages) under sections-1 & 2 presented in gray, green and blue colors have been handed over to the contractor upon the EMA's validation of LARP implementation in 1st (December 23, 2022)8, 2nd (December 27, 2022)9 and 3nd (March 7, 2023)10 EMRs approved by ADB. Additionally, the IVS report approved by ADB and Provincial Government and LARP implementation in terms of compensation payment will run simultaneously towards the commencement of civil works and full implementation of LARP. The LARP implementation status is presented at a glance in **Table 4**.7.

Table 4.7: Section and Mouza-wise Clearance of LARP Implementation under BHPP

Section	Mouza (Village)	Component of BHPP	UTM Coordinates	Total Acquired Land in Kanal/ (Acre)	1 st Clearance by EMA (December 23, 2022)	2 nd Clearance by ERM (December 27, 2022)	EMA (N	rance by larch 7, 23)
	Ghanool	Surge Shaft and access road to Surge Shaft	E 351684.82 N 3830355.72	30.95/ (3.87)	30.95 / (3.87)			
1	Sangar	Access Tunnel to Cavern Powerhouse, access roads, tailrace, staff colony and switch yard	E 3503113.03 N 3828607.92	817.45 / (102.18125)		817.45 / (102.18125)		
2	Bela Sacha	Dam Right Side Abutment, Reservoir, Diversion/ Sediment By-Pass Tunnel and Access Road to Diversion/ Sediment By-Pass Tunnel	E 357872.122 N 3836447.78	175.575 / (21.947)			175.575 / (21.947)	
	Paras	Dam Left Side Abutment, Reservoir, Intake of Headrace Tunnel and Access Road to Dam Crest	E 359038.92 N 3836812.05	787.375 / (98.422)				787.375 / (98.422)
		Total		1811.35 / (226.42)	30.95 / (3.87)	817.45 / (102.18125)	175.575 / (21.947)	787.375 / (98.422)
Legen d:		Mouzas under section-1 in grey of LARP implementation provid Mouzas under section-1 in gree of LARP implementation provid Mouzas under section-2 in blue of LARP implementation provid	led in 1 st EMR. en color which ha led in 2 nd EMR. e color which had	d been cleared a	and allowed for c	onstruction base	ed on EMA's	validation

55. Furthermore, the PIU confirms that unpaid compensation is secured in the district treasury, and unpaid DPs having legal/administrative impediments have been fully informed about processing and payment of their claims as and when they show up. However, all exhaustive efforts on part of the PIU and PMC will be continued till the completion of LARP implementation. Therefore, the SASMR (internal) for January-June 2024 reports full

⁸ https://www.adb.org/projects/documents/pak-49055-007-smr-4

⁹ https://www.adb.org/projects/documents/pak-49055-007-smr-3

¹⁰ https://www.adb.org/projects/documents/pak-49055-007-smr-6

implementation of LARP¹¹ is confirmed and validated by the EMA through his 1st, 2nd, 3rd and 4th EMRs in entire BHPP (except for gap filing measures identified by IVS, if any).

-

¹¹ Full implementation of LARP construe that the all payable DPs have been fully compensated, and payment of any differential amount assessed by IVS and unpaid DPs having impediments are approached and documented. The pending compensation costs are secured in the district treasury to ensure unpaid DPs having impediments are paid their entitled compensation as and when they approach after resolving their issues.

5 LARP IMPLEMENTATION MONITORING SET-UP

5.1 LARP Implementation Monitoring

- 57. Implementation and monitoring of LARP consistent with the project loan covenants and ADB's SPS 2009 are the key requirement to hand over the sites to the contractor and proceed with physical works. Therefore, for smooth and efficient implementation of LARPs, safeguards management is set up at the PIU, as the focal unit for LARP implementation, to (i) maintain updated LARP data about DPs with respect to compensation, entitlements and payment record; (ii) facilitate consultations with stakeholders, including DPs, project executors, and district land revenue authorities; (iii) track and monitor day-to-day implementation progress, and prepare periodic monitoring reports; and (iv) maintain a log of complaints received and redressed, and facilitate project GRCs to review and resolve the complaints.
- 58. Similarly, LARP implementation is also monitored externally through an EMA by PIU. The objective of resettlement monitoring is to validate implementation of LARPs, payment of compensation to DPs, and livelihood restoration support; and ensure safeguards monitoring compliance during implementation as per ADB's SPS 2009.

5.2 Exhaustive Efforts

- 59. Since the start of LARP implementation on August 2, 2022, the PIU of BHPP, through its safeguard's management set-up, is closely coordinating with the LAC and district land revenue offices to facilitate timely completion of land acquisition, processing and payment of compensation to the DPs, and ensure full implementation of LARPs before handing over of the sites to the contractor. Meanwhile, the safeguards team, headed by the Deputy Director Social and Resettlement, maintained close liaison with the affected persons and local communities in the project-affected villages to disclose LARP-related information, and facilitate DPs in accessing requisite valid claim documents (i.e. getting their land title documents from land revenue offices and CNIC, opening bank accounts, and processing and payment of compensation). With coordinated efforts, the land and non-land compensation has reached to a reasonably good percentage in all the four mouzas of the BHPP by the LAC's office of District Mansehra.
- 60. No doubt, LARP implementation is a long, time-consuming and challenging process, yet all possible exhaustive efforts to expedite the process has been taken by the concerned project staff. Based on the compensation payment progress explained in previous sections, it is perceived and confirmed that all payable DPs have been compensated for their acquired land and assets. The remaining unpaid DPs are those who have valid legal/administrative impediments. All such DPs have been approached and informed that the compensation amount has been secured in the district treasury account for payment to them as and when they will show up with valid claim documents after resolving their issues. The PIU and PMC staff monitor the progress of paid and unpaid DPs as mentioned in the respective acquaintance roll at the revenue department, and collect and use the data for monitoring purposes for each affected area. In addition, following ADB's guidance note on handling compensation cases with legal and administrative impediments in **Annexure-1**, all accessible DPs were approached and additional documents as needed have been recorded and

maintained during the monitoring period by the safeguards team of PIU and PMC. The efforts by the PIU safeguards team for information dissemination and ensuring participation of affected communities and in line government departments for smooth implementation of LARPs are summarized in the sub-sections below.

5.3 Community Consultations/Meetings

- 61. To expedite the LARP implementation process, PIU staff, including Deputy Director Social and Resettlement, Deputy Director Health, Safety, Environment and Gender, and Assistant Director Social and Resettlement, along with PMC staff regularly conducted consultation meetings (photographs annexed) with male and female DPs of each affected mouza of the project. During the reporting period, 28 meetings have been conducted, in which 202 male and 117 female DPs raised all their queries/concerns regarding compensation and allowances for their affected assets. Accordingly, they were all informed to receive their due compensation and allowance amount from the revenue department. Similarly, there was wide publicity through print and electronic media, announcements in local mosques (masjids), banners, and LARP information brochures distributed among the meeting participants as well as in the affected mouzas of the project.
- 62. **Table** 5.1 shows the number of meetings along with participants in each section/mouza under BHPP.

Table 5.1: Summary of Community Consultation Meetings with DPs (January-June 2024)

Continu	Moure (Villege)	No of Mostings	No. of	DPs	Total
Section	Mouza (Village)	No. or weetings	Men	Women	Participants
4	Ghanool	3	29	11	40
'	Sangar	9	65	27	92
0	Bela Sacha	4	19	14	33
2	Paras	12	89	65	154
	Total	28	202	117	319

63. The DPs' issues, concerns and the PIU/PMC's responses are in Table 5.2. Attendance sheets and consultation activity reports are in **Annexure-4**.

Table 5.2: Issues/ Concerns of DPs and Response from the project team

S. No.	Summary of Issues/ Concern	Response from the PIU/PMC
1.	Most DPs ask about the compensation amount for land, timber trees, and built-up properties as they were not agreed with DC rates. They demanded to increase at the maximum level of affected assets.	The PIU/PMC responded to each query of the DPs, and clearly communicated that they accepted the DC rates, and DPs received due compensation amount at this stage. An IVS consultant conducted assessment and approved their report by ADB, and soon will prepare the acquainatance roll by IVS/ DC office and fill the gaps (if any) in land and non-land assets compensation will be paid.
2.	Most of the DPs enquired about the employment opportunities and small contracts for locals during construction phase.	PIU/PMC replied that during construction phase all affected DPs on need basis and according to their skills level, will be employed for short/long term in the project. DPs will even develop their own capacity through the skills development program as and when established at site.

S. No.	Summary of Issues/ Concern	Response from the PIU/PMC
3.	Issue related to inheritance mutation process causing delay in paying compensation retravel.	The PIU/PMC regularly coordinated with, and requested the revenue department officials to facilitate with DPs for recording and speeding up the inheritance mutation process. However, the legal heirs of the DPs will have to submit a request for mutation, and follow the procedures under the law. The compensation payment could only be paid when legal heirs of deceased DPs can submit their claims with valid titles after inheritance mutations of land. All of the inheritance mutation cases in mouzas have been recorded according to the SPS guidance note of ADB.
4.	DPs residing out of city, out of village, and working abroad.	Most of the unpaid DPs in affected mouzas are residing out of city, and some are working abroad. All such DPs' addresses and contact numbers (if available) are gathered through village headmen/notable (malik/patwari) persons and their relatives in the mouza. But in some cases, the local community lacks address and contact numbers of those DPs who migrated a long time ago. All those DPs have been documented through the malik/patwari in all mouzas of project.

5.4 Coordination Meetings with District Revenue Officials

64. The DC Mansehra office has been regularly contacted during the reporting period for the required information and documentation. These include the disbursement of land and non-land compensation; payment of meager compensation amount; and all other issues related to DPs, including inheritance mutation, and IVS positive differtial compensation, Additional land acquisition, shifting of graves and other public structures and all admissible allowances payment. A summary of meetings conducted with DC Mansehra and other district administration officials is given in Table 5.3 below.

Table 5.3: Summary of Coordination Meetings with District Administration

Purpose/ Issues Discussed	Outcomes/Agreed Actions
DC Mansehra (5 meetings)	
 Speed up the disbursement of all types of compensation to DPs of all mouzas. Disburse all sorts of admissible allowances in all affected mouzas to the eligible DPs as soon as possible. Facilitate and support pending court cases of DPs. Speed up the process of signing vouchers already prepared/referred by ADC/Tesildar concerned. Discuss all the issues faced by DPs during disbursement of compensation, and suggest to resolve them on priority basis. Expedite the unpaid non-land assets compensation, i.e., trees and public structures as soon as possible. Shifting of graves in the affected villages on priority basis. Shifting public structures on reasonable location. To accelerate the process of additional land in mouza Bela Sacha. Discussion on the preparation of acquaintance roll under the IVS positive differential cost for each mouzas. 	 staff/concerned Tehsildar to expedite the process of voucher preparation for all sorts of DPs' compensation and allowances. Rectified the names of any DPs as mentioned in acquaintance roll on priority basis. Facilitate and support the DPs at the time of voucher preparation regarding their affected land and non-land assets and khasra number as per the acquaintance roll. The process of graves shafting has been initiated in Mouza of Sangar. Under Section-4 of LAA 1894 has been notified and issued for additional land. Completed the formation of graveyard committee, and directed the committee

Purpose/ Issues Discussed Outcomes/Agreed Actions ADC/Tehsildars/Focal Person of Tehsil Balakot District Mansehra (8 meetings)

- Discuss and issue public notices in local newspapers for untraceable DPs, and fixed public notices in villages and advertised contact details of officials to whom the DPs can contact for payments.
- Expedite unpaid non-land assets compensation, i.e. trees and public structures as soon as possible.
- Disburse the meager amount to all the unpaid DPs in each mouza.
- Install banners on various prominent locations at tehsil and district levels.
- Provide regular support by PIU/PMC to the revenue department in preparing vouchers and other documentation for DPs.
- Support and guide women and vulnerable DPs in open bank accounts.
- Identified land with the Consensus of community for graves shifting.

- Regularly supported the revenue staff by PIU/PMC which directly facilitated all DPs in terms of voucher preparation and requisite stationary for documentation.
- Banners have been placed in prominent locations accordingly.
- PIU staff supported the DPs in opening of bank accounts for receiving compensation.
- Land has been identified and acquired for graves shifting.

5.5 Dissemination of LARP related Information¹²

65. In order to expedite the LARP implementation process, PIU, supported by PMC, disseminated LARP-related information to all concerned DPs which included but not limited to installation of 8 banners in public offices, such as AC/Tehsildar's offices and service delivery center in Balakot and other public places like Masjids and Jamia Masjids of affected mouzas in the project area. During the exhaustive efforts, the PIU produced information related to LARP implementation through print media i.e. local and national newspapers for public awareness to receive their compensation. Various posters and flip charts have been displayed showing salient features of BHPP. The safeguards team of PIU and PMC disseminated the LARP information brochure through community consultation meetings, and interaction with DPs at revenue department and other prominent places in each mouza. Awareness among the DPs regarding LARPs has been created through social media link available in **Annexure-7**. The PIU staff along with the revenue department staff are frequently visiting the mouzas under sections-1 and 2 for the purpose of disbursements of compensation and allowances.

-

¹² https://pedokp.gov.pk/Main/news/294/ok

6 PROJECT IMPACT ON WOMEN MOBILITY AND PRIVACY

- During LAR implementation stage in the reporting period, there is no major impact 66. recorded regarding women mobility and privacy in the project area due to project activities. The major activity is the information dissemination and facilitation by PIU/PMC social safeguard team to disseminate the LARP information among the affected households and communities in the affected mouzas of the project. They were also informed regarding opening bank accounts, and preparing valid CNIC for receiving compensation amount smoothly against their affected land and non-land assets. The PIU, Deputy Director Health, Safety, Environment and Gender, and Assistant Director Social and Resettlement, along with PMC staff, regularly conducted the consultation meetings with female DPs of affected mouzas of the project. During the reporting period, multiple meetings have been conducted with 117 female DPs to address all their queries/concerns regarding compensation and allowances of their affected assets. The women were also informed of their male household members to receive due compensation amount from the revenue department. The gender action plan (GAP) is being implemented in accordance with its terms under each output in the project's design and monitoring framework. Under the LARP's implementation, the compensation and allowances have been provided to the eligible female DPs. The other outputs of GAP are linked with LRP implementation through the consultant NGO. All such activities of GAP will be implemented during implementation of LRP by the consultant NGO. The consultant NGO has been mobilized since September 7, 2023 in the project area.
- Ouring the reporting period, there is no major impact recorded regarding gender issues, particularly regarding women in disbursing compensation and allowances. The LARP also identified the female DPs in terms of the loss of their assets. Like the male DPs, the women are also receiving their payments. The PIU and PMC are thoroughly facilitating in resolving issues related to compensation/allowances payment at the district revenue office. The field staff are regularly conducting consultation meetings with the female DPs to keep them updated about the project and their compensation payments, and addressing any issues during disbursement. Attendance sheets of the consultations are attached in **Annexure-4**.

7 LIVELIHOOD SUPPORT INTERVENTION MEASURE

7.1 Employment Opportunities

- 68. Under output 4 of the project's design and monitoring framework: income-earning opportunities and skills for local communities increased, relevant training facilitation support under the LRP through the consultant NGO will be provided to the DPs. Training on agriculture production, livestock rearing, beekeeping, fish farming, and linkages with microfinance institutions will be provided as per the local requirements, particularly for unemployed youth, both men and women, for relevant skills improvement/capacity building to reduce impacts on their livelihood. The consultant NGO has been mobilized since September 7, 2023 in the affected project areas. The consultant NGO will conduct another round of consultations and livelihood assessment to upgrade the draft LRP into an implementation-ready level, and implement the LRP.
- 69. Furthermore, as per draft LRP, it is planned that a livelihood skills development center for women will be established to cater short and long-term employment opportunities to the local affected person/DPs. The center will be established by the consultant NGO as per their approved terms of reference. The timeline for establishing the skills development center will be finalized by the NGO.

7.2 Short-Term Project-Based Employment

70. The LARP provided for employment of local laborers and members of DPs. PIU has been following up with the contractor and PMC in providing job opportunities to the locals. The information regarding employment opportunities were disseminated through consultation meetings with DPs, brochures, and through GRC members of each mouza. As per the contractor record, the contractor and consultants have employed a total of 932 persons for short-term employment (skilled and un-skilled labor), of which 595 (63.8%) are locals, including 337 DPs employed from the affected mouzas of the project. Hiring of skilled and unskilled labor from the project area is monitored by the PIU through the monthly progress reports of the contractor. The list of skilled and un-skilled employees is in **Annexure-12**. The summary of skilled and un-skilled laborers working in the project sites is in **Table** 7.1.

Table 7.1: Summary of Skilled and Un-Skilled Laborers

Contractors/ Consultants	Skilled Laborers	Un-Skilled Laborers	Total
Project Management Consultants/ PIU	2	0	2
The Contractors	201	392	593
Total	203	392	595

8 GRIEVANCE REDRESS MECHANISM AND COMPLAINTS HANDLING

71. The GRM aims to mediate conflicts, and respond to complaints related to environment and social safeguard (LARP) performance of the project. At the project level, the disbursement of compensation and allowance committee and GRCs disburse entitled allowances and redress grievances of affected communities. The field level GRCs were notified on September 15, 2022 for mouzas Ghanool and Sangar under section-1, mouza Bela Sacha (separately) under section-2 on September 26, 2022, and mouza Paras on January 12, 2023 with the following compositions. The GRC notifications are in **Annexure-10**.

•	Deputy Director Social & Resettlement	Chairman
•	Deputy Director Environment, Health, safety & Gender	Member and focal person
•	Resettlement Expert	Member
•	Patwari of Mouza Sangar	Member
•	Patwari of Mouza Ghanool	Member
•	Patwari of Mouza Bela Sacha	Member
•	Patwari of Mouza Paras	Member
•	Representative of Mouza Ghanool	Member
•	Two Representatives of Mouza Sangar	Member
•	Two Representative of Mouza Bela Sacha	Member
•	Three Representative of Mouza Paras	Member

- 72. A complaint register is maintained at site with the contractor as well as in the office of the Project Director (PIU). The placing of the complaint register at the contractor's camp is well publicized. Detailed GRM is affixed on the sign board installed at the Chief Engineer's office to guide complainants. The office of the Chief Engineer of the PMC is the first level to register and resolve the complaint if it is not addressed by the contractor. The Chief Engineer will deliver his decision within one week of registration of the case. If no understanding or amicable solution can be reached, or if the affected person does not receive a response from the Chief Engineer' offices within one week of the registry of the complaint, the affected person can appeal to the GRC in writing to the office of the Project Director PIU-BHPP. The GRC at the PIU level will address the complaint on priority, and is fully responsible to resolve the complaint.
- 73. **Applications/ Concerns of DPs Submitted to PIU:** As of reporting period of January-June 2024, total of 45 applications/ concern registered under GRC which were received by PIU from the affected communities, i.e., 2 applications regarding pending labour wages, 26 concern/ apprehension related to additional/missing monetary allowances, 10 applications related to internal family dispute on LARP's allowances, 1 concern regarding partial assessment of built-up property, 2 concern about demanding of business allowances, 3 applications regarding objection on the GRC members of village Paras GRC and 1 application related to damage of material mixture machine by local administration. Out of total, 43 applications/ concern have been resolved and only 2 pending applications/ concerns

unresolved due to non-availability of both parties for attending the grievance resolution meeting at GRC level. The summary of applications/ complaints tabulated under Table 8.1.

- 74. Complaints of DPs Submitted to ADB's Accountability Mechanism: Office of Special Facilitator (OSPF) and Compliance Review Panel (CRP): Before implementation of LARP-1, OSPF received one complaint in June 2022 from the village which was related to land acquisition, valuation and compensation. However, CRP received two complaints in January 2024 regarding missing business allowance from village Bela Sacha. Parallel commencement of LARPs implementation, PIU completed an IVS that determined a differential in the awarded prices and IVS rates. The IVS differential has been approved by the provincial government for additional payments to DPs through the addendum LARPs. Similarly, CRP complainant provided additional documents to support his claims of business allowance. Based on the documents provided by the concern DPs, PIU has accepted the claims for business allowance of 2 DPs as Annex-11 provides the complainant's satisfaction note on PIU accepting the claim of business allowance. The summary of applications/complaints tabulated under Table 8.1.
- 75. During field visits in all affected villages, PIU/PMC staff conducted additional consultations with members of GRCs on the issue of "Chullah allowance". The GRC of Mouza Paras initially submitted appliactions of 279 DPs for Chulla allowance, which after thorough scrutinization by PIU and PMC and clarifications, were reduced to only 124 cases by the demands of the GRC. Similarly, in Mouza Bela Sacha, DPs initially identified as 29 but came down to only 18 by the GRC, whereas in the Mouza of Sangar, the DPs are recorded as 10. After delibrate discussion/meetings with GRC members by PIU/ PMC and based on provided documentary proof, the finalized and agreed number of eligible DPs for Chulla Allowance from each village are completed i.e., the eligible number of DPs under missing Chulla allowances from village Paras are 45, from village Bela Sacha is 1 DP and from village Sangar is also 1 DP. However, remaining DPs are mostly eligible for one-time structure relocation (255 DPs) and business allowance (25 DPs) in all 4 villages. All such DPs along with their claims and provided documents are scrutinized in accordance with the criteria in approved LARPs under section-1 and 2. The detail information of the eligible DPs under missing allowances are available in the 1st and 2nd sectional LARP's addendum.

Table 8.1: Summary of Complaints Registered of BHPP

S.	Detail of	Catego Complainats		Resolved/	Remarks/ Outcome
No.	Grievances	PIU/GRM	ADB: OSPF/ CRP	being resolved	Remarks/ Outcome
1	Labor wages (Contractors)	2	1	2	The field staff of PIU and the contractors resolved the applicant's issues at site.
2	Partial assessment of affected built-up properties.	1	-	1	The applicant was satisfied and withdrew his application during a meeting conducted with the IVS consultant in affected village/mouza of the project.

S.	Detail of	Catego Complainats		Resolved/ being	Remarks/ Outcome
No.	Grievances	PIU/GRM	ADB: OSPF/ CRP	resolved	Remarks/ Outcome
3	Applications/ Concern for additional/ missing monetary allowances.	26	-	26	 All the 26 applicants regarding additional/ missing allowances have been satisfied through the provision of admissible allowances under approved LARP as per eligibility criteria provision. Additionally, the applicants/ GRC members also provided a statement of satisfaction certificate to PIU regarding resolution of their concerns.
4	Internal family disputes over LARP allowances.	10	-	10	With the intervention of PIU staff and through respective GRC members, all their concerns were amicably resolved.
5	Applications/ objection against GRC member of village Paras.	3		1	1 applicant has withdrawn his application while remaining 2 applications pending unresolved due to non-availability of both parties for attending the grievance resolution meeting at GRC level.
6	Applications/ complaints for missing Business allowances	2	OSPF 2 CRP 1 All ineligible	*3	 The only 2 complaints registered (in January 2024) with ADB's Compliance Review Panel regarding missing business allowance from village Bela Sacha. After deliberate discussion/ meetings with the complainants in accordance with ADB's guidelines, the PIU with the support of PMC, the complaints resolved amicably through submission of documentary proof for additional/missing allowances under the eligibility criteria which has been approved and resolved. Additionally, the applicants/ complainants also provided a statement of satisfaction certificate to PIU and consider the complaints resolved.

S.	Detail of	Catego Complainats	/Grievances	Resolved/ being	Remarks/ Outcome
No.	Grievances	PIU/GRM	ADB: OSPF/ CRP	resolved	Remarks/ Outcome
7	Damage of construction materials Mixture Machine	1	·	1	After thorough verification by the GRC members and PIU staff at site, there is no evidence identified regarding the damages of materials mixture machine.
8	Complaint regarding land acquisition, valuation and compensation amount.	-	1	1	 Only this 1 complaint registered (June, 2022) with ADB's accountability mechanism/ OSPF from mouza/ village Sangar regarding land acquisition, valuation and compensation. The IVS study was conducted and the top-up will be provided to meet ADB-SPS replacement cost requirements and the complainant's satisfied through the IVS study outcome and provided a statement of satisfaction certificate to PIU and consider the complaint resolved.
	Total	45	3	45	

² of 3 complainants complained through GRC also.

9 LARP Implementation and Social Safeguards Compliance Plan

76. The commencement of civil works will be subject to the satisfactory implementation of LARP, including payment of compensation for land, structures, trees and allowances, and redressal of community concerns. LAR implementation should be verified by an independent/ ERM. The updated schedule for the implementation of LARP (milestones) and its associated activities are in **Table** 9.1.

Table 9.1: Updated Action Plan for LARP Implementation of BHPP

Activities	Responsibility	Tentative Date of Completion	Remarks
Institutional Arrangements			
Hiring and mobilization of Deputy Director Social and Resettlement	PIU	April 2022	Completed
Hiring and mobilization of Assistant Director Social and Resettlement	PIU	January 2023	Completed
Hiring and mobilization of EMA	PIU	September 2022	Completed
Internal Monitoring	T		
Submission of internal SASMRs	PIU/PMC	6th SASMR Jan- Jun 2024. Subsequent reports to be submitted every 6 months (3rd week) thereafter.	5 th SASMR Jjuly- December 2023 submitted and approved by ADB, and validated by EMA.
Preparation and submission of LAR completion report	PIU/PMC	6 months before closing of project	Later stage activity
External Monitoring			
Mobilization of ERM	PIU/PMC	September 2022	Completed
Submission of draft inception report	EMA	Submitted	Completed
Submission of final/revised inception report	EMA	Submitted	Completed
Package-specific LARP compliance report within 2 weeks after receipt of request for handing over for civil works (supported by a compensation, monitoring/ progress report).	EMA	After substantial payment of compensation and allowances in all affected mouzas.	Both sectional LARP compliance reports submitted.
Monthly progress report during implementation of the assignment describing activities undertaken during specific month of assignment.	ЕМА	After 1 month of inception report	 - 1st EMR approved by ADB on December 23, 2022. - 2nd EMR approved by ADB on December 27, 2022.
EMR (two reports x 4 years) within 6 months from mobilization, and after every 6 months to monitor implementation of the remaining compensation payments, livelihood restoration activities, and civil works.	ЕМА	Subsequent reports to be submitted every 6 months thereafter	- 3 rd EMR approved by ADB on March 7, 2023. - 4 th EMR Approved by ADB on March 22, 2024.
Post LARP and LRP evaluation report within 6 months before closing the project.	EMA	Within 6 months before closing the project.	To be disclosed on the ADB website.
Final report	EMA	After completion of LARP	Later stage activity.

Activities	Responsibility	Tentative Date of Completion	Remarks
Information Disclosure, DP Outrea	ach and Consul		,
Translation of updated LARPs information booklet to Urdu language.	PMC	September 2022	Completed
Dissemination of LARP information brochure	PMC	Jan-Jun 2024	Dissemination completed so far for receiving compensation/ allowances.
Consultations/outreach regarding land award and entitlements, and documentation of cases with legal and administrative impediments	PMC/ PIU	Jan-Jun 2024	The entire process is going on in the affected mouza, and all documentation of cases with legal impediments followed guidance note of ADB SPS 2009.
Grievance Redress Mechanism	T		
Notification of GRC	PIU	January 2023	Completed for all mouzas
GRC meetings Recording/documentation of grievances	PIU PIU/ PMC	Need-based As required	Ongoing activity To be reported as required.
Land Acquisition Process			required.
Issuance of notification of land award under section-11 of LAA 1894.	DC/LAC Mansehra	July 6, 2022	Completed
Distribution of payment notices and advertisements in local newspapers.	DC/LAC, PIU supported by PMC	August 2022 and onwards	Ongoing
Disbursement of payments, and documentation of cases with impediments (land, structure and trees)	LAC/DC Mansehra, PIU supported by PMC	September 2022 and onwards	- Ongoing -Documentation of cases with legal impediments to follow ADB's SPS 2009 guidance note.
Disbursement of payments of all allowances/assistance (vulnerability allowance, severity allowance, transition allowance, etc.)	LAC/DC Mansehra, PIU supported by PMC	September 2022 and onwards	-Ongoing -Will depend on disbursement of compensation by LAC and availability of DPs.
Livelihood Restoration (NGO)			T -
NGO shortlisting	PIU	September 2022	Completed
Technical Bid Evaluation	PIU	March 2023	Completed
Price Bid Evaluation	PIU PIU	June 2023	Completed Completed
Contract Signing Contract Effectiveness/NTP	PIU	July 2023 July 2023	Completed
NGO inception report submission	NGO	September 2023	Ongoing
LRP Updation	NGO	December 2024	The provided LRP updation date is tentative. As the NGO will update, finalize and implement the LRP, the realistic date will be provided by the NGO consultant.
Finalization of IVS	IVS	December 2023	IVS report approved by ADB in March 2024.
Verification of census/socio- economic survey on missed out DPs	PIU/ PMC	August 2023	Completed

Activities	Responsibility	Tentative Date of Completion	Remarks
Action and efforts regarding unresolved/unpaid court cases	LAC/DC Mansehra, PIU supported by PMC	Ongoing	Ongoing
Status of action plan implementation per EMA recommendations (Table 8.1 in EMR)	PIU/PMC	June 2024	Complied
Civil Works			
Sign civil works contract	PIU	09 March 2021	Completed
Pay mobilization advance	PIU/ Contractor	27 September 2021	Completed
Joint survey/demarcate in the field areas to be kept from civil works.	PIU/ PMC/ Contractor	Not yet finalized	After basic design approval.
Issue no objection to notice to proceed for civil works in cleared areas as verified by the EMA.	ADB	December 2022 and March 2024	Completed for both Sectional LARPs, and no objection to NTP issued by ADB as - 1st EMR approved by ADB on December 23, 2022 2nd EMR approved by ADB on December 27, 2022 - 3rd EMR approved by ADB on March 7, 2023 - 4th EMR approved by ADB on March 22, 2024

Annexure-1: Guidance Note on handling compensation cases with legal and administrative impediments of ADB

(Revised draft: 18 July 2016)

GUIDANC NOTES	E	X	Handling Compensation Cases with Legal and Administrative Impediments				
Policy Requirement	100 mm 200 mm	compensation omic displacem	and provide other resettlement entitlements before physical or nent.1				
Key Pointers SPS and legal covenants	proje listed incon place comp LARF	1. ADB Safeguard Policy Statement (SPS2009) requires the borrower/client to ensure that no physical displacement or economic displacement will occur until (i) compensation at full replacement cost² has been paid to each displaced person (DP) for project components or sections that are ready to be constructed; (ii) other entitlements listed in the resettlement plan have been provided to DPs; and (iii) a comprehensive income and livelihood rehabilitation program, supported by an adequate budget, is in place to help DPs improve, or at least restore, their incomes and livelihoods. While compensation is required to be paid before displacement, full implementation of the LARP might take longer.³ To ensure policy compliance, specific provisions are included in the Project/Loan agreements to keep on-hold civil works until compensation payments.					
When is compensation considered paid?	bank accor good	the amount in account, or in unt, in lieu of p	on for both land and non-land assets is deemed to have been paid cash or cheque has been provided to DPs ⁴ or deposited into their an escrow account. ⁵ Depositing the compensation in an escrow providing cash or cheque to the DP is justified only when sufficient all legal requirements for contacting and notifying the DPs have				
LAA requirement on compensating before displacement	paym Colle recei if the refen	e acquired lan- nent has been rector is required ve the amount, are is a dispute red to the court	and Acquisition Act (1894) allows the government to take possession d once land award has been made as per LAA Section 11, and made or deposited in court as per LAA Section 31. Accordingly, the d to pay the full amount to the DP, unless (a) the DP refuses to (b) there is no competent person to receive the compensation, or (c) as to the title to receive the compensation. Such cases may be and the compensation amount deposited in the court. In case the centatives did not come forward to collect their compensation, the				

See Involuntary Resettlement Safeguards Policy Principle 11, ADB Safeguards Policy Statement (2009), page 17.

³ See SR 2: Involuntary Resettlement, ADB SPS (2009), para 14.

6 Reference to the court may only be made after the lapse in the period in Section 18 (2) of the LAA.

Page 1 of 9

SPS defines full replacement cost for land and non-land assets as based on the following elements: (i) fair market value; (ii) transaction costs; (iii) interest accrued, (iv) transitional and restoration costs; and (v) other applicable payments, if any. In case of non-land assets, depreciation of structures and other assets should not taken into account. See SR 2: Involuntary Resettlement, ADB SPS (2009), para 10.

Displaced persons include: (i) persons with formal legal rights to land lost in its entirety or in part, (ii) persons who lost the land they occupy in its entirety or in part who have no formal legal rights to such land, but who have claims to such lands that are recognized or recognizable under national laws, and (iii) persons who lost the land they occupy in its entirety or in part who have neither formal legal rights nor recognized or recognizable claims to such land. The borrower/client is required to provide adequate and appropriate replacement land and structures or cash compensation at full replacement cost for lost land and structures, adequate compensation for partially damaged structures, and relocation assistance, if applicable, prior to their relocation. DPs without legal rights to the affected land should be compensated for the loss of their non-land assets, and for other improvements to the land, at full replacement cost prior to their relocation provided they occupied the land or structure before the cut-off date. See SR 2. Involuntary Resettlement, ADB SPS (2009), para 7-8.

An escrow account is a separate, dedicated or trust bank account for keeping money that is the property of others. It is relevant in the case of absentee landlords whose property is acquired for a public purpose, or when there is litigation regarding the compensation amount for land acquisition. This mechanism enables payment of compensation once the legal cases were settled and ownership documents were submitted. Source: A Planning and Implementation Good Practice Sourcebook – Draft Working Document, ADB November 2012, para 152.

amount may be deposited in the Revenue Department payable to the DPs, after sufficient efforts have been made to contact and encourage DPs to appear and notifying the DPs in which treasury the deposit has been made. As per LAA Standing Order 28, the Acquiring Officer is required, to the extent possible, to pay DPs in or near the DPs' village to facilitate collection of compensation.

- 4. Both the LAA (1894) and ADB SPS (2009) require that DPs are compensated before displacement but allow a mechanism for dealing with cases with legal and administrative impediments to disbursing compensation provided that sufficient goodfaith efforts are demonstrated to (a) contact, notify and assist DPs, and (b) deliver compensation payments. This guidance note clarifies:
 - What are cases with legal and administrative impediments to payment of compensation to DPs?
 - What are the requirements under the LAA related to cases with legal and administrative impediments to payment of compensation to DPs?; and,
 - iii. When can good-faith efforts be considered as sufficient and how to document that good-faith efforts have been made?
- Cases with legal and administrative impediments to payment of compensation include:
 - DPs who did not accept the award due to objection to the measurement of the land or affected asset, the amount of compensation, the person to whom it is payable, or the apportionment of the compensation among the persons interested:
 - Absentee landowners (DPs living overseas or in other parts of the country), and without an authorized representative to collect compensation;
 - iii. DPs with pending inheritance mutations;
 - iv. DPs who are unenthusiastic to collect meager compensation amount;
 - v. DPs who are unable to alienate the acquired asset either by being a juvenile with no legally documented guardian or due to other issues.

Cases not valid as legal and administrative impediments

Cases with

administrative impediments

legal and

6. Non-disbursement/non-delivery of compensation due to (a) insufficient funds or delay in approval of funds; or (b) insufficient staff or resources does not justify not paying compensation to DPs before displacement. EAs/IAs have the power and responsibility to ensure that sufficient funds and staffing are available in a timely manner to undertake the required land acquisition. Similarly, non-compensation of affected non-land assets (structures) and improvements by DPs who have no formal rights to the affected land is not considered as a valid legal and administrative impediment (see footnote 4).

Why is it important to address cases with legal and administrative impediments? 7. DPs facing legal and administrative impediments could only be paid when the impediments have been resolved. In such cases, it is uncertain when DPs will receive their compensation causing untoward delay in project implementation and burden to local communities and project stakeholders. More importantly, these impediments prevent the project from assisting these DPs to enhance, or at least restore, their livelihoods and to improve the standards of living of the displaced poor and other vulnerable groups.

Good-faith efforts for cases with 8. Compensation of these DPs is beyond the control of the EA. These are mainly dependent of the actions of the DPs or ruling/decision from a third-party i.e. the court or BOR. However, good-faith efforts are needed from the EA/IA to (a) contact and notify DPs through their last known address, village heads or kins; (b) inform DPs who to

Page 2 of 9

⁷ Financial Commissioner Standing Order No. 28 Land Acquisition, para 88 (V), page 29.

legal and administrative impediments contact or where to proceed to collect their compensation; and (c) advise DPs on possible actions that may help them receive their compensation.

Need for sustained community outreach

- 9. It is important that the LAR management team⁸ undertakes continued community consultations and outreach to locate, assist and guide DPs with legal and administrative impediments. Documentation of the efforts by the LAR management team including multiple visits⁹ to DPs' villages, organizing village meetings, posting of notices in public places, serving notices at last known address of DPs and publishing the names of unpaid DPs in the print media is needed to demonstrate that due efforts were conducted in addressing cases with impediments to paying compensation.
- 10. Some issue-specific measures to confirm DPs understanding about the availability of compensation, payment mechanism, time-lines, and DPs agreement to the commencement of works (wherever required) while the issue is being resolved can help show and validate the efforts exhausted by the EA to achieve the policy objectives and enable the decision makers to allow the construction works accordingly. For each issue, documentation requirements and recording of certification statements are discussed below. Standard templates for additional documentation are provided against each issue as and wherever required:

Cases with title disputes and litigation

Land Title Disputes or Litigations among the DPs or Court References Against Award

- 11. When there is a dispute on the title of the affected land before a competent court of law or when DPs file references against award, compensation can only be made after the court decrees which may take years. Further, right to appeal against court's decree cannot be forfeited or denied under law which could further delay the payment. In such cases, payment of compensation in a given time frame is impossible and it would be appropriate to deposit compensation in treasury at courts disposal to make sure the DPs are paid as and when court verdict is passed. For these cases, the process provided in the succeeding paras should be followed.
- 12. Immediately after identifying such cases, the EA after seeking court's permission should deposit the compensation amount in the court for payment to the DPs as and when court decides their reference or title dispute. The receipt and records for such deposits should be maintained at the EA's project office. Meanwhile, the EA through its LAR staff should liaise with the DPs to inform them about the compensation payment mechanism and compensation deposited in the treasury or the court. The EA's project office should prepare and maintain the following record:
 - Database/listing and field reports on activities done to identify and screen DPs with their legal/administrative issues including nature of dispute and reference court where pending
 - · Field reports on activities done to coordinate with the DPs for early resolution of

Page 3 of 9

The LAR management team may include Land Acquisition and Resettlement Staff engaged by the EA i.e. EA's Land Management Staff, Land Acquisition Collector deputed by BOR, Resettlement Specialists and social mobilizers either recruited by the EA or mobilized through Consultants (Safeguards Management or Construction Supervision Consultants) to support the EA in effective LAR management...

Repeated visits in three consecutive months scheduled for each village by the Land Acquisition Collector/Land Acquisition Unit of the EA to deliver compensation to unpaid DPs and identify those with legal and administrative impediments. The repeated visits should be documented showing visit schedule, information disclosure reports, list of persons met and field visit reports duly endorsed by the local community and the village headman confirming number of identified DPs with legal and administrative impediments.

their issues and with courts for seeking permission/guidance and deposit of compensation in treasury at court's disposal.

copy of the delivery of notices (with signed receipt) to the DPs confirming deposit
of amount at court's disposal and clarifying mechanism for payment.

Absentee land owners


Absentee Landowners (DPs Living Overseas or in Other Parts of the Country).

- 13. Many rural households migrate to cities for better livelihood opportunities and standard of living. Moreover, hereditary division over time resulted in the segmentation of agricultural land parcels into unproductive units. While some families with land and assets in different parts of the country divide their land based on their places of residence, many do so without legally formalizing such settlements and getting land records updated accordingly. Some family members who have migrated overseas permanently had land in their name or retained their respective share in family-owned land as per land revenue records. Such DPs who own or have share in the land as per record but are not living in the village are termed as absentee landowners.
- 14. Absentee landowners ¹⁰ are also recorded as DPs. The compensation to absentee land owners could not be made until they appear before the acquiring officer for processing and payment of compensation. LAA requires that notices are delivered against each land parcel either through (a) co-sharers in the acquired land parcel, (b) DPs relatives living in the village, or (c) through the village headman. The legal requirement is to serve notices to DPs at their places of residence either through special messenger or registered post, which can only be met if the whereabouts and residence of the absentee land owners is known. An additional measure that may be considered to notify absentee land owners whose whereabouts are unknown is to publish their names in print media (National Daily News Paper).¹¹
- 15. It is vital to collect information about the DP's contact details including the mailing and residential address. The following measures are proposed to contact absentee landowners and maintain record of all efforts made by the EA:
 - Identify and record DPs relation in affected village or local contact person, collect information about DP's present place of residence. See template 1 below:

Page 4 of 9

Land owners who are recorded in the landholding rights register as owners but they have shifted from the village to other areas in the country or overseas for better income opportunities and living standard.

In NTCHIP tranche-1 and NHDSIP tranche -II projects (i.e. M-4 Faisalabad-Gojra Section (ADB Loan 2400) and Sukkur-Jacobabad (N-65) (ADB Loan 2540)) and the National Motorway M-4 Gojra-Shorkot Section Project (ADB Loan 3300), the notices with the names of the DPs who have not come forward to collect compensation were published in the National News Papers (Urdu language) as a last resort effort to approach unpaid DPs for compensation delivery.



- Deliver formal notice to the DP's last known address (recorded in template 1) through registered post with acknowledgement receipt attached. Keep on-file a scanned-copy of the notice and acknowledgement receipt.
- In case no contact person or relative of the DPs is identified in the village and the
 local community confirms DPs whereabouts are unknown, a certification
 statement from any of the resident land owner in the village preferably by the
 president or member of the Displaced Persons Committee (DPC) and duly
 witnessed by (a) the village headman and, (b) land revenue patwari should be
 recorded and maintained. See Template 2 below (to be translated to Urdu).

	Date prepared:
Particular of DP and acquired land parcel	range 11.100.12.200 removement to the
	sident of{Enter DP Last known address} Land
Plot KhasraNos	Located Village
Statement:	
	Cor local resident land asset/owner, on behalf of the other residents in
illage solemnly declare that:	
 To my information, the DP and his family never lived in vill 	cords but for last () they have never been seen in the village, age, neither any relative of DP lives in village/area nor any of the village
resident know the whereabouts of the DP and his family.	
	I efforts to outreach the DPs in village and those living in other areas and
	ed in treasury that can be claimed as and when the DPS show-up to claim.
vilage	hich is withessed by the Village Headman and I land revenue Patwan of
vilage	nich is withessed by the Village Headman and I land revenue Hatwan of
vilage The Declarant Sign/Thumb Impression	nich is withessed by the Village Headman and Tand revenue Patwan of
vilage The Declarant Sign/Thumb Impression Same	nich is withessed by the Village Headman and Tand revenue Hatwan of
vilage The Declarant Sign/Thumb Impression Signe Wilage Headman/Local resident land owner	nich is withessed by the Village Headman and Tand revenue Patwan of
	nich is withessed by the Village Headman and Tanci revenue Hatwan of
vilage ———. The Declarant Sign/Thumb Impression same Mlage Headman/Local resident land owner	nich is withessed by the Village Headman and I sinc revenue Harwari of
vilage ———. The Declarant Sign/Thumb Impression Same Vilage Headman/Local resident land owner Resident of Witnessed By Vilage Headmanand land revenue Patwan of village (P	ut village name here), personally know Mr/Mrs
vilage ————————————————————————————————————	ut vilage name here), personally know Mt/Mrs. (), and witness versolly of statement made by him affirming that the
wilage ————————————————————————————————————	ut vilage name here), personally know MrMrs. (), and witness versotly of statement made by him affirming that the members are not lising in villages area since for — and their current.
wilage ————————————————————————————————————	ut vilage name here), personally know Mr/Mrs. (), and witness versorly of statement made by him affirming that the members are not living in vilage/area since/for — — and their current vilage.
vilage ————————————————————————————————————	ut vilage name here), personally know MrMrs. (), and witness versotly of statement made by him affirming that the members are not lising in villages area since for — and their current.
vilage The Declarant Sign/Thumb Impression Same Village Headman/Local resident land owner Nitroesed By We the Village Headmanand land revenue Patwan of village (President/member of DPC or local resident land owner of village DN Named (Abut name OPC here) himself or any of his family blaces of residence are not known to any of the local residents in	ut vilage name here), personally know Mr/Mrs. (), and witness versorly of statement made by him affirming that the members are not living in vilage/area since/for — — and their current vilage.

DPs with pending inheritance mutation

iii) DPs with Pending Inheritance Mutations

16. Land records are maintained by the local land revenue authorities who are responsible to enter land mutation transactions as and when reported by the landowners and update land records accordingly. Some heirs of DPs who passed away fail to get inheritance mutations recorded and get land records updated accordingly. On average, land acquisition process is completed almost in two years. During the acquisition or after land awards are announced, some DPs pass away without receiving their entitled

Page 5 of 9

compensation. Although the legal heirs of the deceased DP are eligible for compensation, they could not be paid until the inheritance mutation is recorded and remaining land of deceased DP is transferred in their name.

- 17. The law requires heirs of the DP to report to the local land revenue authorities about the demise of the DP and apply for the updating of the land record. Upon receipt of the application, the land revenue authorities undergo a legal process to record the inheritance mutation, update the land record reflecting the names of legal heirs and their respective shares in the land record. When it is done, the compensation can be paid to the legal heirs as per their respective share. This process normally takes three to four months. For cases where inheritance mutations are not timely reported, recording becomes more difficult and can take a longer period to complete.
- 18. When it is determined that the DP has passed away, the LAR management team should approach the legal heirs to apprise them on the process for getting compensation and assist them in approaching land revenue authorities to get their inheritance mutations recorded. The LAR management team should carry-out the following activities to facilitate the mutation of inheritance and early payment of compensation to the heirs and document their efforts:
 - Identify all living legal heirs of the DP, visit the heirs residing in the village and quide them on the process and facilitate in inheritance mutation process:
 - Collect a statement from the legal heirs¹² confirming that their inheritance
 mutation of land is pending, acknowledging the EA's efforts to assist them,
 indicating awareness that funds are available for compensation delivery, and
 concurring that works may commence while their inheritance mutation is being
 processed.
 - Keep copies of the signed statement in the EA project office files. See Template 3 below (to be translated to Urdu):

Page 6 of 9

To the extent possible, all legal heirs living within the village should sign the Statement. If some heirs are not available to sign, the LAR management team should prepare a field report indicating who are the heirs who were not able to sign the statement and the circumstances why they were not able to sign i.e. out of the village or country, ill, etc. The LAR management team should also record the names of heirs who are out of the village or country and their last known address and advise the other heirs to relay the information to those who are away.

Template 3: Inheritor's Statement When Inheritance Mutation is Pending
Date Prepared:
Particulars of DP and acquired land parcel Name of DP(enter DP Name with Parentage as of land record), owner of Acquired Land Plot Khasra Nos
Statement by the Inheritor's
We the persons listed below as legal heirs of DP—{put name of DP here}——against acquired land referred above solemnty declare that The inheritance mutation of above said acquired land is pending; We understand that compensation can be claimed/paid according to inheritance mutation recorded in land record and we are coordinating with the Land Revenue Authorities in this regard. (Name of Staff, Office and EA) has clarified that compensation amount already deposited in treasury can be to legal heirs as and when the inheritance mutation issues are resolved; We have no objection to the commencement project works on our plot while our inheritance mutation of land is being processed; This statement is given free of operiors and compulsions which is witnessed by Village Headman and APC president.
The Declarant
Sign/Thumb Impression Sign/Impression Thumb Name Resident of Resident of
Sign/ Thumb Impression Name Resident of Resident of
Sign/ Thumb Impression Name Resident of Resident of
Witnessed By We the Vilage Headman and President APC village———, personally know the above signatones as legal heirs of the DP, and confirm witness the statement above. Signed Signed
Name: Mr. Name: Mr. Village Headman Chak President OPC Chak President OPC Chak

iv) DPs Who are Unable to Alienate the Acquired Asset:

DPs unable to alienate the land

- 19. Minors, juveniles and DPs with mental disability are not capable to alienate the acquired land under law. The law provides that compensation could be paid through legally-designated guardians or managers who can act and alienate the immovable property on behalf of the DP. In cases where the guardians are not designated by the court, the compensation is put on-hold until the minor attains the age of majority and claim compensation.
- 20. It is common that children inherit their parents' immovable properties, but is kept in possession and used by adult male members of the extended family or kinship group as a joint family asset. It is not a common practice to appoint guardians following the Guardians and Wards Act of 1890. Hence, compensation of DPs with minor age is kept on hold until the DP becomes of legal age unless a valid guardian certificate is produced. Although such cases are not many, it is important to guide the adults who provide care to these DPs to approach the right forum or court for appointing a guardian under law.
- The LAR management team should carry-out the following activities in dealing with pending guardian's appointment and in documenting its efforts:
 - Coordinate with the Living Parent or other grown up members of the household the DP is living with and guide them on the process of appointing a guardian.
 - Collect a certification statement from the Living Parent or other grown up member of the household the DP is living with, that i) confirms EA's efforts to notify and guide them and secure funds for compensation payment, ii) states that the appointment of guardian is pending, and iii) concurs to the commencement of civil works on the plot while the guardianship certificate is being processed. Such statement should be witnessed by the village headman and the village DPC chairman or member. See Template 4 below (to be translated to Urdu).

Page 7 of 9

Template 4: Guardian Statement if DP is Ju-	venile
2000 N - 2000 N - 2000 N - 10	Date Prepared:
Particular of DPs and acquired land parcel Name/Names of DPs i) (enter DP Name/names of DPs with Parentage), ii)	and iii) Resident
of (Enter DP current address) Own acquired Land Plot Khasra	Nos Located VIIIage
Statement by Guardian	
Statement by Guardian [th whom the minor DPIDPs (ives) of
DP/DPs (). (put name of DP/DPs here) (i). (ii)	as natural guardian solemnly declare tha
 The DP/DPs is/are minor who lives with me and as natural guardian of DP/DPs, I am 	responsible for his/her/their well-being and
bringing him/her/them up;	
 (indicate name of staff, unit, and EA) has clarified that compensation are 	
to legal guardian of DP/DPs after production of the valid Guardian Certificate issued	
 A petition for issuance of guardians certificate is filed/being filed in the competent co 	urt and the court's decision is pending:
 The awarded compensation in name of DP/DPs will be collected upon issuance of g 	
guardian I have no objection to commencement of project works; and	uardian's certificate by court, however, as natu
	uardian's certificate by court, however, as natu
guardian I have no objection to commencement of project works; and	uardian's certificate by court, however, as natu
guardian I have no objection to commoncement of project works; and This statement is given free of coercion and compute on which is witnessed by Villag The Declarant	uardian's certificate by court, however, as natur
guardian I have no objection to commencement of project works; and This statement is given free of operation and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression	uardian's certificate by court, however, as natur
guardian I have no objection to commencement of project works; and • This statement is given free of coercion and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name	uardian's certificate by court, however, as natu
guardian I have no objection to commencement of project works; and This statement is given free of operation and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP	uardian's certificate by court, however, as natu
guardian I have no objection to commencement of project works; and • This statement is given free of coercion and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name	uardian's certificate by court, however, as natur
guardian I have no objection to commencement of project works; and • This statement is given free of operation and computation which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of	uardian's certificate by court, however, as natur
guardian I have no objection to commencement of project works; and This statement is given free of operation and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of Witnessed By	uardian's cerificate by court. However, as natu se Headman and DPC president.
guardian I have no objection to commencement of project works; and This statement is given free of coercion and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of Witnessed By We the Village Headman and President APC village———, personally know MrMrs	uardian's certificate by court. however, as nature Headman and DPC president. and witness veracity of stateme
guardian I have no objection to commencement of project works; and This statement is given free of coercion and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of Witnessed By We the Village Headman and President APC village———, personally know Mt/Mrs made by confirming that the Minor DP/DPs named above fives with himther in village/bity_{	uardian's certificate by court. however, as nature pe Headman and DPC president. and witness veracity of stateme Put name of village city here).
guardian I have no objection to commencement of project works; and • This statement is given free of operation and computation which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of	uardian's certificate by court. however, as nature to Headman and DPC president. and witness veracity of stateme
guardian I have no objection to commencement of project works; and This statement is given free of coercion and compulsion which is witnessed by Villag The Declarant Sign/Thumb Impression Name Relationship with DP Resident of Witnessed By We the Village Headman and President APC village———, personally know Mt/Mrs made by confirming that the Minor DP/DPs named above fives with himther in village/bity_{	uardian's certificate by court. however, as nature pe Headman and DPC president. and witness veracity of stateme Put name of village city here).

DPs with meager compensation

v) DPs with Meager Compensation

- 22. The compensation amount itself proves driving factor for DPs to submit their claims. In cases where small land holdings are in joint ownership with several entitled persons, shares in compensation for each DP become very small (\$100 and below). A good number¹³ of DPs fall in this category and they never show-up to collect compensation. The situation is further aggravated when such DPs also face other legal or administrative issues like pending inheritance mutations of acquired land or living overseas and other parts in the country.
- 23. Although the law provides a mechanism that includes cash payment at the village or payment through money order in case of absentee land owners ¹⁴, such is no longer practiced. The only available mode is payment through voucher debit-able to the treasury which requires the DP to travel repeatedly to the district/tehsil headquarter to receive their compensation, making the transportation cost higher than their compensation. This also requires that the DP has or opens a bank account.
- 24. The LAR management team should explore other payment modes allowed under the LAA including cash payment or payment through money order if the DP is living out of the project area. If such unclaimed compensations are deposited at court's disposal as legal remedy, it will be of no gain because a significant number of the DPs will remain unpaid. Following actions should be taken and recorded to explore specific measures and seek guidance from BOR in this aspect.
 - Define a maximum slab of amount to be termed as meager compensation and get it endorsed by the EA;
 - · Document coordination efforts with BOR including i) official correspondence and

Page 8 of 10

¹³ In the National Motorway M-4 Gojra-Shorkot Section Project, almost ± 10% DPs are entitled to a compensation below 100 US \$

¹⁴ Rule 87, Financial Commissioner's (Board of Revenue) Standing Order No 28 (1909) on land acquisition procedures.

ii) meet with BOR to seek guidance on the issue at the project and EA levels.
 Maintain a record of actions taken by the project team for payment to DP or deposit compensation at court's disposal following guidance from BOR.

Page 9 of 9

Annexure-2: Scanned copies (sample) of recorded documents for DPs with impediments

DPs entitled to meager Compensation amount (Mouza Paras)

			بالاكوت بانتيزروبادريرا التيكنت، بالاكل عمولي عو (AMOUNT CASE	Ť.		
18-06-2	024 315			_		رازير
2	ط <u>ع عالته ه</u>	-	قص <u>ل</u> بالأكو ث		وريانام الرس	وضواع
الهر قبض الوصول	مة الرّه محض كا موجوده بيد الدائر كافحان فمير	حاثه فض عدائد	گائل ش جم خض سے دابلہ اوائر کانام اور موبائل تمبر	رِ اجْلِتْ كَ الرَّاتِ كَلْ هِم	pt6000000	12/
/603	All Sant	داشته دار	راض شاه	زسن 💮	دىرى	6
1785	13.5%	- مجيا ذار	alizandi	10	عبرالرشيد	(2
2043	المام	عا فرق ذا د	مفامت شاه	ir	المغم الله	0
2180	مالره	دستثروار	مير الحريثان	47	غنام ب ن	(5)
2920	مان،	15056	سيافرناه	زمئ	2/33	(3)
3090	العربي إماء	رند	خارياه	ige;	ستوكث م	0
	الفدين كتده		-AMPRICE 15		المنكحة	لوبات حا
		TU MADE	CP GRC (field	t level) Alas	ساء الله	٤
	ند	Padre.	MPP. T		*	
		D	1,41	As .	טעל על	

DPs entitled to meager Compensation amount (Mouza Sangar) بالاكوث بأنيذ دوياوريرا فيكث مبالاكوث سأشهره (MEAGER AMOUNT CASE) 18-06-2024 310 جمين باداكوره علع عالزه موضع / گادل کانام ستاره فلل كاموتدوية گاؤی شن جس محض سے رابلہ نمير فبق الوصول عال، فقل ساد الله حاثره فحض كانهم يراجك كالالحاك 12 اوراس كافون نير ہوا ک کا تام اور مو باکل تمبر 209 Util to والمرتز واو Ubjela Cr; 0 6:11) 1311 وفامير 00 (2) عاول ذار فالهزار 135% is 0 1927 3,0 2632 المحتداد (9) والره 2069 3 1513 أيست آماد ارتبرفان 00 ا میٹ آلیا ہ تعدیق کندہ 2521 15 معلوات حاصل كشدد GRC (field level) メイルナ とうりし


DPs Living abroad and Other Cities in Pakistan (Mouza Paras)


يل فير_ شع (كاناد			هميل ناواکر ع		طن <u>ما ترو</u>	16-86-20
A.	مناش كانام	پ ایجات کے افراعت کی حم	گاؤل على ميش خنص سنة رابط عداس كانام دور موياكل تمير	حال محتل سارات	الراس كافران الموجود وي: اوراس كافران فهر	فير فيش اوسول
a	سربازل ايحد	زمن	سيخابرناه	- محارار	l'up 1	1117
	سيرا فحبر على شاه	(1)	مسر انفرتاه	رمنت دا بر	studien.	1576
0	ى قى آئىرنە	رنين	wigin .	جه خالهواء	43.50	1656
(9	محدضاء في شاه	رامح	لعبو تختیر شاه	عامون دار	Wille	2076
(3	اعالثاه	60	000-1100	15,50	11/2/10	3629
i 3	ندلىرىسىن شاه	ازمن	مبدريا من سياناه	دمتث	315	3169
باعدمامر	مل كتده:	×	of.		التعديق كشده	
	عبادار	NOTE OF THE PROPERTY OF THE PR	SHERRICS COMMITTEEN, GRC (Red			
1	36	Hevel) メジルメ	GRC (IIII	MATO	19	

DPs Living abroad and Other Cities in Pakistan (Mouza Sangar)


	Core		بالاکوشهائیڈرویادر پراجیکٹ مہالاً سال باش تحکی ریٹلادہ سرے گاہار	عد المنظم المنظمة المن		
16-06-20	سر <u>ماني م</u>	ā	صی باداکورخ	6		یریل فیر موضح انا
تمبر فيغن الوسول	متاژه فخش کا سوج دورید اور اگر کا فوان تمبر	عال الحس سدين	گاؤں بیل جس الفراسے وابلہ عواس کانام اور موباکل فیر	پرا ف کششکارات کی هم	مثاثرة المثل كالاس.	نبرفد
145	اسالع اما و	عجا ذار	The tier	Ui	محد نزامت	0
569	(ingl	(3-	ومايت	زين	متواتس	0
799	سعودل ورب	عِياً قمالاً	الفع الزين	زس	هجير أذوالذتها براحزت	0
830	سعوری حرب	فاخرن ذاء	لعيم ارزكن	60	to day.	3
1129	الرامينان	فالهزار	اكعنت	زمین	عين د کين	(3)
	الصدايق كننده		a f		مل كنده!	ملواشدما
		rt	CRC (fel	d bevol) of law	ماراني	>_(
		Redress	GRC (field	185° 2	学	13%
		No	المر ا	z;	ما والأرث	


Inheritance Mutation of DPs not yet completed of Mouza Paras





Inheritance Mutation of DPs not yet completed of Mouza Paras

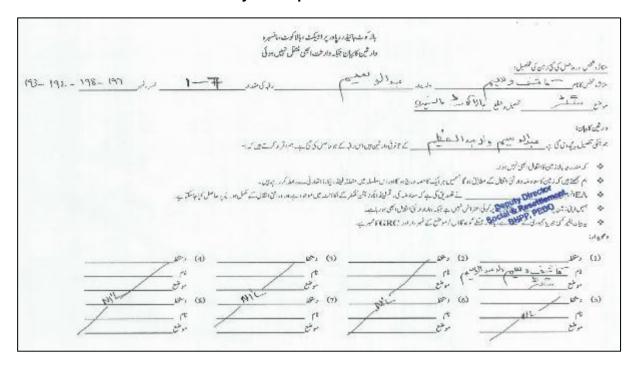



Litigant DPs with pending title disputes and court cases (Mouza Sangar)



اطلاع برائے مالکان ارضیات کورٹ ریفرنسز بالا کوٹ ہائیڈرویا ورتر قیاتی پر اجیکٹ تحصیل بالا کوٹ، ضلع مانسپرہ

نام: مسمور ولد: مسمور کی این آم مالکان اراضیات جن کی زشتن ریفرنس قمبر 30 / 18 ہذامیں سالمان نے مسمور کی مسمور کے این تمام مالکان اراضیات جن کی زشتن ریفرنس قمبر 30 / 18 ہذامیں سالمان نے مسئول علیم کی اداخی و درختان کے معاوضہ کے متعلقہ وعوی اریفرنس درخ کیا ہے۔ لہذا اس نوٹس کے ذریعہ آ بچو مطلع کیا جاتا ہے کہ آ بچی رقوم بابت قیت اراضیات ، درختان ، تغییر شدہ مکانات کورٹ ریفرنسز کی وجہ سے کہ آ بچی رکھوں کے متعلقہ کی سرپر دکیا گیاہے۔

Annexure-3: Compensation and Allowance Voucher/ Payment Receipt of Mouza Paras and Bela Sacha

				Aris.	Phin	er Pe	urjeet	Maner	Non	and the same					1	oneher for	Balako	The state of	-				
		Baln	hat H	-	TV TO		100								1	1 A 60 40 6	DAIE T	WAGEN	Power I	Project 6	Samuel in	1	
	See and				7	Halling.	177								12		825	40000	学小	Sand	THE P	HT HA	-
																S Ryll		10	1720			Dries	
						Both									- 5	ri Religio		No.	921975	100	1926	150	
					3	Harris .											57901	X4,1760.	Shire		52150	Reits	
					1	85.9									12	7 Ka.164		RA194	34477	84,370%	1902	B12558	17801
															- 5	3 Ru3967	1802:4	5.767	-	En. 166			34411
															- 8	E Royl	855914	Reliti	HIQ1	86,5953	180312	Bi-Witt	
															18	P RATHUM	137416		8559/3	1690	65592		\$1590
			Til	tal.		3603	12/2								100	Rs.15743/-	-	Rs.78076	E17475	R4.7817	83746	Na.11712	
			-				A TILL SU	WIE WIE		00.0						TANOX	9.87	Rs.157426	32	Ru(5743)		Radjein	
											10.5504				- 10	TO REAL				1000		L. Constitution	-
		80	CH	EC N	N	=deC	710	-							- 11					05 4 F	II. NW/P361	173-1700PM	
								a Villagen							-	- 12	VOCE	ERN	01	De)		100	SHIRE
															-			M. Same	Section in con-		-		
	-			L MICH	1	S MARY LA	10	pronting							- 11	1920 11	A11.02/123	3000 X G-1123	Directi Es	Market Land	Parame		
	200		baut			196		Maski		6,7227					- 11								
	4 "				160	444.00	y 34(2)	-(Thirty-)	16 774		Thom.				100		Descript Dec	Dr.	Chime L	at top ray,	Heatre		
		244	44					ng throws							- 11	5	54				North I No.	200	
	Assert	No. 35	2														- 1		2000000		tin (K day o		
	Batmit: Di								(5)	والماح	60.00	4			1	pl chen						M.Thousal	
	taket Hydr			ntt				100	-11	3 (4)	1801	3			1	Award No. 3	54		- Section Sect	to trace Ray	an (supple	ing the arrest	PRO WAL
		Sanga						40.000		1000	F. F. C. S.				3	ted: 19-08-	2022		47.63	20100	2000	LOS est	Sant
															-	kat Hydro Pa	Wer Prote	ect	THE				
							8	8	0	SH					1			161				DD KTP	4100
															-	Mousa Pari	16		13-12-30	02.Tar 19-12	200/10	· 21 - 11 - 11 - 11 - 11 - 11 - 11 - 11	takingi k
	besiet						100												10000				Mary
							- F		76	N1991						contract and the	Mary C			# E &			
						Pates	at for Face	CHAI	San	Tena	ref				18	CALLES BY IN	NEIDI.			216-01			
							PEL				how				1.0		-	-	3	July			
							20.30	127 St.							- 11					- Two	divinue PLLS		
								Minwo							12					- 12			
																					85.78111/	-6/	1
					п			th							-						1 -	-	-/
						11cg	uny that		uni:						-					- 3	-	-1 -	
					п		no Lan	d Acqui		66					-				Dep	Deout	iniones, 1	Minmehra	-
		100					Mun	settru		117		20					Treasury (39cer	18	Deputy	Commiss	April 1	Pin
S	4	In	(Wildery)	Office	4					32	Sec.	8			1		TTERSBITO.			Collec	SEL PITTE	Diam.	
				_																100			
					who design	-	-	-	-	-	-			TATA	· ·	e Roll of I	E 61 75	Hydro	nowet	Protei	ct. Mor	uza Pa	as
-				inter	_	COR	as p	-	na/	(13.5)					100	e Roll of	Jaiako	1	po	1		1	
		ymer	nt of	alle	war		8					8										- 3	
10000000			1	allo			Houses	emme emme	8	the state of		i i	12 mg	9	2	1				1		9	
The state of the s			1				for Houses	or Comme	owanoe	Assistan	but	Viowanc	for 12 mo	OWance	atlon / C		Signat	ure/	Signat	ure/	Signat	ure of	
Control March Control	to Acquaintance diStructure		1				ance for Houses	oe for Comme ctures	Allowance	ing Assistan	A Rond	et Allowan	moe for 12 mo	Allowance	slocation / C	Total	thur	mb	thun	nb dn	(Verificar)	Deputy	5igr
Control of the contro	to Acquaintance diStructure	Household	strand Name	ement	hy Allowance	cation Allowance	Sowance for Houses	wance for Commercia Structures	Rion Allowance	Moving Assistan	House Rent		lowance for 12 month	ricity Allowance	d Dislocation / Chula Allowance	Total		nb sion of	Signat thun impres of with	nb islon	(Verific	Deputy r (S&R)	5ig
Control of the contro	to Acquaintance diStructure	Household	strand Name		hy Allowance	cation Allowance	g Allowance for Houses		ransition Allowance	sess Moving Assistan	House Rent			Secricity Allowance	shold Dislocation / Cl Allowance	Total	impress	nb sion of	impres	nb islon	(Verific Officer) Directo	Deputy r (S&R)	5igr
ESPECIAL DESCRIPTION OF THE PROPERTY OF THE PR	to Acquaintance diStructure		1	ement		cation Allowance	Willing Allowance for Houses		Transition Allowance	lusiness Moving Assistan	House Rent	Severe Impact Allowand		Electricity Allowance	ousehold Dislocation / Cl Allowance	Total	impress	nb sion of	impres	nb islon	(Verific Officer) Directo	Deputy r (S&R)	5ig
		Household	strand Name	ement	hy Allowance		Shiffing Allowance for Houses		Transition Allewance	Business Moving Assistance	House Rent		Business Allowance for 12 mo	Electricity Allowance	Household Dislocation / Cl Allowance	3770	thur impress own	mb sion of ver	thun impres of with	nb islon ness	(Verific Officer) Directo	Deputy r (S&R)	5ig
The state of the s	to Acquaintance diStructure	Head of Household	strand Name	ement	hy Allowance	cation Allowance	Shiffing Allowance for Houses		Transition Allowance	Business Moving Assistan	House Rent			Electricity Allowance	Household Dislocation / Cl Allowance	3770	impress	mb sion of ver	thun impres of with	nb islon ness	(Verific Officer) Directo	Deputy r (S&R)	Fi Sigr AD Mar
Charles and the control of the contr	to Acquaintance diStructure	Head of Household	Fatheri Husband Name	ement	hy Allowance	cation Allowance	Shifting Allowance for Houses		Transition Allewance	Businesa Moving Assistan	House Rent			Electricity Allowance	Household D	3770	thur impress own	mb sion of ver	thun impres of with	agenti-	(Verific Officer) Directo	Deputy r (S&R)	5igr
	to Acquaintance diStructure	Head of Household	Fatheri Husband Name	Settlement	hy Allowance	Structure Relocation Allowance	Shiffing Allov		Transitio	Business Moving Assistan	H	Severe Imp		Electricit	Household D	الا متيامه الرش ناه مد	thur impress own	mb sion of ver	thun impres of with	nb islon ness	(Verific Officer) Directo	Deputy r (S&R)	5igr
	to Acquaintance diStructure	Head of Household	Fatheri Husband Name	Settlement	hy Allowance	Structure Relocation Allowance	Shiffing Allov		57,000 Transition Allowance	Business Moving Assistan	H			20,010 Electricity Allowance	Household D	3770	thur impress own	mb sion of ver	thun impres of with	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	Household	Fatheri Husband Name	ement	hy Allowance	cation Allowance	31,000 Shifting Allowance for Houses		Transitio	Business Moving Assistan	100,010 House Rent	Severe Imp		Electricit	2,603,000 Household Dislocation / Cl Allowance	الا متيامه الرش ناه مد	thur impress own	mb sion of ver	thun impres of with	agenti-	(Verificar) Officer) Directo PE)	Deputy r (S&R)	5igr
	to Acquaintance diStructure	Head of Household	strand Name	Settlement	hy Allowance	Structure Relocation Allowance	Shiffing Allov		Transitio	Business Moving Assistan	H	Severe Imp		Electricit	Household D	الا متيامه الرش ناه مد	thur impress own	mb sion of ver	thun impres of with	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	Head of Household	Fatheri Husband Name	Settlement	hy Allowance	Structure Relocation Allowance	Shiffing Allov		Transitio	Business Moving Assistan	H	Severe Imp		Electricit	Household D	المار معنى أماره الروش أماره 2,302,000	thur impress own	mb sion of ver	thun impres of with	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	-Oth Tasleem Kausar Head of Household	Fatheri Husband Name	Settlement	hy Allowance	Structure Relocation Allowance	Shiffing Allov		Transitio	Business Moring Assistan	H	Severe Imp		Electricit	Household D	الا متيامه الرش ناه مد	thur impress own	mb sion of ver	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	-Oth Tasleem Kausar Head of Household	Syed Mazhar Shah Fatheri Husband Name	Settlement	hy Allowance	31,000 Structure Relocation Allowance	Shiffing Allov		57,000 Transitio	Business Moring Assistan	100,000 Hou	63,400 Servere limp		20,010 Electricil	2,603,809 Household Di	المار معنى أماره الروش أماره 2,302,000	thur impress own	nb sion of ser	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	-Oth Tasleem Kausar Head of Household	Syed Mazhar Shah Fatheri Husband Name	Nhan	Vulnerability Allowance	31,000 Structure Relocation Allowance	31,000 Shiffing Allow		57,000 Transitio	Business Moving Assistan	100,000 Hou	63,400 Servere limp		20,010 Electricil	2,603,809 Household Di	المار معنى أماره الروش أماره 2,302,000	thur impress own	nb sion of ser	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	-Oth Tasleem Kausar Head of Household	Syed Mazhar Shah Fatheri Husband Name	Settlement	Vulnerability Allowance	Structure Relocation Allowance	Shiffing Allov		Transitio	Business Moving Assistan	H	63,400 Servere limp		Electricit	Household D	المار الرش كان 2,302,000	thur impress own	nb sion of ser	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	to Acquaintance diStructure	-Oth Tasleem Kausar Head of Household	Fatheri Husband Name	Nhan	Vulnerability Allowance	31,000 Structure Relocation Allowance	31,000 Shiffing Allow		57,000 Transitio	Business Moving Assistan	100,000 Hou	63,400 Servere limp		20,010 Electricil	2,603,809 Household Di	المار الرش كان 2,302,000	thur impress own	nb sion of ser	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5ig
	to Acquaintance diStructure	Head of Household	Syed Mazhar Shah Fatheri Husband Name	Nhan	Vulnerability Allowance	31,000 Structure Relocation Allowance	31,000 Shiffing Allow		57,000 Transitio	Business Morting Assistan	100,000 Hou	63,400 Servere limp		20,010 Electricil	2,603,809 Household Di	المار الرش كان 2,302,000	thur impress own	nb sion of ser	ن شاه می استان شاه استان شاه استان شاه	agenti-	(Verificar) Officer) Directo PE)	cation Deputy r (S&R) DO	5igr
	S. No According to Acquisitance Roll of Land/Siructure	Muhammad Yousef -Bibh Tasleem Kausar Head of Household	After All Styde Mather Shah Father Husband Name	Mihan Settlement	Vunerability Allowance	31,000 Structure Relocation Allowance	31,000 Shiffing Allor	Shifting Allowa	67,000 57,000 Transitio		100,000 100,000 How	63,000 63,000 Servere lmp	Business Allow	20,000 20,000 Electricil	2,000,000 2,000,009 Household Di	المام الدون عام 2,302,000 13 <u>5</u> 01— 2,302,000	ss-magenta	المالة ا	المنافقة ال	عادد	(Verfill Officer) Directo PEI	Z.L.	Sign
	S.No According to Acquaistungs Roll of LandSinvolun	Muhammad Yousef - Oth Tasleem Kauser Head of Household	After All Strate Syed Mazher Shah Father Husband Name	Nihan Settlement	Vulnerability Allowance	31,000 31,000 Structure Relocation Allowance	31,000 Shifting Allor	Shifting Allowar	57,000 57,000 Transitio		100,000 100,000 How	63,000 63,000 Servere Imp	Busines Allow	20,000 Electrici	2,006,000 2,609,000 Household Di	2,302,000	1 that impress out of the court	11-3 44 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	ا مال	عمران ما در الم	(Verfficon) Officer) Directo PEI	Z. be	Signal
	S.No According to Acquaistungs Roll of LandSinvolun	Muhammad Yousef - Oth Tasleem Kauser Head of Household	After All Strate Syed Mazher Shah Father Husband Name	Nihan Settlement	Vulnerability Allowance	31,000 31,000 Structure Relocation Allowance	31,000 Shifting Allor	Shifting Allowar	57,000 57,000 Transitio		100,000 100,000 How	63,000 63,000 Servere Imp	Busines Allow	20,000 Electrici	2,006,000 2,609,000 Household Di	المار الرش كان 2,302,000	1 that impress out of the court	11-3 44 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	ا مال	عمران ما در الم	(Verfficon) Officer) Directo PEI	Z. be	Signal
	S.No According to Acquaistungs Roll of LandSinvolun	Muhammad Yousef - Oth Tasleem Kauser Head of Household	S 2 After All Styde Manher Shah Fatherflusband Name	Nihan Settlement	Vulnerability Allowance	31,000 31,000 Structure Relocation Allowance	31,000 Shifting Allor	Shifting Allowar	57,000 57,000 Transitio		100,000 100,000 How	63,000 63,000 Servere Imp	Busines Allow	20,000 Electrici	2,006,000 2,609,000 Household Di	2,302,000	1 that impress out of the court	11-3 44 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	ا مال	عمران ما در الم	(Verfficon) Officer) Directo PEI	Z. be	Signal

Annexure-4: Community Consultation Meetings Report and Attendance Sheet of DPs Balakot Hydropower Project

	Community Co	onsultation Meet	ting Report		
111	andre en Fallenia	n -1		Date:	11-06-2024
area j	000 11 303	y mees	7 2-1	Locat e-	3112
		#E-0			
-the	moes	Ling watthe	chiff	eres	issues
Lowel	Poffme-	P. Varano	y vocas	4 Str.	co. Pure
				-	
				west.	ed them
				Care Inc.	The second secon
	- the dis	aled june 11 303. affected Con The more discovered i Low-of proffme- LVS out to The meety frees to re consulation with vailable DPS	aled june 11 3034, Much affected Community The meety with discovered i.e. Compan Low-of popponent, Valence LVS onet come. The meety The to Pees to received The companions and moso vailable DPS to received.	the miety with diff discount in a company with the discount in Company want of the meety The train it has been all their discount would be to received Their discount waitable pps to received the mailable pps to received the	aled June 11 3034, Muchig weld a offected Community with The The The meeting with different discussed i.e. Compensations of land Land poffment, valuable valuat of 5186

Balakot Hydropower Project Community Consultation Meeting Attendance Sheet

Name of Mouza: _	Paras.	Date:	11-06-2024
S. No.	Name	Contact No.	Signature
0	Syed-Rioz enal	0343-9626363	Que de la constante
0	aged umorabbas	0345-9075280	-U-ANG
3	eyes Rilal otheral		(B) Alfa
9	syed good that	0341-8824096	Dod
(3)	M. T.	0345-9685240	4 Star
3	syed Zwatiquer sud	0346-5842796	-Z-From
3	gred Zahow shul	0345-9675612	7 40
8	Sted Ritogaland	-0345-9669167_	- Pi show
9	syed prigshor	0334-6976417	Africal
0	gred midel	0343-5896792	العال
0	wager show	0348-8152897	
(1)	Asad Shoch.	0302-9567207	- A sed

		Balakot H	ydropower P	roject		
		Community Cons	sultation Mee	ting Report		
					D.	ate: 21-05-202
on Ma	421,2024	morning	oreld	WILE	-72re	appeared
	111	of mongo				15.0
200000	-	4	U			
10	The	meeting	Varyious	18 suca	wes	co discussed
WILE	The	enominity.	ic lar	A come	and m	m-land
Comp	ansalian	pogment	end 11	Is ont	Corre-	- 4.0
-the	teams	interm	1 76	formal	dom	mounify to
	and the second					5 8000 0S
		ubo infr		2317		
	rensativ					
		WALLES OF THE PARTY OF THE PART		01115	Pine	a oguerstan c
roll.	13	purpored.				
the	affects	vis agree	and	Sout	1 1	trat we
	6-6	ed our				
abo.			0			
1ha	team			1 76.	5250000	
11.0	(Chron	also i	31 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	1447	OFFICE	ess to Into

Balakot Hydropower Project Community Consultation Meeting Attendance Sheet

Name of Mouza:	Songar	Date:	1-05-202
S. No.	Name	Contact No.	Signature
a	m. Asig Ali	0345-9565264	AND
3	M- Farrige	0345-9752204	M. Taxiq
0	M. Bachir	0343-8911239	2 2
CP.	JamilAhnad	0342-5677607	Jaiole
0	General and and	0841-9380339.	- A :
0	UMOYDON	0343-2941219	وناهدا
3	Arstrad Knan	0841-8897211.	- AZP
3	Agerl Khan	0345-9085952	- Strel
0	Abdul Breken	0346-4619521	- Julie
		A CONTRACTOR OF THE PARTY OF TH	

Balakot Hydropower Project Female Community Consultation Meeting Report

medij en	eld with	The granule	Date: 04-66 2024.
270	y mouza		
	he meet		
	lie land		
report o	al comes.		
	- the DPS a		
	ion will some		
	e compansation		The second secon
	affectal. Th	TO SECURE A SECURE ASSESSMENT ASS	
	-pre area		
	at our m		
and word	formed 7hu and will r	coived the	furzlyg the
	The acquirem		

Balakot Hydropower Project Female Community Consultation Meeting Attendance Sheet

Date:

Name of Mouza:

04-06-2024

S. No. Name Contact No. Signature Gal Nosreen 0 0 Shochida 0245-9026390 0 Zaib-un-Nisa (3) Bibi Shafiqua 0846-9842720 3 Phili Zalda 0344 GREATER_ (3) Anihi Bascerell ---Ribi Ramida O 0 Publi Safoora 6345-9327723 @ Faib; Hilliam 3343-5856273

Annexure-5: Meeting Minutes and Presentation of IVS Consultants and GRC/Community Members

<u>Dissemination of Independent Valuation Report (IVS) to the Members of</u> Grievance Redress Committees and Community Members

Project: Balakot Hydropower Project (300MW)

 Venue:
 PIU Office Balakot

 Date:
 Friday. May 17, 2024

List of Participants:

19. Asif Ali:

Mr. Aziz Raza: Project Director BHPP-PIU-PEDO

2. Dr. Naveed Afsar: Deputy Director (Social & Resettlement). BHPP

3. Mr. Shareef-ud-Din: Deputy Director (Admin) BHPP

4. Muhammad Shoaib Anderson Consulting Pvt Ltd. (IVS Consultants

Briefed Virtually)

Mr. Ashfaq Khokar: ADB (Joined virtually)

Mr. Mushtaq Hussain: Institutional Support Specialist (ISS-ADB)
 Ibad Ullah: Assistant Resettlement Expert (PMC)

8. Wagar Ali Khan: Patwari BHPP

Ghulam Mustafa: GRC Village level Committee Member

(Ghanool)

10. Muhammad Tarig: GRC Village level Committee Member (Sangar) 11. Arshad Hussain: GRC Village level Committee Member (Sangar) 12. Muhammad Arshad: GRC Project level Committee Member (Sangar) 13. Syed Jabran Ali Shah: GRC Village level Committee Member (Paras) 14. Syed Tanveer Hussain Shah: GRC Village level Committee Member (Paras) 15. Syed Tahir Hussain Shah: GRC Village level Committee Member (Paras) 16. Syed ljaz Shah: GRC Project level Committee Member (Paras) 17. Syed Azhar Hussain Shah: Community Member/Affectee from Paras 18. Syed Husnain Shah: Community Member/Affectee from Paras

Member from Sangar.

Village Council Chairman & Community

20. Rizwan Hussain: Community Member/Affectee from Sangar

Summary of Key Discussions of IVS briefing


- 1. Project Implementation Unit (PIU) of Balakot Hydropower Project organized a hybrid meeting at PIU Balakot Office on May 17, 2024. The purpose of the meeting was to disseminate the results of the IVS report to the GRCs and community members of the affected villages. Project Director BHP welcomed the participants and invited the IVS expert to present the study findings. The meeting started at 11:00am and ended on 12:40pm. Attendance sheet of all participants is attached as annex 1 and photographs of meeting as annex 2. Summary of key discussions and views of GRC members on the IVS report are presented below:
- 2. The IVS consultant presented the IVS process and the valuation methodology. After collecting the already available data from the client, the consultant surveyed the field and considering the grievances of the community, they visited all the complainant's structures and the affected land. In order to consider all the issues raised by the complainants, all their structures were physically checked on site. After physical verification, data collection, proofs etc., the consultant started organizing and analyzing the data and office work as per their already set rules/policies and international standards.
- The IVS consultant further added that in resolving the complaints regarding rates of the land and non-land assets, the consultant take into consideration the following:
 - Merit of the complaints/case received for consideration
 - Evidences to take a decision on the complaint
 - Witness statements
 - Observations made on the field
- 4. After explaining the procedure of the valuation work of the Balakot Hydropower Project, the consultant presented each and every village overall differential to the available GRC members as well to the other community members who were physically present for the virtual briefing in the PIU-BHPP Office. The consultant also informed the participants that the LAC adopts a traditional practice of valuation which is used by them from the past years about the land and non-land assets, however the IVS consultant uses a different way of valuation of assets which is according to international practice and a gap between the prices of the LAC and IVS is identified if any.
- 5. He further explained that each and every case which was given to them by the PIU-BHPP to verify in the field was 100% checked and physically visited along with the presence of the GRC members/Affectees. After the briefing, the GRC members asked questions about the differential and showed their concerns if there are some deductions from the government side in the IVS report, on which the IVS consultant replied very clearly that the approved report is the one which is formulated by them and the same was approved by ADB and later the same was approved from the Government by the PIU-BHPP, PEDO. Which means that there is no decrease or any cutting from the client PIU-BHPP.

- 6. In addition to the above, Mr. Ashfaq from ADB clarified "full replacement costs" in light of SPS 2009, although some participants interpreted "replacement cost" according to their own perceptions which may not considered merely based on wish lists. ADB SPS required valuation by an expert and PEDO thankfully complied with it by engaging an accredited valuation expert to determine replacement cost. He thanked the IVS expert for explaining the valuation process to the participants in an easy-to-understand way further clarifying that the report has been reviewed by ADB and approved by the Government of KPK. Therefore, no further additions or amendments can be made to the report.
- 7. IVS expert also conducted a detailed due diligence of the awarded prices by crosschecking the rates with the real market value to work out any gaps in the "rates" for PEDO to consider bridging the gaps through top up payments to eligible APs. The consultant then informed all the participants that they found some gap in land rates which as per IVS is the differential and that this gap / difference can be filled by paying the differential amount which is given in the final summary.
- 8. After presenting the study findings and answering the questions of the GRC and community members, PD-BHP and the IVS expert asked them about their satisfaction of the valuation process. All GRC and community members thanked PIU for listening to their concerns and demands and taking them into consideration for practical solutions. They expressed satisfaction on the conduct of the study and its results. However, they requested PEDO/PIU and ADB for continued support and sympathetic approach to their concerns, even though some concerns may look childish.

Conclusion:

9. After the detailed presentation of the study findings and answering the questions of the participants, all the GRC and community members expressed their satisfaction on the study findings and they requested PIU for early release of payment of differential. The PD BHP clarified to them that payment of differential will be paid through the two "Addendums of LARP 1 and 2" after approval of the same by ADB. Payments will be made through the Land Acquisition Collector, Office of the Deputy Commissioner, Mansehra.

nexure 1: Attendance Sheet of the IVS Briefing Session





The IVS consultant briefing/ presenting the IVS study findings to the GRCs/ DPs/ community members.



The GRCs/ DPs/ community members listening the IVS consultant's presentation/ findings.



The GRC/ DPs/ community members participated in question-and-answer session from IVS consultants regarding study outcome.



The PD-PIU questioning from the IVS consultants.

Annexure-6: Meeting Minutes with Deputy Commissioner, District Mansehra

Minutes of Meeting Deputy Commissioner Mansehra June 13, 2023

A meeting with DC Mansehra and PIU staff took place at DC office, Mansehra. Everyone was welcomed by the chair for the subject meeting attended by the following officials of DC office Mansehra and PIU. Attendees in the meeting were:

- 1. DC Mansehra
- 2. ADC Mansehra
- 3. PD-PIU
- 4. DDS&R-PIU
- 5. Tehsildar Land Acquisition
- 6. Concerned Patwaris

The main discussions points and decisions taken were:

> Expedite the Payment of Compensation to DPs:

The DC Mansehra directed the revenue staff/ concerned Tehsildar to expedite the process of voucher preparation for all sorts of DPs compensation. Rectification of the names of any DPs as mentioned in acquaintance roll on priority basis. To facilitate and support the DPs at the time of voucher preparation regarding their affected land and non-land assets and khasra number as per the acquaintance roll.

> Completion of Payment of Public Built-up Properties and its evacuation:

The Deputy Commissioner also informed about the pending payment of built-up properties (public and communal) to the respective department and communities. Accordingly, the DC and ADC directed the revenue staff to complete the required anomalies and procedures and clear all the outstanding payment as soon as possible.

Payment of Meager Compensation Amount:

The DC Mansehra, informed about the regularly issued public notices in local newspapers and social media. The DC directed the revenue department relevant staff to mobilize all the DPs in each mouzas for receiving compensation and their allowances particularly focus on having meager compensation amount DPs. Also directed that the revenue staff to inform all the meager compensation DPs to recieve their due shares. The PIU staff ensure that regular support has been provided to the revenue staff which directly facilitate all DPs in terms of voucher preparation and requisite stationary for documentation.

Meeting ended with thanks to all participants.

Annexure-7: Advertisement in Newspaper, Public Notices and Social Media Link (Local Urdu Language)









1- Social Media Link:

- https://m.facebook.com/story.php?story_fbid=pfbid02SNjZLhhz4hduAfX4Rv1xBy44Q2zr2cUK6FDJiGMnhEdUepjL6sEKUaGZPPkhQBFnl&id=105565947734987
- 2- https://www.facebook.com/109105080449257/posts/pfbid0VTczQfDtKtrfTHdkKnHy8XT2v4TWjMcpsFhLUnWaYvJmjxg18YDDHRYWLCs15pXAI/?sfnsn=scwspmo.

Annexure-8: Information Brochure in Local Urdu Language for DPs

یکٹو تو اوانر کی ڈورپوشٹ آر گنائز کٹن (پیڈو) 300 میگاواٹ بالاکوٹ بن کلی تھر معاشر نی دماحو لیانی اثر ایت کے اقد عمامت کا خلاصد

مقومت قبير ويختر تواد ورويختر تواد الرق العطيات أنه تكوير تين (بدير) كدور اليه الدرائيس ويودت ويك (ADN) كدار التي ويودت ويك (ADN) كدار تواد التي ويودت ويك في المراق المر

- * تحلت عملی اور الفیاعی (عاقی) گیروی اگر ادامک برائے تحقیار عمل 2014 میں شرباط کے تعقیا کے تعلقہ کے تعلقہ کے تعلقہ کا معالی کا تعقیم کی تعقیم کی تعلقہ کا معالی کا معالی کے تعلقہ کا معالی کا معالی کے معالی کی گرف ہے کی معالی کے معالی کے معالی کے معالی کی معالی کے معالی کا اور معالی کی معالی کی معالی کے معالی کے معالی کے معالی کے معالی کے معالی کے معالی کی معالی کی معالی کے معالی کے معالی کے معالی کے معالی کے معالی کے معالی کی معالی کے معالی کی معالی کے معالی کی معالی کے معالی کے معالی کی معالی کے معالی کی معالی کے معالی کی الدی معالی کے معالی کی معالی کے معالی کی معالی کے معالی
- فائلة يود كالم كريست ب كالحمل كي و في كريس كال عن التعاليد و كدار ال الله في طرف معان كريسة و كر
- خوال بادرا تقلب قرار در کے دیکی آن در میں بازیاج ہے گئے ہا انظمی پر مصنی و گاہؤ کر مطابق مقدار میں بیانی کو زوری آن ہے کا اس میں دائیمٹر او کیا گئی میرچوز کی کا ایک گیٹ دیاج ہے گا۔
- ا مع من المحافظة على مرتف يده يعشر كون في مرتف هد كر الحس كالميان 1373 منز به كراه 154 كيدك. - يان ك الزون كرالية بين كان كار

محسوب کی کی قاص موصوصات الحیل میں بائی دیادہ سے زیادہ او کی گئے مستدر سے 1289 میٹر دو گاہ اس کے سے کمانی کی مندر سے دیالا اسٹر ہوگا۔ محمل کے بعد ہرے وجیانت 2000 میگا اس فلی روز آئر گاہ ہے کہ 55 سال میں اوسطان (1143 کا ایس میں قبال کی بیدائی بائی کے کمیل سے درجہ کا افران بر سال موسم کرد کے محمول میں کہو ہے کہ جانب در بائی بائی کی مقدار 154 کیا ہے ہے ہو۔ اور جب بائی کا برو کم بر گاہ آئر دو تھ کی کیا ہو اپنی گئی کی بیداداد اور پائی بائر قرار کالے کہا استعمال کیا ہے کا

- م نو النام کا حسول او اس کے لئے تقریبے 224 انگر زنگان کی طرورت ہوگی جس عمیا ہے 118 انگر کھیل اور انگر کھر کیا گئے ہوئے 135 انگرز نامی پروجیات کے دیگر قبیرات اشول انگانے کا دی اور دیلے موکول کے لیے مجتمع کیا گیا ہے۔ طریع میر کہ بور مواد خسرور اگف والا بھے مشابان کیا ہے۔ اس مشہبان شدہ مواد ہے بھی کی چش کا اگر ہے) کو بورائرے کیسے پیڈو کرا ہے۔ انگ لیل کی جانب سے ایک آزاد و بابی تورز کی شرور سے کی جلگ گا۔

💠 مندرجه الحي الاولس مناثرين كوديا كيليه _

اكائى تىت	قم	16/2
63,000	(Cut-whealth elementum) が別じななな	731
31,000	رُعَا يُنِ لِنَّالِ الْكُوْلِ (Saucture Helioceson Allowanoe) الْعَالِي الْكُوْلِ الْكَالِيَّةِ الْكَا	.2
21,000	العربي المنظني (Abiling Alexanderia Houses)	3
31,000	كاروردكي والمناتج والمنظل (Commercial Structure Strilling)	.4
57/000	تتعلق الأشي (Trans tion All awards)	.5
62,000	كالدويركي فتحل التكاشى ومصاحبته بالمصادرة بالمصادرة المتعادية	.6
100,000	مالتی کے دوران کھرکے کرانے کی شر درمت (House Fee-1)	.7
62,000	(Severa Project Alexander) グルムデ	.8
50,000	12 أنتون كـ في كالدون والأناف الاستان كالمساور	.9
20,000	المجي (Bootic ty Al ostarios) مجي (Ce ²	.10
2,000,000	سیر پلوچنتی کرچ خیالااو کس (c.sehok: Dakomon Aksemos) : سید (c.sehok: Dakomon Aksemos)	.11

محمی محی شایات کی صورت شروعت در به زنبل دخانه که بینته قول نیمرو (شایات تال) کینی مجر ان سے دامید اگر مکن این -

يراجكك فالزيكتر

ح اجَيَاتُ المَهِيَّمِنْتِيثُنْ بُونِتْ يَيْدُهُ بِاللَّاكِيثِ ، عَلَمِيالْسِرُهُ

ير الطعند (من يو مندي يورسوالا

أون أجر: 4-360003 - 1997

ولاكوت بالجارد فاورير اجبكت

يرا البيك مينجرت كنسليش بالأكوث إقراد بإدري البيكت والأكوت، طلح السود فون تهر: 6-155-1607

Annexure-9: Notifications of Allowances Disbursement Committee at LAC/ PIU



OFFICE OF THE DEPUTY COMMISSIONER / LAND ACQUISITION COLLECTOR MANSEHRA



No. 1401

_/BHPP/Acq/DC(M)

Dated__15_/09/2022

NOTIFICATION.

A committee consisting of the following is hereby constituted to make payment of the LARP amount to all concerned. The LARP amount is being shifted through Treasury Voucher to the ADC(G), Mansehra for further course of action.

- 1. Additional Deputy Commissioner (G), Mansehra. ----- Chairman
- 2. Mr. Naveed Afsar, Deputy Director (S&R), BHPP ------- Member
- 3. Mr. Ibadullah, Assistant Resettlement Expert, PMC ----- Member

TORs.

- 1. The concerned beneficiaries of LARP shall be informed properly.
- The committee shall make payments according to the record to rightful owners.
- 3. Proper record and cash book of the payments be maintained.
- Utmost care be adopted while making payment to avoid payment especially in cases where status quo is involved.
- 5. Reconciliation of payment.
- Consolidated reports be submitted to the undersigned.

Deputy^l Commissioner/ Land Acquisition Collector Mansehra

No. 1402-08 /BHPP/Acq/DC(M)

Copy forwarded to:-

The Sectary Energy & Power Department Govt. of Khyber Pakhtunkhwa, Peshawar.

The Commissioner Hazara Division, Abbottabad.

The Secretary Board of Revenue Khyber Pakhtunkhwa, Peshawar.

4. The Project Director, Balakot Hydro Power Project, PEDO, Peshawar.

5. The District Accounts Officer, Mansehra.

6. All concerned.

Deputy Commissioner/ Land Acquisition Collector Mansehra

Annexure-9: Notification of Allowances disbursement committee at LAC/ PIU

OFFICE OF THE DEPUTY COMMISSIONER / LAND ACQUISITION COLLECTOR MANSEHRA

1448 /BHPP/Acq/DC(M)

Dated 20 /09/2022

ORDER.

Additional Deputy Commissioner (G), Mansehra is hereby authorized to sign treasury vouchers under Central Treasury Rules 142 pertaining to the LARP payment to the concerned beneficiaries of Balakot Hydro Power Project belonging to "Mouza Ghanool & Sangar" in respect of the amount worth Rs. 59,565,000/- (Fifty Nine Million Five Hundred Sixty Five Thousand Rupees Only) received through Cheque No. 47789712 dated 23-08-2022 from the Government of Khyber Pakhtunkhwa, Pakhtunkhwa Energy Development Organization (PEDO) vide their letter No. PEDO/PD/BHPP/2022-23/848-51 dated 23-08-2022 and deposited Under Head G-11215 Revenue Deposit vide deposit No. 182 dated 19-09-2022, in National Bank Main Branch, Mansehra.

Payment shall be made accordance with the TOR's laid down in this office Notification No. 1401/BHPP/Acq/DC(M) dated 15-09-2022.

Deputy Commissioner/ ` Land Acquisition Collector Mansehra

No. 1449 - 1455 /BHPP/Acq/DC(M)

Copy forwarded to:-

- 1. The Sectary Energy & Power Department Govt. of Khyber Pakhtunkhwa, Peshawar.
- 2. The Commissioner Hazara Division, Abbottabad.
- 3. The Secretary Board of Revenue Khyber Pakhtunkhwa, Peshawar.
- 4. The Project Director, Balakot Hydro Power Project, PEDO, Peshawar,
- The District Accounts Officer, Mansehra w/r to his letter No. 5497-5506 dated 20-05-2022 alongwith specimen signature of the Additional Deputy Commissioner (G), Mansehra.
- The Manger National Bank of Pakistan (Main Branch), Mansehra alongwith specimen signature of the Additional Deputy Commissioner (G), Mansehra.

7. All concerned.

Deputy Commissioner/ Land Acquisition Collector Manschra

Annexure-10: Notifications of Grievances Redressal Committees



PEDO

PAKHTUNKHWA ENERGY DEVELOPMENT ORGANIZATIO

Government of Khyber Pakhtunkhwa Peshawar

Energy & Power Department



Dated Peshawar the 12/01/2023

NOTIFICATION

No.1306/PEDO/PD Balakot HPP/. The Competent Authority is pleased to notify the following Grievances Redressal Committee (GRC) at village level for Paras (300 MW Balakot Hydropower Project, District Mansehra) for implementation in its true letter & spirit.

The Village level GRC composition is as under;

S. No	Name/Designation	Role in the Committee
1	Deputy Director (Social & Resettlement), PIU, BHPP	Chairman
2	Deputy Director (Environment, Health, Safety & Gender), PIU, BHPP	Member
3	The Resettlement Expert, PMC, BHPP	Member
4	Patwari, Mouza Paras	Member
5	Syed Tanveer Alam Shah S/o Syed Muzamil Shah	Member
6	Syed Jabran Shah S/o Syed Imdad Hussain Shah	Member
7	Syed Tahir Hussain Shah S/o Syed Noor Hussain Shah	Member

Project Director Balakot HPP, PEDO, Peshawar.

Copy Forwarded for Information to;

- 1. The Chief Engineer (Development /Plan) PEDO, Peshawar
- 2. The Deputy Commissioner, Mansehra
- 3. The Assistant Commissioner, Balakot
- 4. PS to CEO PEDO, Peshawar
- 5. The Principal Energy Specialist, CWEN, ADB
- 6. The Team Leader, PMC, BHPP
- 7. Members concerned

Project Director Balakot HPP, PEDO, Peshawar.

Annexure-10: Notification of Grievances Redressal Committees (GRCs)



PEDO

PAKHTUNKHWA ENERGY DEVELOPMENT ORGANIZATION

Government of Khyber Pakhtunkhwa Peshawar

Energy & Power Department

Dated Peshawar the 15/09/2022

NOTIFICATION

No.876-83/PEDO/PD Balakot HPP/. The Competent Authority is pleased to notify the following Grievances Redressel Committee (GRC) at village level for Sangar & Ghanool (300 MW Balakot Hydropower Project, District Mansehra) for implementation in its true letter & spirit.

The Village level GRC composition is as under:

S.No.	Name/Designation	Designation
1	Deputy Director (Social & Resettlement), PIU, BHPP	Chairman
2	Deputy Director (Environment, Health, Safety & Gender), PIU, BHPP	Member
3	The Resettlement Expert, PMC, BHPP	Member
4	Patwari, Mouza Sangar	Member
5	Patwari, Mouza Ghanool	Member
6	Mr. Ghulam Mustafa (Community Member, Mouza Ghanool)	Member
7	Mr. Arshad Khan (Community Member, Mouza Sangar)	Member
8	Mr. Muhammad Tariq (Community Member, Mouza Sangar)	Member

Copy Forwarded for Information to:

1. The Chief Engineer (Development /Plan) PEDO, Peshawar

The Deputy Commissioner, Mansehra

3. The Assistant Commissioner, Balakot

4. PS to CEO PEDO, Peshawar

5. The Principal Energy Specialist, CWEN, ADB

6. The Team Leader, PMC, BHPP

7. Members concerned

Project Director Balakot HPP. PEDO, Peshawar.

Project Director Balakot HPP. PEDO, Peshawar.

Annexure-10: Notification of Grievances Redressal Committees (GRCs)



PEDO

PAKHTUNKHWA ENERGY DEVELOPMENT ORGANIZATION Government of Khyber Pakhtunkhwa Peshawar

Energy & Power Department



Dated Peshawar the 26/09/2022

NOTIFICATION

No.920/PEDO/PD Balakot HPP/. The Competent Authority is pleased to notify the following Grievances Redressal Committee (GRC) at village level for Bela Sacha (300 MW Balakot Hydropower Project, District Mansehra) for implementation in its true letter & spirit.

The Village level GRC composition is as under;

S. No	Name/Designation	Role in the Committee
1	Deputy Director (Social & Resettlement), PIU, BHPP	Chairman
2	Deputy Director (Environment, Health, Safety & Gender), PIU, BHPP	Member
3	The Resettlement Expert, PMC, BHPP	Member
4	Patwari, Mouza Bela Sacha	Mcmber
5	Syed Anwar Ulhaq Shah S/o Aziz Ud Din Shah	Member
6	Syed Hasnain Ali Shah S/o Munir Hussain Shah	Member

Project Director 26 Balakot HPP, PEDO, Peshawar.

Copy Forwarded for Information to;

- 1. The Chief Engineer (Development /Plan) PEDO, Peshawar
- 2. The Deputy Commissioner, Mansehra
- 3. The Assistant Commissioner, Balakot
- 4. PS to CEO PEDO, Peshawar
- 5. The Principal Energy Specialist, CWEN, ADB
- 6. The Team Leader, PMC, BHPP
- 7. Members concerned


Project Director Balakot HPP. PEDO, Peshawar.

Annexure-11: Statement of Satisfaction Certificates (IVS and LARP Allowances) of the Complainants

اطميتان كابيان

05/06/2024/BJB

جیلہ کمیلیں مہر ان QR (ویلیج ویر اجکے)، میر ان ویلی کو نسل موضع پارس بیان کرتے ہیں کہ حال ہی بین شائع ہوئے وال 200 مردے کی راہد رہے یہ ہم سطمتن ہیں اور بال کوٹ حائیہ روز اجکے کی افکام سے ہے جد مطلور ہیں کہ جمہوں نے استد کم حرصے بین طیر جانیہ او مردے کر واکر جارے تصدان کا از ارکیا۔ اور ہم مستشل ہیں ہی پر اجکے انتہامے سے ایسے ہیں افکام سکوک کی قواقع اسکے اور ہم جملہ میر ان بات کا بھین والے ہے اور موسم کرتے ہیں کہ قولی اجبت کے مائل اس پر اجکیٹ کو ہم فی جمل کر کا میاب کر واکیل میں۔ اور جم بھی مسائل مستقبل ہیں آخی کے فی وجے کے مل کر بیک افغان اللہ



اطمينان كابيان

05/06/2024/もん

ہم جلہ کمیشیں میران CRC (ویلیج و پراجیکٹ) بمبران ویلی کو نسل موسع پارس بیان کرتے ہیں کہ مسئک اندب الاؤنسسز (برنس وچ لبا ودیگر) موقد پر ہماری موجود کی ہیں تصدیق کو کرچ است تیار کی اس پر ہم کھل طور پر سلمٹن ہیں اور بالاکوٹ ھاکیل ویا ویکٹ کی انتظامیہ کے بے مدمنگلوراود عشر کراد ہیں کہ جنہوں نے بڑی واریک چی اور سپائی ہے مسئک ادب الاؤنسسز الحدیق کر واکر جاری شکایات کا ازالہ کیا۔ اور ہم مستقبل ہی مجی پر اجیکٹ افتا میں۔ ایسے بی استھے بر تا واسلوک کی آئی رکھتے ہیں۔

اور بم جملہ عمیران اس بات کا بھین دانہ ہے ہیں اور عزم کرتے ہیں کہ قوی اجیت کے حال اس پر انتکٹ کو ہم ال جل کر کامیاب کرواکیں گے۔ ۔ اور ہو بھی مسائل مستقبی جیں انجیں کے انجیل فی جھے کے طل کر چھے۔ افشاءات



Annexure-12: Skilled and Un-Skilled Employment by Contractors/ PIU

S. No	Name	Position	CNIC Number	Address
5. NO	Bakir Shah	Driver	13503-9770772-3	Mansehra tehsil&Distric Mansehra
2	Sabir Hussain	Driver	13503-6921680-7	Mansehra tehsil&Distric Mansehra
3	Nazir Hussin	Excavator Operator	13501-9663886-9	mahandri jarad balakot Mansehra
4	Ata Ur Rahaman	Cook	13501-9043036-5	Paris tehsil Blakoat Distric Mansehra
5	M Mushtaq	Cook	13501-0320501-1	Shawal Tehsil Balakoat Distric Mansehra
6	Usama	Electration	13501-2369583-7	Garlat at tehsil Balakoat Distrci Mehnsara
7	Siddique	Cook	13501-7407076-1	BalakoatTehsil Balakoat Distric Mansehra
8	Baber	Loader Operator	13501-9172387-5	Kholian Thesil Balakot Dristric Mansehra
9	Zaheer Abbas	Mechanic	13501-1714997-7	Balakot tehsil balakot Distric Mansehra
10	Zahid Hussain	Electrician	13501-7584783-1	Balakot tehsil balakot Distric Mansehra
11	Manzhar Abbas	Mechanic	13501-1299188-5	Balakot tehsil balakot Distric Mansehra
12	Danish Khan	Mechanic	13501-6657642-5	Balakot tehsil balakot Distric Mansehra
13	M Riaz	Machanic	13501-4552156-9	Balakot Fridabad tehsil Balakot Distric Mansehra
14	M Umair	Loader-operator	13501-2733966-9	kholian tehsil balakot Distric Mansehra
15	Muneer	Dozer Operator	13503-1009122-7	Jba tehsil and Distric Maansehra
16	Waqas Imtiaz	Machanic	13501-1079796-9	Nara tehsil Balakot Distric Mansehra
17	Zeshan	Mechanical Electration	13501-4975091-5	Garlat at tehsil Balakoat Distrci Mehnsara
18	Ali Shan	Loader Operator	13501-1093253-5	Kahghan tehsil Baalakot Distric Mansehra
19	M Shafeeq	Foreman	13501-8009061-9	Kholian Thesil Balakot Dristric Mansehra
20	M Sharif	Cook	13501-8938509-5	Kholian Thesil Balakot Dristric Mansehra
21	Ab Ghafoor	Mason	13501-1293818-1	Kholian Thesil Balakot Dristric Mansehra
22	Mir zaman	Mason	13501-1291194-3	Kholian Thesil Balakot Dristric Mansehra
23	M Farooq	Mason	13501-8635934-7	Kholian Thesil Balakot Dristric Mansehra
24	Saeed Ur Rahman	Carpenter	13501-6266139-5	kholian tehsil balakot Distric Mansehra
25	M Imran	Steel fixture	13501-6070825-7	kholian tehsil balakot Distric Mansehra
26	M Maskeen	Carpenter	13501-6080139-1	kholian tehsil balakot Distric Mansehra
27	M Mukhtair	Carpenter	13501-9364117-3	kholian tehsil balakot Distric Mansehra
28	Ab Basit	Carpenter Mason	13501-3576051-7	kholian tehsil balakot Distric Mansehra
30	Nazeer Hussain Ab Latif	Mason	13501-7268603-9 13501-1346629-7	kholian tehsil balakot Distric Mansehra kholian tehsil balakot Distric Mansehra
31	Mumtaz Ahmed	Steel fixture	13501-1340029-7	kholian tehsil balakot Distric Mansehra
32	M Faisel	Ex operator	13501-9993094-7	Balakot tehsil balakot Distric Mansehra
33	M Abbas	Loader Operator	13501-0485684-5	Ghanool tehsil balakoat Distric Mansehra
34	Yasir Hussain	Loader Operator	13501-3028584-7	Balakoat tehsil Balakoat Distrci Mehnsara
35	Ab Aziz	Dumper Driver	13501-8648675-5	Boonja tehsil Balakot Distric Mansehra
36	Rafaqat Hussain	Dumper Driver	13501-1295682-5	Juraid tehsil Balakot Distric Mansehra
37	Mumtaz	Loader Operator	13501-1311192-3	Balakot tehsil Blakot Distric Mansehra
38	Jawad	Welder	13501-2306530-3	Balakot tehsil balakot Distric Mansehra
39	Kashif Rasheed	Welder	13501-5585416-7	Ghanool tehsil Balakot Distric Mansehra
40	Faisel Zaib	Welder	13501-5546215-7	Balakot tehsil balakot Distric Mansehra
41	M Rafique Bahdir Ali	Welder	13501-4313929-1	Balaakot Distric Mansehra Balaakot Distric Mansehra
42	Tariq Aziz	Welder Loader Operator	13501-1339333-9 13501-0553067-3	Ghanool tehsil Balakoat Distric Mansehra
44	Shah zaib	LTV Driver	13503-7848964-1	Kaghan Tehsil Balakoat Distric Mansehra
45	Ab Jabar	Electrician	13501-6180521-7	kholian tehsil balakot Distric Mansehra
46	Qamar Ul Islam	Welder	13501-1283135-5	kholian tehsil balakot Distric Mansehra
				Narrah Balakot Tehsil Balaakot District
47	Israr Ahmed	Driver	13501-5603647-1	Mansehra
48	Naveed Ahmed	Driver	13501-6109656-9	Dhano Mahandri Tehsil Balakot Districtc Mnasehra
49	Muhamad Ashraf	Driver	13501-7346950-9	Ghanool tehsil Balakot district Mansehra
50	Ghulam Mujtaba	Driver	13501-9389012-9	Dabrian Balakot District Mansehra
51	Muhammad Banaras	Driver	13501-8461345-1	Ghanool tehsil Balakot district Mansehra
52	Shams Ul Islam	Elictrician	13501-5076718-9	Shohal Mazullah tehsil Balakot District Mansehra
53	Zeeshan Javed	Elictrician	13501-4975051-5	Garlat Balakot tehsil Balakot District Mansehra
54	Muhammad Ashfaq	Mechanic	13501-5718176-1	Bhangian Tehsil Balakot District Mansehra
55	Muhammad Asif	Store keeper	13501-2438134-7	Ghanool tehsil Balakot district Mansehra
56	Muhammad Rafaqat	Excavator oprerator	13501-4228123-9	Sangar Tehsil Balakot District Mansehra
57	Ahtisham Khan	Excavator oprerator	13501-8153159-1	p/o Mahandri tehsil Balakot District Mansehra
58	Asad Dildar	Excavator oprerator	13501-4907976-9	Sangar Tehsil Balakot District Mansehra
59	Muhammad Sajjad	Mechnic	13501-1345689-3	Ghanool tehsil Balakot district Mansehra
60	Usama	welder	13501-4422057-5	Paras tehsil balakot district mansehra
61	Muhammad Umar	Elictrician	13501-9420012-3	Ghanool tehsil Balakot district Mansehra
62	Bilal Ahmed	Mehcanic	13501-4717760-1	Narah Balakot Garlat disytict Mansehra

		T =	0.110.11	T
S. No	Name Mugadaa Apwar	Position	CNIC Number	Address
63	Muqadas Anwar	Driver	13501-7087924-1	Jaraid tehsil balakot district mansehra
64	Muhammad Tabsheer	Jambo Operator	13501-3677724-5	Ghanool tehsil Balakot district Mansehra
65	Muhammad Jameel	Driller	13501-7093021-7	Kholian tehsil Balakot District Mansehra
66 67	Jabbar Noor Zaman Banish Khan	Driler welder	13501-6543476-1 13501-6557642-5	Ghanool tehsil Balakot district Mansehra Balakot tehsil Distric Mansehra
68	ZAHEER ABBAS	welder	13501-0357642-5	Balakot tehsil Distric Mansehra
69	ZIAFAT UMER	Driver	13503-4672916-3	Jareed tehsil balakot district mansehra
70	WASEEM AHMED	Mason	13501-3348115-1	Mangli Tehsil Balakot District Mansehra
71	TOUSEEF AHMED	driver	13501-2246549-3	Sangar Tehsil Balakot District Mansehra
72	Amir Hussain	cok	13501-8406409-5	Paras tehsil balakot district mansehra
				Village Narra tehsil balakot district
73	Mukhtiar Ahmed	Loader Oprerater	13501-1311102-3	mansehra
74	Tanveer Ahmed	Carpenter	13503-4111970-7	Phagal Mahandri Tehsil Balakot District Mansehra
75	Muhammad Waqas	Carpenter	13501-4828060-1	Ghanool tehsil Balakot district Mansehra
76	Syed Kamil Hussain sh	Driver	13501-5693206-3	Bari Paras tehsil Balakot District Mansehra
77	Abdul Qadeer	Driller	13501-0821896-5	Mahandri tehsil Balakot District Mansehra
78	Syed Yakhya Ali	Driller	13501-5284209-5	Paras tehsil balakot district mansehra
79	Naeem Rafique	Driller	13501-0511645-1	Jabbian Kghan Tehsil Balakot District Mansehra
80	Muhammad Idrees	Short creat Operator	13501-3078183-9	Banda Manoor Kghan Tehsil Balakot District Man
81	Muhammad Anwar	Short creat Operator	13501-1299689-5	Banda Manoor Kghan Tehsil Balakot District Man
82	Azhar Mehmood	Repair Man	13501-1272401-5	doseri p/o Kaghan tehsil Balakot D Mansehra
83	Mehtab Hamayun	Steel Fixer	13501-6425946-3	Garlat Balakot District Mansehra
84	Kafeel	shortcrete opt	13501-8501646-5	Bela Kaghan Tehsil Balakot District Mansehra
85	Abdul Saboor	Driver	13501-5341883-1	Sangar Tehsil Balakot District Mansehra
86	Usama	Welder	13501-6849883-7	Dabrian Sangar Tehsil Balakot District Mansehra
87	Muhammad Junaid	Welder	13501-9595099-3	Kewai tehsil balakot district mansehra
88	Syed Abdullah Shah	Welder	13503-2897862-3	Attarshisha Tehsil District Mansehra
89	Azhar Hussain	Welder	13501-8534201-5	Hangrai Tehsil Balakot District Mansehra
90	Shafqat Rasheed	Welder	13501-7792660-9	Ghanool tehsil Balakot district Mansehra
91	Muhammad Niaz	welder	13501-3144776-5	Balakot District Mnsehra
92	Waqar Ahmed	cook	13501-7337496-3	Lasan Kewai Tehsil Balakot District Mansehra
93	Waqar Ahmed	Dumper Driver	13501-3451667-5	Muzafrabad Shaheed Gali
94	Muhammad Munir	Dozer Operator	13501-1009122-7	Jaba p/o Sheep Fom District and Tehsil Mansehra
95	Syed Mehar Ali Shah	Crane Operator	13503-1903741-1	p/o Hado bandi tehsil and district mansehra
96	Sajid	Driver	13503-0634880-1	Darmiani P/O Ogra Mohanian tehsil Mansehra
97	MUKHTIARAHMED	welder	13501-6471708-5	Paras tehsil balakot district mansehra
98	Khizer Hayyat	Welder	13501-8686815-7	Sehri Post Office Khas Dabryian Sanghar
99	Nazakat	Electrician	13503-2116737-9	Sanghar tehsil Balakot Mansehra
100	Rafaqat Shah	Driver	13501-9621191-7	Sanghar Tehsil Balakot District Mansehra
101	Muhammad Waqas	Driver	13501-1216380-9	Sehri Post Office Khas Dabryian Sanghar
102	Adbul Sahboohk	Driver	13501-1303300-1	Sehri Sanghar Post Office Dabriyan
103	Naeem Afzal	Loader Oprater	13501-2047191-9	Sanghar Tehsil Balakot District Mansehra
104 105	Shujait Khan Muhammad Ismail	Exvator Oprator	13501-9641397-1	Sanghar Tehsil Balakot District Mansehra
105	Hamza Awar	Exvator Oprater Driver	13501-3382139-3 13501-1840361-7	Sehri Post Office Khas Dabryian Sanghar Sangar Tehsil Balakot District Mansehra
106	Muhammad Awair	Driver	13501-1640361-7	Sanghar tehsil Balakot Mansehra
107	Ageel Ahmed	Loader Operator	13501-1349071-1	Kiwai Tehsil Balakot District Mansehra
109	Muhammad Awais	Exvator Oprater	13501-8262418-9	Kiwai Tehsil Balakot District Mansehra
110	M Niasier	B.Operator	13501-3469077-1	Narah Balakot Garlat disytict Mansehra
111	Sabir Hussain	B.Operator	13501-3249285-3	Sanghar tehsil Balakot Mansehra
112	Syed Husnain	B.Operator	13501-9315648-7	Sanghar tehsil Balakot Mansehra
113	M SAEED	B.Operator	13501-5694973-3	Paris tehsil Balakoat Mahnsara
114	Arshad	Electration	13501-6832153-3	Sangar Tehsil Balakot District Mansehra
115	Hamza Jahan	Excavator oprerator	13501-4759030-5	Narah Balakot Garlat disytict Mansehra
116	Muhammad Abbas	Mechanic	13501-1471712-7	Sangar Tehsil Balakot District Mansehra
117	Faiz Muhammad Khan	Mechanic	13501-1316486-1	Sangar Tehsil Balakot District Mansehra
118	Safdar Hussain	Mechanic	13501-6699944-7	Paris tehsil Balakoat Mahnsara
119	Muhammad Asif	Mixer Driver	13501-1348378-9	Paris tehsil Balakoat Mahnsara
120	Sohail Habib	Loader Operator	13501-5017011-5	Paris tehsil Balakoat Mahnsara
121	Sheraz Ahmed	Dumper Driver	13501-2745302-1	Paris tehsil Balakoat Mahnsara
122	Saqib Hussain	Dumper Driver	13501-3209034-1	Sangar Tehsil Balakot District Mansehra
123	Saeed Ahmed	Dumper Driver	13501-8150025-5	Sangar Tehsil Balakot District Mansehra

S. No	Name	Position	CNIC Number	Address
124	Aamir Sharil	Loader Operator	13501-6468237-9	Paris tehsil Balakoat Mahnsara
125	Ahzaz Shah	Loader Operator	13501-0485515-9	Sanghar tehsil Balakot Mansehra
126	Abdul Waheed Shah	Dumper Driver	13501-9435856-1	Sehri Post Office Khas Dabryian Sanghar
127	Ishtiaq Ahmed	Driver	13501-4348784-1	Sangar Tehsil Balakot District Mansehra
128	Basharat Shah	Dumper Driver	13501-2460512-9	Sanghar tehsil Balakot Mansehra
129	Saqib Alam	Jambo Operator	13501-0468957-3	Kiwai Tehsil Balakot District Mansehra
130	Shoaib Ismail	B.Operator	13501-1557071-7	Kiwai Tehsil Balakot District Mansehra
131	M Tayyab	B.Operator	13501-8858205-9	Kiwai Tehsil Balakot District Mansehra
132	M Rafi	Site Safety officer	13501-8865492-3	Sangar Tehsil Balakot District Mansehra
133	Sha Fahat	Mason	13501-1334255-1	Paris tehsil Balakoat Mahnsara
134	Waqar Shah	General Management	13501-6514060-3	Paris tehsil Balakoat Mahnsara
135	Riaz Hussain	Mason	13501-6415466-9	Sangar Tehsil Balakot District Mansehra
136	Syed AbBasif	General Management	13501-4983583-7	Paris tehsil Balakoat Mahnsara
137	Jamil Shah	Mason	13501-6680598-3	Paris tehsil Balakoat Mahnsara
138	Saleem Shah	Mason	13501-5830027-9	Paris tehsil Balakoat Mahnsara
139	ANWAR SHAH	Mason	13501-5392089-3	Sangar Tehsil Balakot District Mansehra
140	Usman Ali	Dumper Driver	13501-2684900-5	P/o Ismail Ababd Tehsile, Balakot District Mansehra
141	Abdul Qadeer	Dumper Driver	13501-2781277-5	P/o Ghanool Tehsile, Balakot District Mansehra
142	Amir khan	Dumper Driver	13503-3275629-1	P/o Elahi mang Shankiyari District Mansehra
143	M. Mumtaz	Dumper Driver	13501-2490651-5	P/o Sanghar Tehsile, Balakot District Mansehra
144	Tanveer Hussain	Dumper Driver	13501-1034328-3	P/o Ghanool Tehsile, Balakot District Mansehra
145	Baser Khan	Dumper Driver	13501-1344190-5	P/o Ghanool Tehsile, Balakot District Mansehra
146	Ilyas Tanveer	Dumper Driver	13501-1317196-5	P/o Ghanool Tehsile, Balakot District Mansehra
147	Sajid Ali	Dumper Driver	13501-7452306-9	P/o Ghanool Tehsile, Balakot District Mansehra
148	Abdul Jabbar	Dumper Driver	13501-1285387-3	P/o Jigloot Tehsile, District Kohistan
149	M. Asif	Dumper Driver	13501-4011104-3	P/o Ghanool Tehsile, Balakot District Mansehra
150	Nissar Hussain Shah	Masson	13501-1652968-7	Dub Paras tehsil Balakot Mansehra
151	Wazeer Muhammad	Carpanter	13501-9690810-1	Noori Bhoanja Post Office Fareed Abbad
152	Muhammad Hussain	Cook	82502-8349069-5	Kiwai Tehsil Balakot District Mansehra
153	Abid Hussain	Cook	13501-8173565-5	Village Jabri Tehsil Balakot District Mansehra
154	Kabir	HTV Driver	13501-8720748-3	Sanghar Tehsil Balakot District Mansehra
155	Shahid	HTV Driver	13501-8173795-1	Sanghar Tehsil Balakot District Mansehra
156	Salamat Ali	Excevator Operator	13501-9174947-3	Sachan, Sanghar
157	Qadir	Excevator Operator	13501-4402320-7	Nori Bhonja, Sanghar
158	Muhammed Farooq	Mechanic	13501-0133544-9	Barri, Sanghar
159 160	Abdul Qadir Nisar Hussain Shah	HTV Driver	13501-1571212-3 13501-1652968-7	Village Sanghar
161	Shabir Ahamd	Sub-Contractor HTV Driver	13501-1652966-7	Paras Sangar
162	Muhammad Billal	Excavator operator	13501-1352442-3	Sangar
163	Muhammad Shafeeq	LTV Driver	13501-6853158-9	Sangar
164	Malik aman	LTV Driver	82203-4006037-7	Balakot
165	shabir hussain	LTV Driver	13501-1311893-7	Sangar
166	Muhammad Rafaqat	Loader Operator	13501-7713574-5	Kappi Galli
167	Naseer Hussain	Excavator operator	13501-7527301-3	Sangar
168	Muhammad Waseem	LTV Driver	13501-4275006-5	Kewai
169	Salamat Ali	HTV Driver	13501-326367-9	Village Sangar
170	Khizer Ali	Excavator O.P.T	13501-7264011-9	Sanghar
171	Shujat Ali	Store Assisstant	13501-9778780-7	Sanghar
172	Haq Nawaz	Loader Operator	13501-9348300-9	Balakot
173	Abdul Sabooh	Transit Mixer Driver Batching Plant	13501-5094490-5	Kiwai P/O Atar Sheesha Reerh Tehsil & District
174	Muhammad Zaheer	Operator	13503-3074254-1	Mansehra
175 176	M. Rahmat M. Sajid	Capenter Supervisor	37405-1770539-3 13501-2531161-7	Sangar Sangar
176	M. Shahbaz	Capenter	13501-2531161-7	Sangar
177	Kafeel Ahmad	Masson	13501-1348524-3	Sangar
178	Bahadar Khan	Mason	13501-4974224-3	Balakot
180	Aziz Ahmad	Mason	13501-1346800-1	Balakot
181	Waqas Nisar	Mason	13501-2279949-5	Balakot
182	M. Akram	Supervisor	3501-7096127-5	Balakot
183	Nazeer Hussain	Mason	13501-1312951-5	Balakot
184	Ghulam Hassan	Mason	13501-3853957-7	Sangar
				

S. No	Name	Position	CNIC Number	Address
185	Ghulam Sarwar	Foreman	13501-1325623-3	Sangar
186	Muhammad Sohaib	Driver HTV	61101-1810564-3	Sanghar Tehsil Balakot District Mansehra
187	F0\0/07	Tractor Loader Driver	13503-3676430-9	Muhalla Kalhary Gharbi Baffa Town Tehsil &
	Fayyaz			District Mansehra
188	Abdul Sattar	Driver HTV	13501-3208656-1	Phagal Tehsil Balakot District Mansehra
189	Saif ur Rehman	Driver HTV	32303-2262755-1	Dabriaan, Sanghar Tehsil Balakot District
		Toolers Franks		Mansehra
190	Syed Muneeb Haider	Trainee Engineer	32303-2262755-1	Kiwai Tehsil Balakot District Mansehra
191 192	Ishfaq Gul Niaz	Supervisor Mason	32303-2262755-1 32303-2262755-1	Sangar Sangar
193	Salahudin	MAson	32303-2262755-1	Sangar
194	Muhammad Niaz	Plumber	32303-2262755-1	Sangar
195	Dilnawaz	Steel Fixer	32303-2262755-1	Sangar
196	Abdul Aziz	Mason	32303-2262755-1	Sangar
197	Ageel Ahmad Khan	Supervisor	32303-2262755-1	Sangar
198	Abdurasheed	MAson	32303-2262755-1	Sangar
199	Azhar Mehmood	Mason	32303-2262755-1	Sangar
200	Nisar Ahmad	Plumber	32303-2262755-1	Sangar
201	Abdul Qadeer	Plumber	13501-4402320-7	Noori Bonjha Tehsil Balakot District Mansehra
202	Muhammad Azam	Cook helper	13501-3316834-7	Shawal Tehsil Balakoat Distric Mansehra
203	Adil Riaz Khan	Cleaner	13501-9783535-5	Shawal Tehsil Balakoat Distric Mansehra
204	Jaffar	Fuel man	13501-8686231-1	Paris tehsil Balakoat Distrcic Mansehra
205	Noman Shakeel	Cleaner	13501-9755391-7	Shawal Tehsil Balakoat Distric Mansehra
206	Sayed Mahr Ali	Survey Helper Watchman	13501-7957265-1	Paris tehsil Balakoat Distrcic Mansehra
207	M Hasan Ab Razaq	Mechanic Helper	13501-1301861-1 13501-6636269-7	Kholian Thesil Balakot Dristric Mansehra Balakot tehsil balakot Distric Mansehra
209	M Zaman	Labour	13501-0030209-7	Kholian Thesil Balakot Distric Mansehra
210	M Arshid	Labour	13501-7256734-9	Kholian Thesil Balakot Dristric Mansehra
211	M Sabir	Labour	13501-2311446-9	Kholian Thesil Balakot Dristric Mansehra
212	M Liaqat	Labour	13501-4059102-3	Kholian Thesil Balakot Dristric Mansehra
213	Rashid Hussain	Labour	13501-4068283-7	Kholian Thesil Balakot Dristric Mansehra
214	Noor Zaman	Labour	13501-1312120-1	Kholian Thesil Balakot Dristric Mansehra
215	Siraj Muhammad	Labour	13501-9292702-7	Kholian Thesil Balakot Dristric Mansehra
216	Atah Ur Rahman	Labour	13501-0354936-7	Kholian Thesil Balakot Dristric Mansehra
217 218	M Shabir Asad Hussain	Watchman Labour	13501-5093292-7 13501-0371651-9	kholian tehsil balakot Distric Mansehra kholian tehsil balakot Distric Mansehra
219	M Shabir	Labour	13501-9045080-7	kholian tehsil balakot Distric Mansehra
220	M Shakeel	Labour	13501-9021746-5	kholian tehsil balakot Distric Mansehra
221	Maqbool Ur Rahman	Labour	13501-5261458-3	kholian tehsil balakot Distric Mansehra
222	M Saleem	Labour	13501-9188313-1	kholian tehsil balakot Distric Mansehra
223	M Naveed	Labour	13501-2690108-5	kholian tehsil balakot Distric Mansehra
224	Ghulam Rabani	Labour	13501-1311256-7	kholian tehsil balakot Distric Mansehra
225 226	Liaqat Hussain Zia Ur Rahman	Labour Watchman	13501-4218307-5	kholian tehsil balakot Distric Mansehra
227	M Atif	Labour	13501-8377306-9 13501-1736173-5	kholian tehsil balakot Distric Mansehra Phagal Balakot tehsil balakot Mansehra
228	M Asif	Labour	13503-0636920-1	Balakot Distric Mansehra
229	Naveed	Labour	13501-8491317-1	Ghanool tehsil Balakot Distric Mansehra
230	Ab Nasir	labour	13501-1054401-3	Ghanool tehsil Balakot Distric Mansehra
231	M Saleem	Labour	13501-6637989-5	Ghanool tehsil balakoat Distric Mansehra
232	Ishtiaq Ahmed	Labour	13501-1328813-3	Ghanool tehsil balakoat Distric Mansehra
233	M Hanif	Labour	13501-6405385-5	Ghanool tehsil balakoat Distric Mansehra
234	Sajad Ahmed	Labour	13501-0968242-1	Ghanool tehsil balakoat Distric Mansehra
235 236	M Azhar M Shafique	Labour Labour	13501-1543079-3 13501-7322339-7	Ghanool tehsil balakoat Distric Mansehra Ghanool tehsil balakoat Distric Mansehra
236	Naheem Ullah	Labour	13501-7322339-7	Ghanool tehsil balakoat Distric Mansehra
238	Nazakat	Labour	13501-7202434-1	Ghanool tehsil Balakot Distric Mansehra
239	M Wasiq	Labour	13501-7545757-9	Ghanool tehsil Balakot &Distric Mansehra
240	M Sheraz	Labour	13501-6273332-9	Ghanool tehsil Balakot &Distric Mansehra
241	Atique Ur Rahman	Labor	13501-9215048-9	Ghanool tehsil Balakoat Distric Mansehra
242	M Juniad	Labor	13501-7638656-7	Ghanool tehsil Balakoat Distric Mansehra
243	Ab Safeer	Labor	13501-1350544-9	Ghanool tehsil Balakoat Distric Mansehra
244 245	M Tofeeq M Asif	Labour	13501-3469947-1 13501-4784657-3	kholian tehsil balakot Distric Mansehra
245	Mahui Din	Labour Labour	13501-4784657-3	kholian tehsil balakot Distric Mansehra kholian tehsil balakot Distric Mansehra
247	M Umair	Labour	13501-0309343-3	kholian tehsil balakot Distric Mansehra
248	Umar Sharif	Labour	13501-2296136-5	kholian tehsil balakot Distric Mansehra
249	M Naheem	Labour	13501-9376829-5	kholian tehsil balakot Distric Mansehra
250	Ab Majid	Labour	13501-6277694-3	kholian tehsil balakot Distric Mansehra
251	Iftakhar Ahmed	Labour	13501-6684632-1	kholian tehsil balakot Distric Mansehra
252	M Asim	Labour	13501-8191097-5	kholian tehsil balakot Distric Mansehra
253	Amir Nazir	Labour	13501-5300011-7	kholian tehsil balakot Distric Mansehra

0 N=	N	D M	ONIIO Normali a re	Address
S. No	Name Chamas Ur Dahman	Position	CNIC Number	Address
254	Shamas Ur Rahman	Labour Labour	13501-0392579-1	kholian tehsil balakot Distric Mansehra
255	Ab Shakoor	Labour	13501-5447168-9	kholian tehsil balakot Distric Mansehra
256 257	Rafaqat Hussine Murtaza	Labour	13501-9196705-5 13503-0729689-7	kholian tehsil balakot Distric Mansehra kholian tehsil balakot Distric Mansehra
258	Ab Basit	Labour	13503-0729009-7	kholian tehsil balakot Distric Mansehra
259	Ab Manan	Labour	13501-7837626-1	kholian tehsil balakot Distric Mansehra
260	Muhammad Ashraf	Stor keeper	13501-5009610-7	Kiloliali terisli balakot Distric ivialiserila
261	Muhammad Jahangir	Labour	13501-0760356-7	Ghanool tehsil Balakot district Mansehra
262	Muhammad Sadheer	Watchman	13501-0700330-7	Sangar Tehsil Balakot District Mansehra
263	Shams ul Hag	Watchman	13501-0580107-9	Kholian tehsil Balakot District Mansehra
264	Muahammad Arshad	Labour	13501-6345073-3	Ghanool tehsil Balakot district Mansehra
265	Attig Ur Rehman	Labour	13501-6678130-1	Khola Dabrian Balakot
266	Abdur Rab	Labour	13501-8485440-7	Garlat Balakot tehsil Balakot District Mansehra
267	Rafagat Qayyum	Labour	13501-1284233-5	Ghanool tehsil Balakot district Mansehra
268	Adil Maroof	Labour	13501-9607706-9	Kholian Ghanool tehsil Balakot
269	Muhammad Fayyaz	cook helper	13501-3026082-1	Kewai tehsil balakot district mansehra
270	Muhammad Umir	Labour	13501-7174769-5	Kholian Dari Zaman tehsil Balakot District Mansehra
271	Zahoor Hussain	Labour	13501-2630326-5	Ghanool tehsil Balakot district Mansehra
272	Abrar Sher Zaman	Labour	13501-2653634-7	Ghanool tehsil Balakot district Mansehra
273	Muhammad Siraj	Labour	13501-1833401-9	Ghanool tehsil Balakot district Mansehra
274	Muhammad Tufail	Labour	13501-0654337-9	Hasamabd tehsil Balakot District Mansehra
275	MUHAMMAD SHRARIF	Labour	13501-8983509-5	Balakot tehsil Distric Mansehra
276	MUHAMMAD SALEEM	labour	13501-9188113-1	Balakot tehsil Distric Mansehra
277	NAZEER HUSSAIN	labour	13501-7268603-1	Balakot tehsil Distric Mansehra
278	Rafaqat Hussain	Labour	13501-4078639-3	Mahandri Manoor Tehsil Balakot District Mansehra
279	MUHAMMAD KHURSHID	Labour	13501-7152634-9	Ghanool tehsil Balakot district Mansehra
280	Muhammad Tofeeq	Labour	13501-8397788-7	Ghanool tehsil Balakot district Mansehra
281	Muhammad Shafique	Labour	13501-6501425-7	Kholian tehsil Balakot District Mansehra
282	Muhammad Sajjad	Labour	13501-9141869-3	Ghanool tehsil Balakot district Mansehra
283	Zahid Qamar	Labour	13501-6886681-1	Ghanool tehsil Balakot district Mansehra
284	Shazad Ahmed	Signal Man Labour	13501-2458501-1	Sangar Tehsil Balakot District Mansehra
285	Sultan Mehmood	cook Helper	13501-0377561-3	Ghanool tehsil Balakot district Mansehra
286	Muhammmad Rafique	cook Helper	13501-3431284-9	Kholian Ghanool tehsil Balakot district Mansehra
287	MAQBOOL UR RAHMAN	Labour	13501-5888782-5	Sangar Tehsil Balakot District Mansehra
288	Muhammad Nadeem	Labour	13501-0236803-3	Sangar Tehsil Balakot District Mansehra
289	Attique ur Rehman	Labour	135018-451928-3	Sangar Tehsil Balakot District Mansehra
290	Gul Faraz	Labour	13501-1351145-7	Sangar Tehsil Balakot District Mansehra
291	Muhammad AZEEM	Labour	13501-1290913-3	Ghanool tehsil Balakot district Mansehra
292	Noor Muhammad	labour	13501-6297367-7	Sangar Tehsil Balakot District Mansehra
293	Sadam Muhammad	labour	13501-2412010-7	Sangar Tehsil Balakot District Mansehra
294	Muhammad Adil	labour	13501-3348184-1	Sangar Tehsil Balakot District Mansehra
295	Shabbir Hussain	labour	13501-1293419-1	Sangar Tehsil Balakot District Mansehra
296	Muhammad SHARAZ)	labour	13501-2772524-5	Sangar Tehsil Balakot District Mansehra
297	Muhammmad Shahid	labour	13501-5088967-9	Narah Balakot Garlat disytict Mansehra
298	Bilal Idrees	labour	13501-7084145-9	Narah Balakot Garlat disytict Mansehra
299	USMAN AIMSH	labour	13501-5773447-7	Sangar Tehsil Balakot District Mansehra
300	Jameel SajidHussain	Cleaner	13501-5566263-7 13501-1333916-1	Kewai tehsil balakot district mansehra Shoal medan tehsil balakot district
302	MuhammadNazakat	Cookhelper	13501-8932862-7	mansehra Jaraid tehsil balakot district mansehra
303	IrshadHussain	officeboy	13501-1932130-1	Jamu Nka Ghanool Tehsil Balakot
304	MUHAMMADBANARAS	labour	13501-6645273-7	Ghanool tehsil Balakot district Mansehra
305	MHasan	watchman	13501-1301866-1	Kholian Ghanool Tehsil Balakot District Mansehra
306	Raja Shafaqat	labour	13501-1349059-1	Paras tehsil balakot district mansehra
307	ABLATIF	labour	13501-1340629-7	Paras tehsil balakot district mansehra
308	ABDULRAZZAQ	labour	13503-3810057-1	Paras tehsil balakot district mansehra
309	ABBANARAS	Labour	13501-1307932-9	Paras tehsil balakot district mansehra
310	MAHIUEDIN	labour	13503-0509345-5	Paras tehsil balakot district mansehra
311	ZIARAHMAN	labour	13501-7533727-3	Paras tehsil balakot district mansehra
312	FaroorAbdul	支护Labour	13501-3651004-7	Kewai tehsil balakot district mansehra
313	MShaid	labour	13501-508896-7	Kewai tehsil balakot district mansehra
314	Khurshid	Labour	13501-8623352-1	Paras tehsil balakot district mansehra
315	Mehtab Ahmed	Labour	13501-3159683-1	Paras tehsil balakot district mansehra
316	Muhammad Tariq	Labour	13501-4461078-9	Paras tehsil balakot district mansehra
317	Imtiaz Shah	Labour	13503-9599828-7	Paras tehsil balakot district mansehra

0.11-	Na	D M	ONIO Normali a re	Address
S. No	Name Namet I IIIah	Position	CNIC Number	Address Deres to be il belaket district managhra
318 319	Namat Ullah Ahmed Khan	Labour Labour	13501-1328664-5 13501-1295745-1	Paras tehsil balakot district mansehra Paras tehsil balakot district mansehra
320	Muhammad Fayyaz	Labour	13501-1293743-1	Paras tehsil balakot district mansehra
321	Tayyab	Labour	13501-8070335-1	Paras tehsil balakot district mansehra
322	M Arshad	Labour	13503-9097405-9	Kewai tehsil balakot district mansehra
323	Abid Hussain Shah	Labour	13501-2710887-3	Kewai tehsil balakot district mansehra
324	Muhammad Sadique	Labour	13501-9804861-1	Kewai tehsil balakot district mansehra
325	Amir Sohail	Labour	13501-1143038-9	Kewai tehsil balakot district mansehra
326	Muhammad Sadiq	Labour	13501-8934928-9	Kewai tehsil balakot district mansehra
327	Sabir sultan	Labour	13501-1341726-1	Paras tehsil balakot district mansehra
328	Ejaz Hussain	Labour	13501-4069967-5	Paras tehsil balakot district mansehra
329	Zaheer Ahmed	Labour	13501-6897087-5	Paras tehsil balakot district mansehra
330	Moheed	Labour	13501-6827277-7	Paras tehsil balakot district mansehra
331	Muhammmd Murad	Labour	13501-9470292-7	Kewai tehsil balakot district mansehra
332 333	Waseem Taj Nazeer Hussain	Labour Labour	13501-1674335-3 13501-3563425-7	Kewai tehsil balakot district mansehra Kewai tehsil balakot district mansehra
334	Rashid Hussain	Labour	13501-3363423-7	Narah Balakot Garlat disytict Mansehra
335	Muhammad Atif	Labour	13501-7248291-5	Sangar Tehsil Balakot District Mansehra
336	Muhammad Nawaz	Labour	13501-7760303-3	Balakot Tehsil Balakot District Mansehra
337	Muhammad Sajjad	Labour	13503-9923491-3	Balakot Tehsil Balakot District Mansehra
338	Muhammad Zaheer	Labour	13501-0723187-7	Kiwai Tehsil Balakot District Mansehra
339	Muhammad Pervaiz	Labour		
	Khan	Laboui	13501-5601916-5	Narah Balakot Garlat disytict Mansehra
340	Muhammmd Shafique	Labour	13501-9890915-7	Sangar Tehsil Balakot District Mansehra
341	Sameer Mukhtiar	Labour	13501-9447341-5	Balakot Tehsil Balakot District Mansehra
342	Toqeer	Labour	13503-5344935-3	Balakot Tehsil Balakot District Mansehra
343	Togeer Ahmed	Labour	13501-8270962-1	Kiwai Tehsil Balakot District Mansehra
344	Amir Bilal	Labour	13503-0517330-5	Balakot Tehsil Balakot District Mansehra
345 346	Nagash Ahmed	Grouting Labour	13501-4892440-9	Kiwai Tehsil Balakot District Mansehra Kiwai Tehsil Balakot District Mansehra
347	Noor Hussain Shah Hafeez Ur Rehman	Labour Grouting Labour	13501-8379851-9 13501-6971060-1	Kiwai Tensii Balakot District Mansehra
348	Muhammad Haroon	Labour	13501-0971000-1	Kiwai Tehsil Balakot District Mansehra
349	Anayat Hussain	Grouting Labour	13501-1349448-1	Kiwai Tehsil Balakot District Mansehra
350	Nadeem	Labour	13501-6091091-1	Narah Balakot Garlat disytict Mansehra
351	Bilal Hussain	Labour	13501-4290494-7	Sangar Tehsil Balakot District Mansehra
352	Muhammad Fayaz	Grouting Labour	13501-4605202-9	Sangar Tehsil Balakot District Mansehra
353	Abdul Saboor	Grouting Labour	13501-3116201-3	Sanghar tehsil Balakot Mansehra
354	Syed Khursheed Shah	Grouting Labour	13501-9390405-1	Paris tehsil Balakoat Mahnsara
355	Asif Ahmed	Labour	13501-1829718-1	Sangar Tehsil Balakot District Mansehra
356	Riasat Khan	Labour	13501-9978909-3	Sangar Tehsil Balakot District Mansehra
357	Muhammad Tufail	Labour	13501-5213945-5	Sanghar tehsil Balakot Mansehra
358	Ahmed Ali	Grouting Labour	13501-5259431-3	Paris tehsil Balakoat Mahnsara
359 360	Sadam Hussain Mazhar	Labour Labour	13501-9928030-5 13501-3532143-7	Narah Balakot Garlat disytict Mansehra Sangar Tehsil Balakot District Mansehra
361	Issue Mumtaz	Labour	13501-3532143-7	Narah Balakot Garlat disytict Mansehra
362	Syed Naheem Shah	Labour	13501-2108488-9	Sangar Tehsil Balakot District Mansehra
363	Munir Ahmed	Labour	13503-9129210-5	Sehri Sanghar Post Office Dabriyan
364	Fiaz Ahmed	Labour	13501-2311760-1	Sanghar Tehsil Balakot District Mansehra
365	Muhammad Rashid	Labour	13101-8555296-5	Sanghar Tehsil Balakot District Mansehra
366	Masood Ahmed	Labour	13501-4223832-9	Sehri Sanghar Post Office Dabriyan
367	Muhammad Sadaqat	Labour	13501-1224976-3	Sanghar Tehsil Balakot District Mansehra
368	Ikhlaq Hussain Shah	Labour	13501-4133065-3	Sanghar Tehsil Balakot District Mansehra
369	Khurshid	Labour	13501-1555615-1	Sehri Post Office Khas Dabryian Sanghar
370	Muhammad Toqeer	Labour	13503-6993941-7	Sangar Tehsil Balakot District Mansehra
371	Gulzar Hussain	Labour	13501-5192882-5	Sanghar tehsil Balakot Mansehra
372 373	Nawaz Abdul Haq Imtiaz Hussain	Labour Labour	13501-8423741-5 13501-7006375-9	Paris tehsil Balakoat Mahnsara Paris tehsil Balakoat Mahnsara
373	Sohail Sabir	Labour	13501-7006375-9	Paris tehsil Balakoat Mahnsara Paris tehsil Balakoat Mahnsara
375	Zakir Hussain	Labour	13501-3646341-5	Paris tehsil Balakoat Mahnsara
376	Sher Aefal	labour	13501-6861513-1	Kiwai Tehsil Balakot District Mansehra
377	M Asad Jamtl	labour	13501-0867521-9	Sangar Tehsil Balakot District Mansehra
378	Noor Hussain	labour	13501-8338851-5	Sangar Tehsil Balakot District Mansehra
379	M Safeer	labour	13501-2929729-9	Paris tehsil Balakoat Mahnsara
380	Basharat Shah	Labour	13501-2105047-1	Paris tehsil Balakoat Mahnsara
381	Akhtar Shah	Labour	13501-4061271-7	Paris tehsil Balakoat Mahnsara
382	Shabir Shah	Labour	13501-6572534-9	Paris tehsil Balakoat Mahnsara
383	Syed Ishfaq Shah	Labour	13501-4627030-7	Paris tehsil Balakoat Mahnsara
384	Faisal Shah	Labour	13501-6645134-9	Paris tehsil Balakoat Mahnsara
385	Rashid Shah Adeel Shah	Labour	13501-2693830-7	Paris tehsil Balakoat Mahnsara
386 387	Ghulam qasim shah	Labour Labour	13501-6497948-1 13501-1296248-7	Paris tehsil Balakoat Mahnsara Sehri Post Office Khas Dabryian Sanghar
388	Amjid Hussain	Labour	13501-1296246-7	Sangar Tehsil Balakot District Mansehra
500	, anjia i idodalii	Laboai	10001-1000000-0	Sangar Tonon Balanot Bistrict Manschild

S. No	Name	Position	CNIC Number	Address
389	Syed Asif Hussain Shah	Labour	13501-4896753-1	Sanghar tehsil Balakot Mansehra
390	Ahmed Nawaz Shah	Labour	13501-6056664-3	Kiwai Tehsil Balakot District Mansehra
391	Basheer hussain Shah	Labour	13501-9646086-3	Kiwai Tehsil Balakot District Mansehra
392	Fazal Ur Rehman	Labour	13501-7010132-3	Kiwai Tehsil Balakot District Mansehra
393	Abdul Rasheed	Labour	13501-6425490-1	Narah Balakot Garlat disytict Mansehra
394	Nisar Ahmed	Labour	13501-6333021-5	Sangar Tehsil Balakot District Mansehra
395	Manzoor Hussain	Labour	13501-8285843-7	Sangar Tehsil Balakot District Mansehra
396	Manzoor Ahmed Ghulam Jelani	Labour	13501-2164469-3	Sanghar tehsil Balakot Mansehra
397 398	Ghulam Jelani Ghulam Rabbani	Labour Labour	13501-6776358-5 13501-1315490-9	Sehri Post Office Khas Dabryian Sanghar Sangar Tehsil Balakot District Mansehra
399	Aamir Shah	Labour	13501-1313490-9	Sanghar tehsil Balakot Mansehra
400	Javed Irfan	Labour	13501-4885298-1	Kiwai Tehsil Balakot District Mansehra
401	Muhammad Rafique	Labour	13501-1314939-7	Kiwai Tehsil Balakot District Mansehra
402	Muhammad Nazir	Labour	13501-1334257-1	Kiwai Tehsil Balakot District Mansehra
403	Shafique shah	Labour	13501-6952523-9	Narah Balakot Garlat disytict Mansehra
404	Muhammad Banaras	Labour	13501-2649597-3	Sangar Tehsil Balakot District Mansehra
405	Muhammad Saleem	Labour	13501-7510276-7	Sangar Tehsil Balakot District Mansehra
406	Razakat	Labour	13501-9602305-1	Sanghar tehsil Balakot Mansehra
407	Muneer Hussain	Labour	13501-9912146-1	Sehri Post Office Khas Dabryian Sanghar
408	Syed Amjad Ali Shah	Labour	13501-1314103-1	Sangar Tehsil Balakot District Mansehra
409 410	Zaheer Ahmed Zahid Hussain	Labour Labour	13501-6034547-9 13501-2413904-1	Sanghar tehsil Balakot Mansehra Kiwai Tehsil Balakot District Mansehra
411	Ihsan	Labour	13501-2413904-1	Kiwai Tensii Balakot District Mansehra
412	Ilyas ud din	Labour	13501-2316203-1	Kiwai Tehsil Balakot District Mansehra
413	Muhammad Ismael	Labour	13501-3645328-1	Narah Balakot Garlat disytict Mansehra
414	Noman Shakeel	Labour	13501-9555391-7	Sangar Tehsil Balakot District Mansehra
415	Muhammad Bilal Qureshi	Labour	13501-5068895-9	Sangar Tehsil Balakot District Mansehra
416	Muhammad Nadeem	Labour	13501-7450360-9	Sanghar tehsil Balakot Mansehra
417	Syed Husnain ali shah	Labour	13501-5403947-3	Paris tehsil Balakoat Mahnsara
418	Saqib Hussain	Labour	13501-5041044-5	Paris tehsil Balakoat Mahnsara
419	Muhammad Sadiq	Labour	13501-9110835-9	Paris tehsil Balakoat Mahnsara
420	Shafaqat Hussain	Labour	13501-8905293-1	Paris tehsil Balakoat Mahnsara
421	Muhammad Sheeraz	Labour	13501-0137653-7	Paris tehsil Balakoat Mahnsara
422 423	Muhammad Ali Jibran	Labour	13501-6132613-9	Paris tehsil Balakoat Mahnsara Paris tehsil Balakoat Mahnsara
424	Sudheer ahmed	Labour Labour	13501-6661379-9 13501-8902908-3	Sanghar tehsil Balakot Mansehra
425	Abid Hussain	Labour	13501-7808221-9	Sehri Post Office Khas Dabryian Sanghar
426	Sher Afzal	Labour	13501-3798092-1	Sangar Tehsil Balakot District Mansehra
427	Saeed Ahmed	Labour	13501-4438475-1	Sanghar tehsil Balakot Mansehra
428	Muhammad Shafique	Labour	13501-1308476-9	Kiwai Tehsil Balakot District Mansehra
429	Muhammad Shafique	Labour	13501-0889876-5	Kiwai Tehsil Balakot District Mansehra
430	Ajmal	Labour	13501-1160393-1	Kiwai Tehsil Balakot District Mansehra
431	Muhammad Tayyab	Labour	13501-9660476-9	Narah Balakot Garlat disytict Mansehra
432	Muhammad Javed	Labour	13501-9136858-5	Sangar Tehsil Balakot District Mansehra
433	Shafqat Hassan	Labour	13501-0151588-9	Sangar Tehsil Balakot District Mansehra
434 435	Raheel Anwar Syed Ikhtesham termazi	Labour Labour	13501-5039084-9 13501-3567424-7	Sanghar tehsil Balakot Mansehra Paris tehsil Balakoat Mahnsara
436	Hameed ur rehman	Labour	13501-5617473-9	Paris tehsil Balakoat Mahnsara
437	Muhammad Wajid	Labour	13501-6348689-3	Paris tehsil Balakoat Mahnsara
438	Abdul Qayyum	Labour	13501-1331910-5	Paris tehsil Balakoat Mahnsara
439	Muhammad Shafaqat	Labour	13501-7169838-5	Paris tehsil Balakoat Mahnsara
440	Umer zeb	Labour	13501-2250316-7	Paris tehsil Balakoat Mahnsara
441	Munir Ahmed	Labour	13501-7300037-5	Paris tehsil Balakoat Mahnsara
442	Mukhtar Ahmed	Labour	13501-4574639-5	Sanghar tehsil Balakot Mansehra
443	Khalid Mehmood	Labour	13501-1094660-3	Sehri Post Office Khas Dabryian Sanghar
444	Tasadaq Aziz	Labour	13501-2860056-9	Sangar Tehsil Balakot District Mansehra
445 446	Nazar Abbas Muhammad Shafique	Labour Labour	13501-3451925-7 13501-8315463-5	Sanghar tehsil Balakot Mansehra Kiwai Tehsil Balakot District Mansehra
446	Muhammad Safeer	Labour	13501-8315463-5	Kiwai Tensii Balakot District Mansenra Kiwai Tehsil Balakot District Mansehra
448	Riasat Ali	Labour	13501-7792964-3	Kiwai Tehsil Balakot District Mansehra
449	Muhammad Rizwan	Labour	13501-9071217-3	Narah Balakot Garlat disytict Mansehra
450	Muhammad Awais	Labour	13501-6342840-5	Sangar Tehsil Balakot District Mansehra
451	Naseer Ahmed	Labour	13501-2190652-9	Sangar Tehsil Balakot District Mansehra
452	Amir Aziz	Labour	13501-1456712-5	Sanghar tehsil Balakot Mansehra
453	Muzafar Hussain	Labour	13501-0564171-9	Paris tehsil Balakoat Mahnsara
454	Muhammad Aneed Idrees	Labour	13501-7074645-9	Paris tehsil Balakoat Mahnsara
455	Sijad Hussain	Labour	13501-1348127-7	Paris tehsil Balakoat Mahnsara
456	Rizwan Khan	Labour	13501-0847103-9	Paris tehsil Balakoat Mahnsara
457	Muhammad Sajid	Labour	13501-2973913-1	Sanghar tehsil Balakot Mansehra
458	Muhammad Sajjad	Labour	13501-0368632-9	Kiwai Tehsil Balakot District Mansehra

C Na	Nama	Danition	CNIIC Normalism	Address
S. No 459	Name Khizar hayat	Position Labour	CNIC Number 13501-1907721-9	Address Kiwai Tehsil Balakot District Mansehra
460	Abdul Ghafoor	Labour	13501-7518085-9	Kiwai Tehsil Balakot District Mansehra
461	Umair Anwar	Labour	13501-9729183-9	Narah Balakot Garlat disytict Mansehra
462	Shafagat shah	Labour	13501-7713597-3	Sangar Tehsil Balakot District Mansehra
463	Muhammad Arif	Labour	13501-0977072-1	Sangar Tehsil Balakot District Mansehra
464	Shafaqat Hussain	Labour	13501-8889486-3	Narah Balakot Garlat disytict Mansehra
465	Mufti Mehmood	Labour	13501-1326867-3	Sangar Tehsil Balakot District Mansehra
466	Zohaib ali shah	Labour	13501-5985232-9	Sangar Tehsil Balakot District Mansehra
467 468	Muhammad Ali Muhammad Sudheer	Labour Labour	13501-0514849-3	Paris tehsil Balakoat Mahnsara Paris tehsil Balakoat Mahnsara
469	Muhammad Maroof	Labour	13501-5242035-7 13501-8483950-5	Paris tensii Balakoat Mahnsara
470	Muhammad Idrees	Labour	13501-6239558-7	Paris tehsil Balakoat Mahnsara
471	M Liaqut	Labour	13501-2140727-7	Paris tehsil Balakoat Mahnsara
472	Syed Reasat	Labour	13501-1298540-1	Paris tehsil Balakoat Mahnsara
473	Syed Sajjad	Labour	13501-7412497-5	Paris tehsil Balakoat Mahnsara
474	Syed Tahir	Labour	13501-1256211-1	Paris tehsil Balakoat Mahnsara
475	Sadiq Shah	Labour	13501-1574906-1	Paris tehsil Balakoat Mahnsara
476	Asad Shah	Labour	13501-2132018-9 13503-5269075-3	Paris tehsil Balakoat Mahnsara
477 478	Hussain Liqat Saeed	tea boy Store Helper	13501-4977667-1	Paris tehsil Balakoat Mahnsara Paris tehsil Balakoat Mahnsara
479	M Farooq	Store Helper	13501-6852729-3	Paris tehsil Balakoat Mahnsara
480	M Faisal	Labour	13501-7384156-7	Narah Balakot Garlat disytict Mansehra
481	Ali Raza	Labour	13501-1938041-9	Sangar Tehsil Balakot District Mansehra
482	Yasim H	Labour	13501-1391480-7	Sanghar tehsil Balakot Mansehra
483	M Sadiq	Labour	13501-7284882-7	Paris tehsil Balakoat Mahnsara
484	Shakeel A	Labour	13501-5742946-7	Paris tehsil Balakoat Mahnsara
485 486	Ashfaq Ahmad Abdul Razzaq	Labour Labour	13501-0384865-5 13501-1318784-9	Paris tehsil Balakoat Mahnsara
486	Abid Hussain	Labour	13501-1318784-9	Paris tehsil Balakoat Mahnsara Sanghar tehsil Balakot Mansehra
488	M Haneef	Labour	13501-1771887-3	Kiwai Tehsil Balakot District Mansehra
489	M Shakeel	Labour	13501-6750207-3	Kiwai Tehsil Balakot District Mansehra
490	M Abbas	Labour	13501-9546492-1	Kiwai Tehsil Balakot District Mansehra
491	Shoaib M	Labour	13501-0335564-3	Narah Balakot Garlat disytict Mansehra
492	Wali UR	Labour	13501-3298278-3	Sangar Tehsil Balakot District Mansehra
493	Naseer Ahmmad	Labour	13501-8605539-9	Sangar Tehsil Balakot District Mansehra
494 495	Saeed H Usama M	Labour Labour	13501-3116204-7 13501-2113334-5	Narah Balakot Garlat disytict Mansehra Sangar Tehsil Balakot District Mansehra
495	Khakid Shah	Labour	13501-3969080-5	Sangar Tehsil Balakot District Mansehra
497	Akhtar Shah	Labour	13501-9936947-1	Paris tehsil Balakoat Mahnsara
498	Sheh zad Shah	Labour	13503-0734675-1	Paris tehsil Balakoat Mahnsara
499	Qaiser Shah	Labour	13501-4022993-1	Paris tehsil Balakoat Mahnsara
500	Nadeem Shah	Labour	13501-2857716-7	Paris tehsil Balakoat Mahnsara
501	Syed Ali Shah	Labour	13501-4671865-1	Sangar Tehsil Balakot District Mansehra
502	Mazhar Shah	Labour	13503-5844989-1	Narah Balakot Garlat disytict Mansehra
503 504	Arif Shah Ismail Shah	Labour Labour	13501-8306827-7 13501-5421300-5	Sangar Tehsil Balakot District Mansehra Sangar Tehsil Balakot District Mansehra
505	Miskeem Shah	Labour	13501-0428134-1	Paris tehsil Balakoat Mahnsara
506	Jaz Ali	Labour	13501-9169053-5	Paris tehsil Balakoat Mahnsara
507	Babir Ali	Labour	13501-3044682-3	Sangar Tehsil Balakot District Mansehra
508	Naib Shah	Labour	13501-1164667-1	Paris tehsil Balakoat Mahnsara
509	Umir Shah	Labour	13501-9581101-5	Paris tehsil Balakoat Mahnsara
510	M Sadik	Labour	13501-9242509-7	Paris tehsil Balakoat Mahnsara
511	Junaid shah	labour	13501-8880025-3	Paras tehsil balakot district mansehra
512 513	Abdul Majid Talab	Labor Labor	13501-9235977-1 13501-7626990-3	Sehri Sanghar Post Office Dabriyan Sanghar Tehsil Balakot District Mansehra
514	Shafaqat	Store	13501-7626990-3	Sanghar Tehsil Balakot District Mansehra
515	Hassan Awais	Survey Helper	13501-1636469-5	Sehri Post Office Khas Dabryian Sanghar
516	Muhammad Tanveer	Labor	13501-7644914-9	Sanghar Tehsil Balakot District Mansehra
517	Muneeb Ahmad	Labor	13501-2016212-9	Sanghar Post Office Dabriyan
518	Maskeen	Security Guard	13501-0169961-3	Kiwai Tehsil Balakot District Mansehra
519	Hamayun	Labor	13501-5143256-9	Kiwai Tehsil Balakot District Mansehra
520 521	Sadaqat Ali Muhammad Naeem	Excavator Helper Excavator Helper	13501-3169850-3 13501-7215541-3	Mohallah Jagdar Sanghar Kiwai Tehsil Balakot District Mansehra
521	Muhammad Hafeez	Labor	13501-7215541-3	Balakot Tehsil Balakot District Mansehra
523	Muhammad Haneef	Labor	13501-1160026-7	Balakot Tehsil Balakot District Mansehra
524	Zaheer	Labor	13501-7312427-7	Kiwai Tehsil Balakot District Mansehra
525	Mazhar	Labor	13501-8744921-1	Kiwai Tehsil Balakot District Mansehra
526	Shahzad	Labor	13501-0147755-7	Kiwai Tehsil Balakot District Mansehra
527	Noman	Labor	13501-0743321-7	Kiwai Tehsil Balakot District Mansehra
528	Khushdil Khan	Secuirty Guard	13501-1343375-1	Kiwai Tehsil Balakot District Mansehra
529	Muhammad Ijaz	Cook Helper	13501-4531068-7	Village Jabri Tehsil Balakot District
	<u>.</u>			Mansehra

S. No	Name	Position	CNIC Number	Address
530	Naeem Akhtar	Office Boy	13501-2840642-3	Kapi Galli Tehsil Balakot District Mansehra
531	Nazeer	Secuirty Guard Bore Mechine	13501-2729231-9	Kapi Galli Tehsil Balakot District Mansehra
532	Safi Ullah	Labor	13501-1342763-9	Sanghar Tehsil Balakot District Mansehra
533	Adil Khan	Labor	13501-3967894-9	Sanghar Tehsil Balakot District Mansehra
534	Bilal	Security Guard	13501-1245763-9	Sanghar Tehsil Balakot District Mansehra
535	Amir Asif	Labor	13501-6189685-7	Kapi Galli, Sanghar
536	Asad Shabeer	Survey Helper	13501-5845493-9	Kapi Galli, Sanghar
537	Hasnain Farooq	Survey Helper	13501-0792509-1	Baskati, Sanghar
538	Ghulam Qadir	Secuirty Guard	13501-1334361-1	Sandori, Sanghar
539 540	Muhammad Sajad Muhammed Nazeer	Secuirty Guard Secuirty Guard	13501-368632-9 13501-276308-9	Kapi Galli, Sanghar Kapi Galli, Sanghar
541	Muhammad Shahbaz	Survey Helper	42501-3869574-1	Mohallah Barri, Sanghar
542	Muhammad Ali Sarwar	Survey Helper	13501-2770372-9	Village Sanghar
543	Muhammad Ulfat	Hse helper	13503-1355040-9	Village Sanghar
544	Muhammad Shahzad	Desiel Helper	13501-8851663-7	Village Sanghar
545	Adeel Mehboob	Excavator Helper	42201-7303509-5	Baskaty Sanghar
546	Rafeeq Hussain	Cook Helper	135017386847-5	Paras
547	Syed Dilawar Shah	Labor	13501-2582882-9	Paras
548	M. Manzoor	LAbor	13501-3820160-5	Paras
549	Muhammad Nazeer	Labor	13501-9951477-3	Paras
550	Safi Ullah	Labor Cooviety Cyand	13501-1342763-9	Village Sanghar
551 552	Syed Zeeshan Ali shah Abdul Rehman	Secuirty Guard Labor	13501-6282342-3 13501-7626990-3	Paras Sanghar Tehsil Balakot
553	M Nazeer	Secuirty Guard	13501-7626990-3	Village Sanghar
554	Muhammad Afaq	Laboratory Helper	37405-7905426-7	Sangar
555	Umair Azeem	Laboratory Helper	13501-2276094-7	Sangar
556	Noor Rehman	Sweeper	13501-1336558-7	Sangar
557	Abdul Muneer	Tandori Helper	13501-1333442-9	Sangar
558	Atta Muhammad	Security Guard	13501-1317187-3	Sangar
559	Hamza Khan	Excavator Helper	13501-0285092-5	Sangar
560	Muhammad Ateeq	Excavator Helper	-	Sangar
561	Umair Ali	Excavator Helper	13501-1389786-5	Kappi Gali
562	Waqas Farooq Abid Hussain	Excavator Helper	13501-4566227-5	Ghanool
563 564	Muhammad Jameel	Cleaner Tandori	13501-5215536-3 13503-9941351-5	Derian College Doraha Mansehra
565	Muhammad shoukat	Safety Man	13503-9941351-5	Kappi Galli
566	Syed Fahad Hussain	Work Shop Helper	13501-079979-7	Kewai
567	Sadagat Hussain Shah	Labour	13501-1312851-7	Kewai
568	M- Ateeq	Excavator Helper		Sanghar
569	Saqlain ishtiyaq	Mess Helper	13501-0265027-1	Sangar
570	Khizer Hayat	Security Guard	13501-5014530-9	Kapi Gali
571	Hamad Gull	Excavator Helper	13501-7327200-1	Village Sangar
572	Muhammad Nazir	Labour	42201-9127090-5	Balakot
573	Muhammad Raza Minhas	Security Guard	82203-5745053-3	Kiwai
574	M. Shahid	Labour	13501-6557064-5	Sangar
575 576	M. Shakeel	Labour Labour	13501-3123074-1	Sangar
576 577	M. Fazal Afzal Ahmad	Labour	13501-6406757-9 13705-2790178-9	Sangar Sangar
578	Fazal Khan	Labour	13501-4844533-9	Sangar
579	Zohaib	Labour	13501-4974224-9	Sangar
580	Nasir Ali	Labour	13501-8273589-9	Balakot
581	Aqeel Ahmad	Labour	13501-1633023-3	Balakot
582	Abdul Saboor	Labour	13501-9316588-9	Balakot
583	Saqib Zaman	Labour	13501-6534554-1	Balakot
584	Rashid	Labour	13501-4876450-7	Balakot
585	Shamsurehman	Labour	13501-5584931-7	Balakot
586	Naqash U Rehman	Labour	13501-8679569-5	Balakot
587 588	M. Nazeer Aurangzaib	Labour Security Guard	13501-8212617-3 34201-8698433-3	Balakot P/O Garhi Habibullah Jageer Balola Tehsil
589	Meer Muhammad	Security Guard	37405-7283165-7	Balakot District Mansehra Por Garhi Habibullah Tehsil Balakot District Mansehra
590	Muhammad Tariq	Helper	32303-2262755-1	Mansehra Sangar
590	Abdul Wahab	Helper	32303-2262755-1	Sangar
592	Muhammad Arif	Helper	32303-2262755-1	Sangar
593	Muhabat Ameer	Helper	32303-2262755-1	Sangar

Annexure-13: Pictorial view of LARP Activities of BHPP during Reporting Period





Meeting with GRCs/ DPs/ community members of Mouza Paras regarding Missing/ Additional LARP's Allowances



Meeting with GRCs/ DPs/ community members of Mouza Bela Sacha regarding Missing/ Additional LARP's Allowances.



The DD S & R Meeting/ Discussion with Patwari/ Revenue Officials at Revenue Department



Meeting with GRC/ community members of Mouza Paras regarding IVS study findings by the PD-PIU.



ERM Field visit regarding Validation of vacant structure and compensation and allowances payment in Mouza Paras



ERM Field visit regarding Validation of vacant structure and compensation and allowances payment in Mouza Paras



ERM Field visit regarding Validation of vacant structures and compensation and allowances payment in Mouza Paras



The Complainants (OSPF), Mr. Aqeel Ahmad & Mr. Naeem Ashraf signed and handover statement of satisfaction to the Deputy Director Social & Resettlement of PIU.



Meeting with GRCs/ DPs/ community members of Mouza Sangar regarding Missing/ Additional LARP's Allowances.



The DD S & R Meeting/ Discussion with ADC of District Mansehra.



The PD and PIU Staff Meeting/ Discussion with DC Mansehra.
